

STATUS OF PROJECTS IN EXECUTION – FY06
SOPE
REGION: EAST ASIA AND PACIFIC
COUNTRY: CHINA

Operations Policy and Country Services
SEPTEMBER 19, 2006



Report on the Status of Projects in Execution - FY06
SOPE
Region: East Asia and Pacific
Country: China

Introduction

The Status of Projects in Execution (SOPE) Report for FY06 provides information on all IBRD/IDA projects that were active on June 30, 2006.

The World Bank has issued a SOPE Report every year as an internal communication to the Board of Executive Directors. In accordance with the Bank's revised disclosure policy, since FY02, the SOPE Report is available to the public.

The report is intended to bridge the gap in information available to the public between the Project Appraisal Document, disclosed after the Bank approves a project, and the Implementation Completion Report, disclosed after the project closes.

In addition to the project progress description, the FY06 SOPE report¹ contains project level comparisons of disbursement estimates and actual disbursements, and a table showing the loan/credit/grant amount and disbursements to date for all active projects.

¹ Notes:

- Amounts for Projects in currencies other than U.S. dollars may not match exactly due to exchange rate fluctuations over the life of the project.
- Disbursement graphs are not included for Development Policy Loans, which provide quick-disbursing external financing to support policy and institutional reforms. For these loans, funds are disbursed in one or more stages (tranches), released when the borrower complies with agreed conditions.
- Projects which are not yet effective may not have a planned disbursement schedule and thus may not include a graph.



Country: China

Project Name (ID): CN THIRD ODS PHASE OUT (P003409)

Country: China

Board Approval Date : 06/22/1995

Closing Date : 12/31/2010

Loan/Credit/Grant Number : WBTF-20738, WBTF-22002, WBTF-22452

Sector(s): Other industry (97%), Banking (2%), Central government administration (1%)

Theme(s): Pollution management and environmental health (P), Environmental policies and institutions (S)

Project Development Objectives:

The key development objective of this Montreal Protocol Project is the phase-out of Ozone Depleting Substances (ODS) in China.


Progress toward achieving development objective(s):

The project is nearly completed and will close by December 31, 2006 four years ahead of schedule. As of now out of a total of 87 subprojects, all except one have been completed. The last subproject is expected to be completed by September 2006, and no new subprojects are planned to be financed. The project resulted in the phaseout of 19,000 tons of ozone depleting substances (ODS), which constituted about 20% of China ODS consumption. The early closure of this project was possible due to a shift from individual subprojects under ODS III to a sector-wide performance-based approach in ODS IV.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
WBTF-20738	Closed	0.69	0.65	0.00	0.04
WBTF-22002	Effective	120.10	95.38	24.72	0.00
WBTF-22452	Closed	0.14	0.11	0.00	0.03



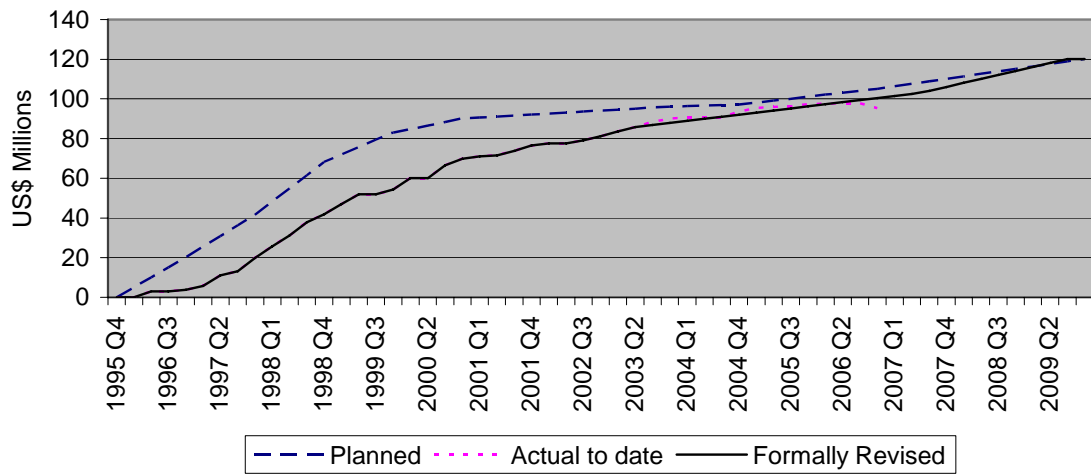

Project Name (ID): CN-Sustainable Coastal Resources Dev. (P003539)

Country: China

Board Approval Date : 05/19/1998

Midterm Review Date : 11/13/2001

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-43220, JPN-29734

Sector(s): Animal production (70%), Other domestic and international trade (20%), Central government administration (10%)

Theme(s): Water resources management (P), Export development and competitiveness (P), Biodiversity (S)

Project Development Objectives:

The objectives are to: (a) promote the sustainable development of the country's coastal resources; (b) reduce pressure on coastal fishery resources; and (c) improve aquatic product quality.

The Project was restructured during the 2006 Fiscal Year

The goals of the restructuring were to: (a) allocate savings to expansion of the Coastal Zone Management component to include investment in mangrove restoration under the Guangxi sub-project; and (b) demonstrate further best practice with regard to the introduction of international seafood processing quality standards under the Fujian sub-project.


Progress toward achieving development objective(s):

Project implementation continues to show progress in all project areas with the planned investments and related activities. As a result of coastal flooding from unusual recent typhoon activity and other factors during the past year, a request to extend the Loan for activities in four of seven project areas for an additional year is being processed by the borrower. Interest has increased further with a provisional list of potential components developed by all project areas currently under the project for a follow-on project that could support provincial and municipal coastal zone management programs, possibly through a combination of investment and grant financing with the latter for conservation activities.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-43220	Effective	100.00	67.38	30.56	2.06
JPN-29734	Closed	0.40	0.40	0.00	0.00



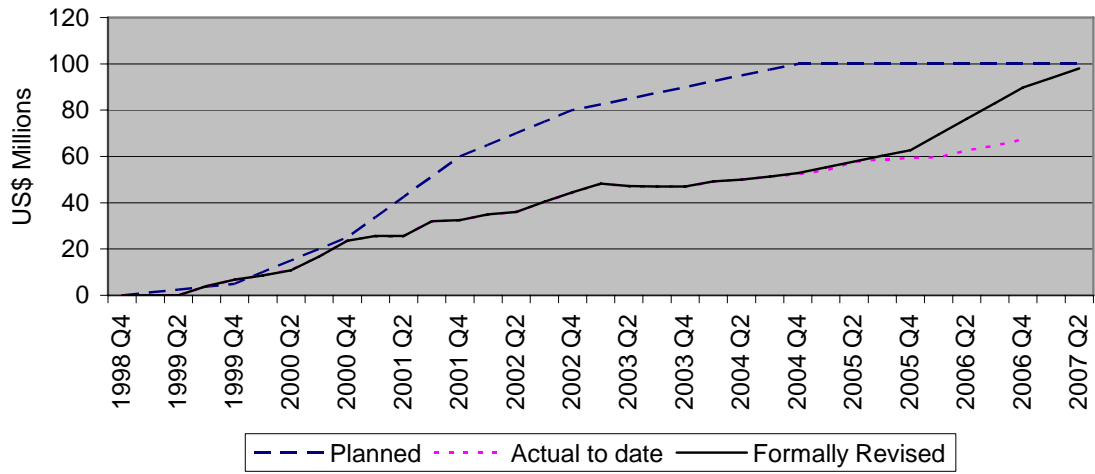

Project Name (ID): China Basic Health (P003566)

Country: China

Board Approval Date : 05/19/1998

Midterm Review Date : 08/15/2001

Closing Date : 06/30/2007

Loan/Credit/Grant Number : IDA-30750, JPN-26562, JPN-27029, JPN-29403, JPN-52892, MULT-52328, UK-04290

Sector(s): Health (77%), Non-compulsory health finance (10%), Compulsory health finance (5%), Sub-national government administration (4%), Central government administration (4%)

Theme(s): Health system performance (P), Rural services and infrastructure (P), Child Health (S)

Project Development Objectives:

The project aims to achieve sustainable health improvement for the populations of poor rural counties through: (a) improved allocation and management of health resources; (b) upgrading of health facilities at township level; (c) improved quality and effectiveness of health services and programs; and (d) increased risk sharing and affordability of essential health care for poor families.


Progress toward achieving development objective(s):

As the project matures, good progress is being made. Health improvements are occurring in poor counties and progress is also being achieved in experimenting with ways to finance the purchase of services by the poor and piloting innovative approaches to service delivery. The government's current rural health reforms programs are drawing heavily from the many important lessons generated by the project. Thus, the project continues to make a strong contribution to finding ways to improve the health of people in poor rural areas. The severe acute respiratory syndrome component continues to provide training and research findings to strengthen the government's capacity to address the challenges of newly emerging infectious diseases.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-30750	Effective	92.61	76.31	10.08	0.00
JPN-26562	Closed	0.40	0.40	0.00	0.00
JPN-27029	Closed	0.20	0.20	0.00	0.00
JPN-29403	Closed	0.21	0.22	0.00	0.00
JPN-52892	Closed	2.00	1.93	0.00	0.07
MULT-52328	Effective	9.01	7.18	2.07	0.00
UK-04290	Effective	27.35	22.37	3.45	0.00



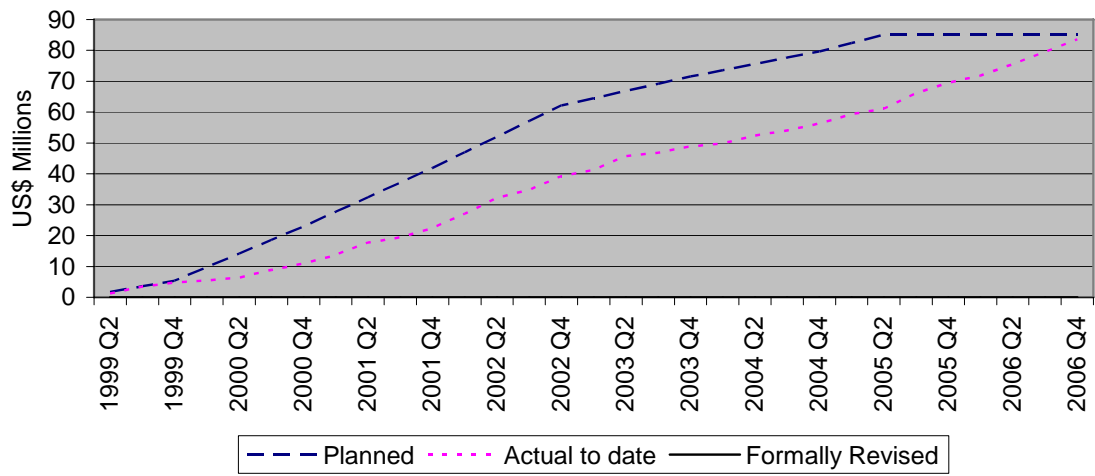

Project Name (ID): CN-Gansu Hexi Corridor (P003594)

Country: China

Board Approval Date : 05/30/1996

Midterm Review Date : 06/12/2000

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-40280, IDA-28700, JPN-29173

Sector(s): Irrigation and drainage (65%), General agriculture, fishing and forestry (15%), Central government administration (10%), General water, sanitation and flood protection (10%)

Theme(s): Rural services and infrastructure (P), Other rural development (P), Pollution management and environmental health (P), Other environment and natural resources management (S), Land administration and management (S)

Project Development Objectives:

The primary objectives are to: (a) raise incomes and standards of living for 75,000 persons now living in absolute poverty through voluntary emigration and settlement on newly-developed irrigated land; (b) reverse the degradation of Central and Southeast Gansu uplands where resources have been over-exploited, and to enhance and protect environments in the proposed settlement areas for sustainable use; and (c) increase food production to ease annual deficits.

Progress toward achieving development objective(s):


The likelihood of achieving the project's development objectives depends on an extension of the project implementation period by 18-24 months.

Project progress during the reporting period has been reasonable. Most of the irrigation construction works are completed. However, although progress has been made the last 12 months on the resettlement activities, resettlement is not yet finalized; out of the 75,000 planned resettlers, about 50,000 have been settled, leaving the project at least one full growing season behind schedule as the land first needs to be prepared before the resettlers can move. As a result, the agricultural development activities are significantly behind schedule. Attention needs to be paid to provide all required social services to the resettlers.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-40280	Effective	60.00	24.09	35.91	0.00
IDA-28700	Effective	90.84	79.49	6.18	0.00
JPN-29173	Closed	0.17	0.19	0.00	0.00



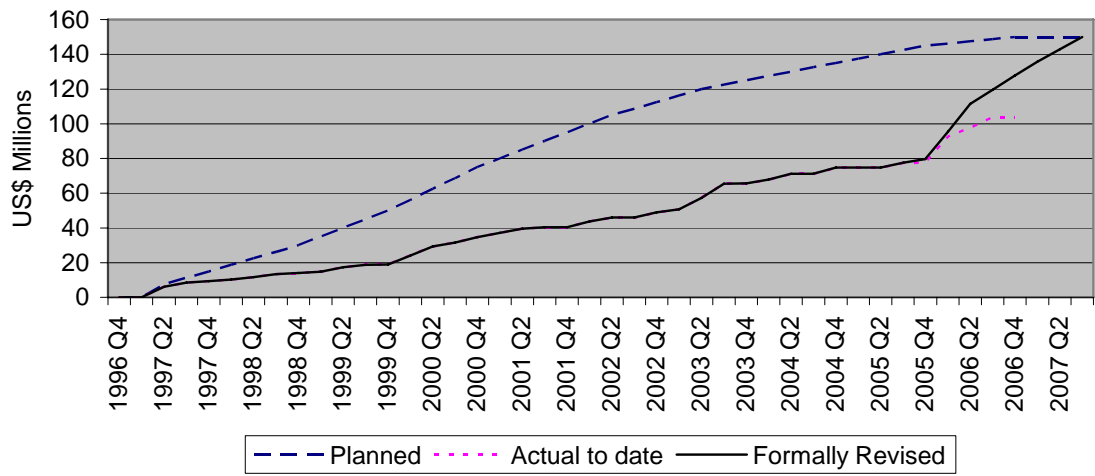

Project Name (ID): CN-Guangzhou City Transport (P003614)

Country: China

Board Approval Date : 05/29/1998

Midterm Review Date : 06/15/2001

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-43290, JPN-25202

Sector(s): Roads and highways (75%), General transportation (25%)

Theme(s): Access to urban services and housing (P), Municipal governance and institution building (P), Pollution management and environmental health (P), Other urban development (P)

Project Development Objectives:


To improve the accessibility of the city center of Guangzhou by promoting the efficient use of the urban transport system in an environmentally sustainable way.

Progress toward achieving development objective(s):

The project has made progress toward achieving its objectives, despite implementation delays earlier. The completed Inner Ring Road has reduced the traffic congestion in the city center continuously. The traffic management improvement program has been expanded, further reducing congestion; this may have assisted in reducing road accidents. Establishment of a road maintenance management system has been under implementation. The improvement of the motor vehicle emission control program has been ongoing. The technical assistant program has been implemented and it has strengthened the overall capacity of many government agencies.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-43290	Effective	200.00	100.20	79.80	20.00
JPN-25202	Closed	0.31	0.27	0.00	0.05

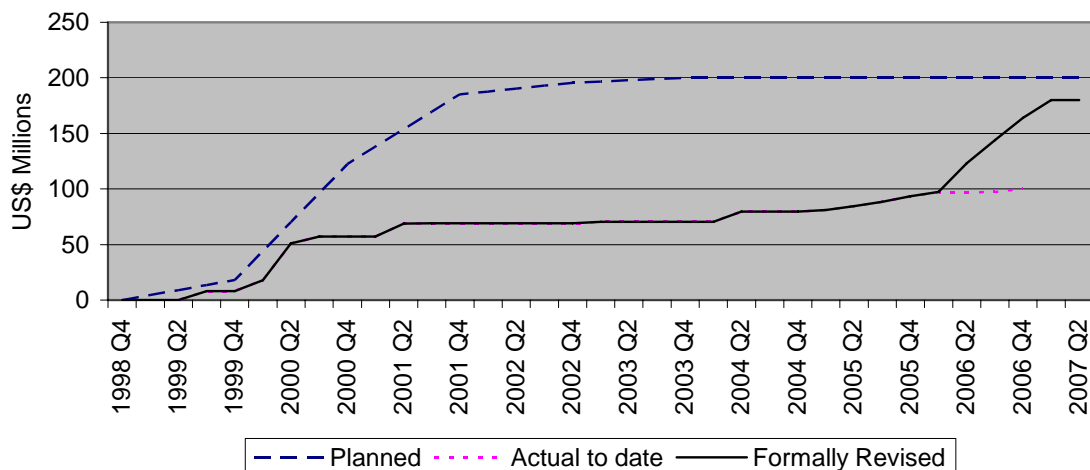

Project Name (ID): CN-2nd Inland Waterways (P003619)

Country: China

Board Approval Date : 05/29/1998

Midterm Review Date : 07/31/2002

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-43280, JPN-29446

Sector(s): Ports, waterways and shipping (100%)

Theme(s): Water resources management (P), Other financial and private sector development (S)

Project Development Objectives:

To provide more efficient and productive inland waterway transport services that are more competitive than current services


Progress toward achieving development objective(s):

Progress toward meeting the objectives is strong. In Jiangsu Province, five shiplocks were constructed and are now operating. Data are being collected to evaluate performance, but early indications are positive. For the Guangdong components, the renovations of two waterways and the dredging works are nearly complete and indicators suggest that this part of the project will also achieve the efficiency and productivity objectives. Guangdong has completed several technical assistance packages including the development of a management information system, design of navigational aids and training. The new database created as a result of the first study has led to a marked reduction in channel maintenance costs. Jiangsu's study on vessel size, now completed, has led to national adoption of standardized vessels size to increase the efficiency of lock operations and increased awareness of vessel noise and pollution. Project training has provided both provinces with the skills necessary to ensure sustainable operation of the channel and shiplock assets.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-43280	Effective	123.00	78.91	7.09	37.00
JPN-29446	Closed	0.39	0.39	0.00	0.00



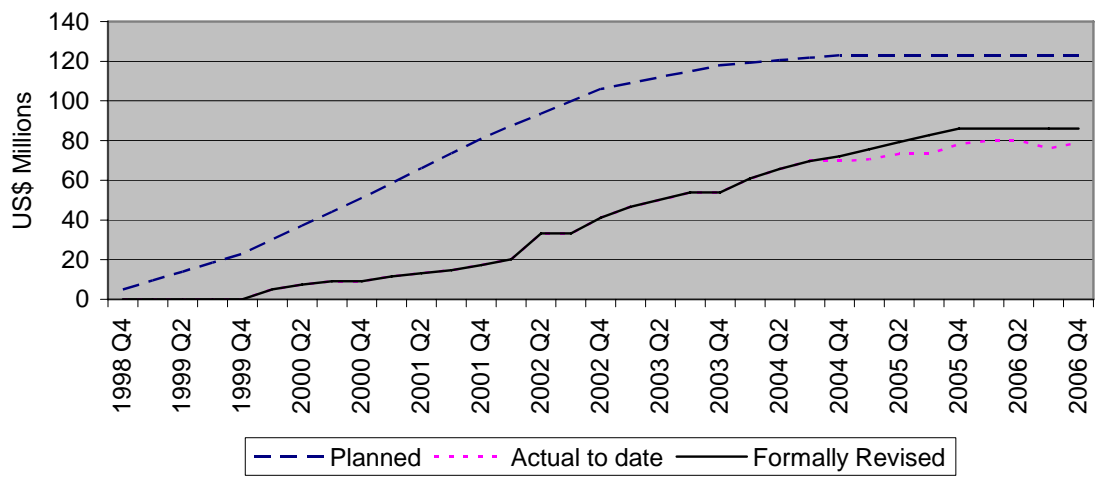

Project Name (ID): NATIONAL RURAL WATER SUPPLY PROJECT (P003637)

Country: China

Board Approval Date : 06/23/1997

Midterm Review Date : 03/15/2001

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IDA-N0270, JPN-29625

Sector(s): Water supply (91%), Sanitation (3%), Health (3%), Primary education (3%)

Theme(s): Rural services and infrastructure (P), Other human development (S)

Project Development Objectives:

Original project objectives: (a) Provide access to safe, conveniently located water to rural people in 40 counties and 5 provinces; (b) improve water-related health and sanitation practices; (c) provide water at the lowest possible cost; (d) ensure sustainability through good maintenance and accounting practices.


Additional objective: to assist the Borrower in carrying out a program to control and manage the incidence and spread of SARS and infectious diseases.

Progress toward achieving development objective(s):

The original rural water supply project was completed and the objectives achieved. The SARS component continues to provide training and research findings to strengthen the government's capacity to address the challenges of newly emerging infectious diseases.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-N0270	Effective	75.56	66.98	0.23	0.00
JPN-29625	Closed	0.58	0.29	0.00	0.28

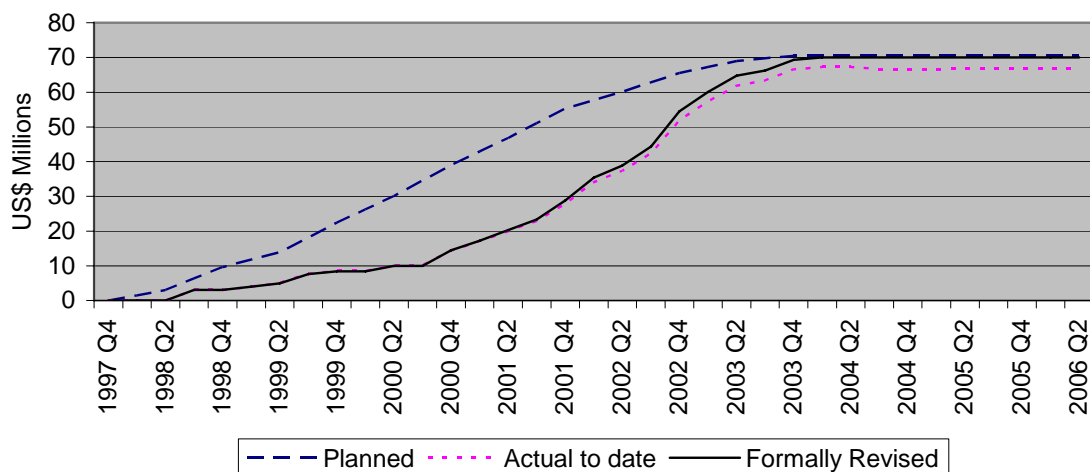

Project Name (ID): CN-Wanjiashai Water (P036405)

Country: China

Board Approval Date : 06/03/1997

Closing Date : 06/30/2007

Loan/Credit/Grant Number : IBRD-41790, JPN-29396

Sector(s): Water supply (60%), Sewerage (20%), Sanitation (14%), Central government administration (6%)

Theme(s): Water resources management (P), Pollution management and environmental health (P), Land administration and management (P), Rural services and infrastructure (S), Other urban development (S)

Project Development Objectives:

The objectives are to: (a) reduce the severe infrastructure bottlenecks in water supply to Taiyuan City that impede economic growth; (b) improve the environment by ending the over-extraction of groundwater and reducing water pollution downstream; and (c) promote integrated water management and financial independence for water institutions in order to create a system to rationalize water use, by sector, and reduce water shortages by managing demand.


Progress toward achieving development objective(s):

The construction of water transfer works has been completed to a good standard and water has been delivered to Taiyuan City. Excessive and unsustainable groundwater extraction in Taiyuan has been brought under control. Water pollution downstream has been reduced. However, the institutional reform for integrated water resources management and the achievement of financial independence for the institutions necessary to maximize the benefit of the project remain a problem. Substantial improvements and actions on this issue are expected before loan closing on June 30, 2007.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-41790	Effective	400.00	320.59	4.41	75.00
JPN-29396	Closed	0.36	0.38	0.00	0.00



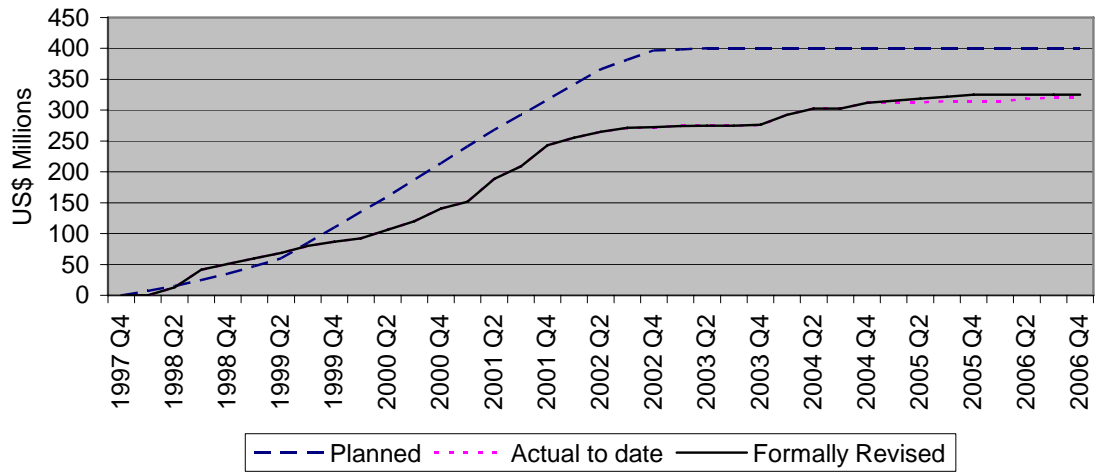

Project Name (ID): GUANGXI URBAN ENVIRONMENT PROJECT (P036414)

Country: China

Board Approval Date : 06/16/1998

Midterm Review Date : 11/02/2001

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-43480, IDA-30970, JPN-29733

Sector(s): Sewerage (76%), Water supply (13%), Solid waste management (5%), Agro-industry (4%), General transportation (2%)

Theme(s): Water resources management (P), Pollution management and environmental health (P), Environmental policies and institutions (P), Access to urban services and housing (P)

Project Development Objectives:

To (a) improve the quality of major water bodies, in particular Chaoyang stream and Yongjiang in Nanning and Lijiang and its tributaries in Guilin; (b) regulate the flow of the Lijiang; (c) improve institutional and financial capacity for environmental protection, environmental services and water resource management; (d) pilot a participatory approach to environmental improvement in poor neighborhoods; and (e) implement pilot schemes for control of sugar refinery pollution.


Progress toward achieving development objective(s):

Progress toward meeting the objectives remains on track. Completion of the new wastewater treatment plant is expected in late 2006. Once completed, the water quality of the Yongjiang River could improve to class III. Water quality in the Chaoyang stream has already improved with the completion of wastewater interception and collection. Completed project investments in Guilin in wastewater and solid waste management have already improved water quality. The remaining works to expand sewerage and construct a pumping station will further improve water quality upon completion. The sewerage companies in both project cities continue to make good progress in becoming commercially oriented autonomous utilities. Environmental improvements in poor neighborhoods have been made, benefiting over 100,000 residents. Pollution control facilities for two sugar refineries have been installed, reducing pollutant discharge significantly.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-43480	Effective	72.00	26.87	31.64	13.48
IDA-30970	Effective	21.90	18.74	1.83	0.00
JPN-29733	Closed	0.15	0.15	0.00	0.00



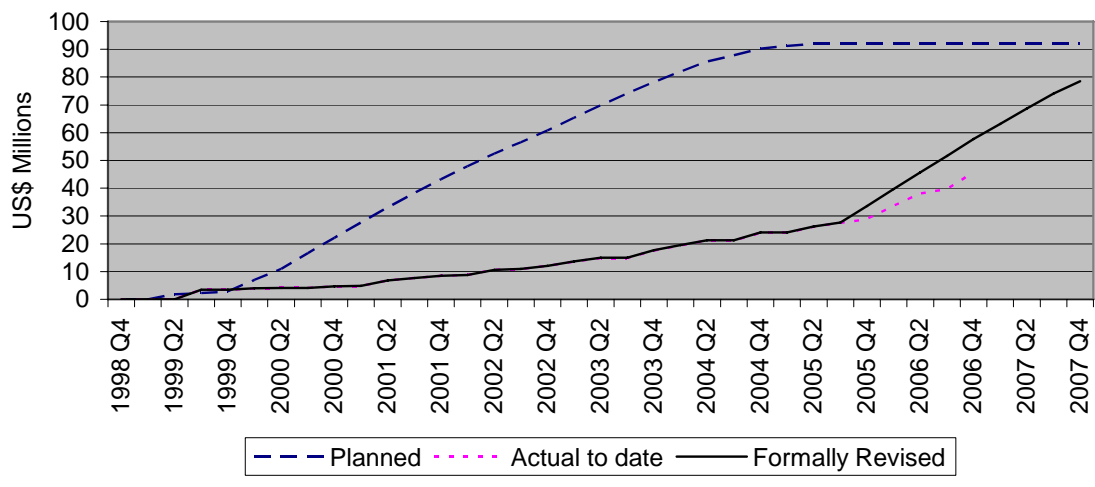

Project Name (ID): China Health Nine Project (P036953)

Country: China

Board Approval Date : 05/04/1999

Midterm Review Date : 04/09/2004

Closing Date : 06/30/2008

Loan/Credit/Grant Number : AUSL-23612, IBRD-44620, IDA-32010, JPN-25401, JPN-26233, JPN-53812

Sector(s): Health (94%), Sub-national government administration (6%)

Theme(s): Child Health (P), HIV/AIDS (P), Population and reproductive health (S), Health system performance (S), Participation and civic engagement (S)

Project Development Objectives:

The objectives are: (1) reducing maternal and child morbidity and mortality and improving child development; (2) preventing and controlling HIV/AIDS and sexually transmitted diseases; and (3) assuring the supply of safe blood for medical use and improving blood management.


Progress toward achieving development objective(s):

Both the Maternal and Child Health (MCH) and HIV/AIDS components of the project are introducing best-practice approaches learned from experience in China and other countries. Among these are: for MCH, use of maternal death audits to analyze preventable causes of death and to link training with the death audit analysis; and training innovations such as tailoring follow-up training to observed skills gaps, refresher courses, and certification of long-term training and training facilities; for HIV/AIDS, use of a multi-sectoral response involving a wide range of public and private institutions; and use of interventions such as methadone treatment, needle exchange, messages on reducing stigma and discrimination, 100% condom use, and standardization of STD management. The MCH component is also piloting a Medical Financial Assistance scheme aiming to cover costs of MCH services for the poorest 5% of the population. The HIV/AIDS component has advanced significantly thanks to an improved policy environment in the country and high-profile support for the program at the highest levels of government.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
AUSL-23612	Closed	1.46	1.16	0.00	0.00
IBRD-44620	Effective	10.00	2.71	6.89	0.40
IDA-32010	Effective	54.09	39.00	12.35	0.00
JPN-25401	Closed	0.10	0.10	0.00	0.00
JPN-26233	Closed	0.40	0.40	0.00	0.00
JPN-53812	Effective	0.66	0.10	0.56	0.00



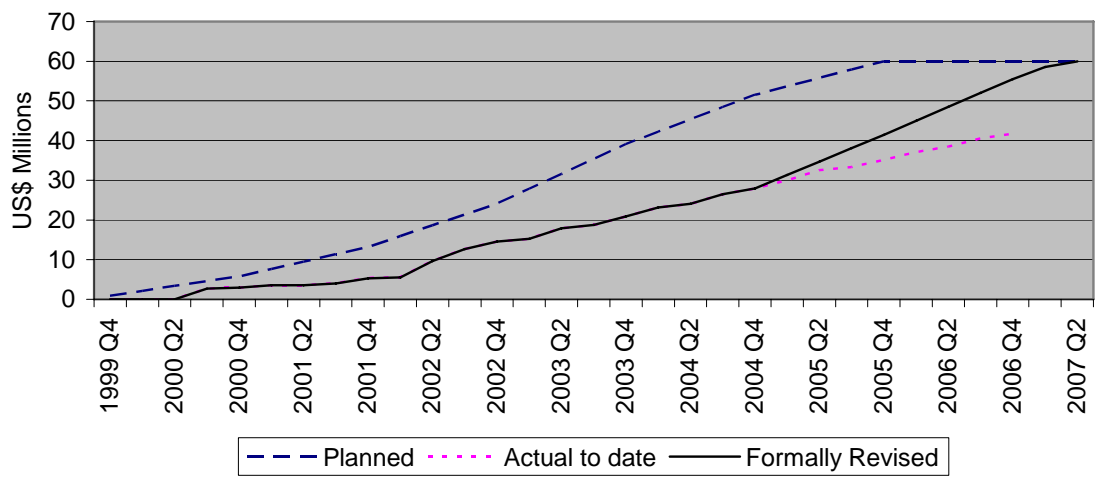

Project Name (ID): Second Beijing Environment Project (P042109)

Country: China

Board Approval Date : 06/20/2000

Midterm Review Date : 11/08/2002

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-45660, JPN-27034

Sector(s): Sewerage (49%), District heating and energy efficiency services (48%), Other industry (2%), Sub-national government administration (1%)

Theme(s): Climate change (P), Pollution management and environmental health (P), Environmental policies and institutions (P), Other urban development (P), Water resources management (P)

Project Development Objectives:

Visible and sustained alleviation of air and water pollution in Beijing


Progress toward achieving development objective(s):

Beijing Government is very committed to improving air and water quality in light of the 2008 Olympics. Air pollution control (Part A) got off to a slow start, but was eventually financed by own funds and implemented with good results. Seventy percent of Beijing's boilers have been now been converted to cleaner fuels; however substantial loan savings (\$150 million) remain. The wastewater management component (Part B) has been successfully implemented, with three wastewater treatment plants constructed and commissioned, but with another \$50 million in loan savings. With these substantial savings, an amendment is underway to finance the rehabilitation of selected sections of several rivers in the Beijing area, plus construction of a wastewater re-use facility and protection of groundwater through construction of a solid waste transfer station. All the additional components will enhance the alleviation of pollution. Finally, under the institutional strengthening component (Part C), Beijing authorities are finalizing plans to bring water supply and wastewater activities under a Water Affairs Group to strengthen coordination. Beijing Drainage company is performing well.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45660	Effective	349.00	108.90	240.10	0.00
JPN-27034	Closed	0.64	0.51	0.00	0.13



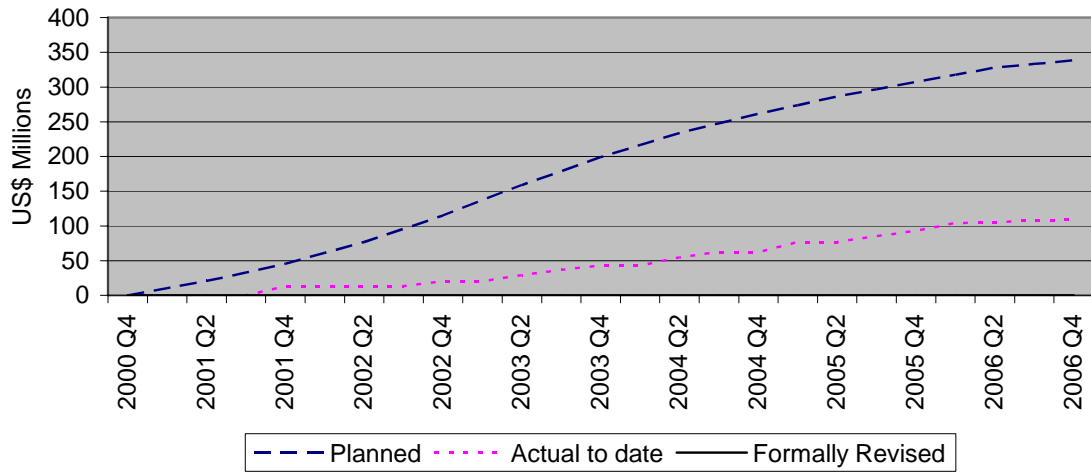

Project Name (ID): CN-Tec Coop Credit IV (P042299)

Country: China

Board Approval Date : 05/18/1999

Closing Date : 10/31/2007

Loan/Credit/Grant Number : IBRD-44730, IDA-32120, UK-53180

Sector(s): Central government administration (50%), Sub-national government administration (50%)

Theme(s): Macroeconomic management (P), Analysis of economic growth (P), Other rural development (P), Other social protection and risk management (P)

Project Development Objectives:

The objective of the project is to provide continued support to the Government of China in its economic and structural reform effort, help capacity building and improve the project preparation.


Progress toward achieving development objective(s):

The project continued to achieve its objectives. Large number of government agencies and institutions, both at the central and local levels, have benefited from the project. The project has put forward and submitted to the decision makers, 20 recommendations in 7 areas, to help rural development and poverty reduction through improvement of rural public finance. Capacity building and enhancement of disaster reduction is obvious and its impact is substantial. The project outputs – regional models and software, have contributed to the design of the disaster reduction satellite, as well as the establishment of China's National Disaster Reduction Emergency system. In addition, the project has helped 3 projects under preparation.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-44730	Effective	10.00	0.89	9.11	0.00
IDA-32120	Effective	37.78	25.08	11.82	0.00
UK-53180	Closed	2.90	2.93	0.00	0.07



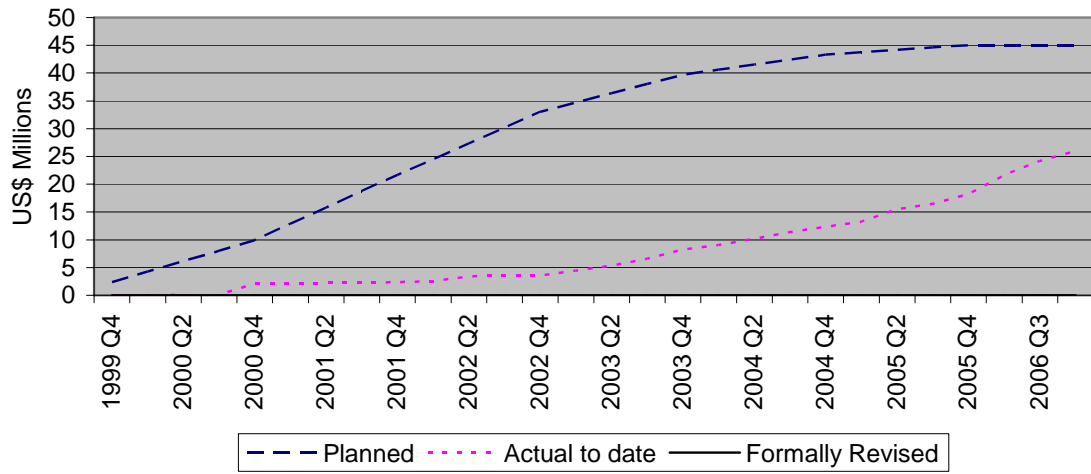

Project Name (ID): SICHUAN URBAN ENVIRONMENT PROJECT (P043933)

Country: China

Board Approval Date : 06/17/1999

Midterm Review Date : 11/17/2003

Closing Date : 01/31/2007

Loan/Credit/Grant Number : IBRD-44960, IDA-32510, JPN-26426

Sector(s): Sewerage (51%), Water supply (38%), Sub-national government administration (8%), Solid waste management (2%), Other social services (1%)

Theme(s): Other urban development (P), Municipal governance and institution building (P), Water resources management (P), Pollution management and environmental health (P), Municipal finance (S)

Project Development Objectives:

To provide a safe environmental setting for the sustainable long-term economic growth of urban areas in Sichuan Province.


Progress toward achieving development objective(s):

Most of the original physical investments have been completed and are helping establish a safer urban environment. Pollution in the Sichuan river system arising from untreated municipal wastewater discharges has been significantly reduced with completion of wastewater treatment plants in Chengdu and Leshan. Substantial loan savings remain and a portion of these savings will likely fund additional works. (A partial cancellation is also likely.) These additional works will require another extension of the loan closing date but will also enhance achievement of the project's benefits. Capacity building efforts are somewhat behind schedule and will be the subject of greater attention in the extension period to ensure sustainability.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-44960	Effective	100.00	39.00	61.00	0.00
IDA-32510	Closed	2.20	1.64	0.34	0.00
JPN-26426	Closed	0.40	0.22	0.00	0.18



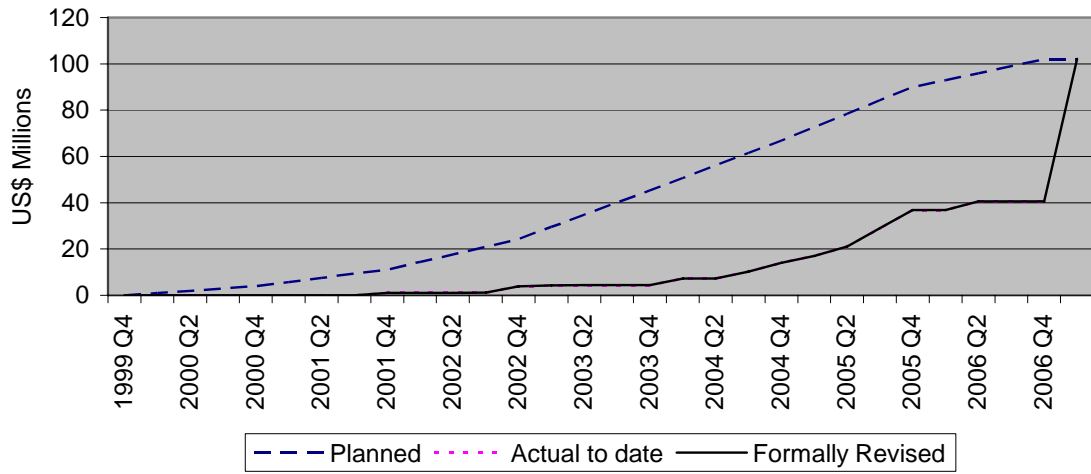

Project Name (ID): SHANGHAI WAIGAOQIAO (P044485)

Country: China

Board Approval Date : 06/24/1997

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-41970

Sector(s): Power (100%)

Theme(s): Climate change (P), Pollution management and environmental health (P), Other financial and private sector development (P), Regulation and competition policy (P), Decentralization (S)

Project Development Objectives:

To (a) increase electricity supply to reduce the acute power shortages in Shanghai; (b) develop a program to apply for the first time in China the "bubble concept" for cost effective air quality management; (c) support the ongoing power sector reform; increasing private sector involvement, and adjusting the tariff level; and (d) promote an innovative and diversified financing model for large infrastructure projects and improve the access of power entities to international financial markets.


Progress toward achieving development objective(s):

The commissioning of the first and second 900 MW units contributed significantly to the reduction of acute power shortages. Shanghai authorities officially commended the implementing agencies on reducing the impacts of power shortages in the municipality economy and society. The two 900 MW units have achieved all key performance indicators expected at appraisal. The "bubble concept" has been successfully demonstrated. The FGD units linked to the Waigaoqiao 300 MW units and co-financed by the Japanese Bank for International Cooperation (JBIC) have been commissioned and are operating satisfactorily. The reform went beyond what has been envisaged at appraisal time. Shanghai is participating in the East China Competitive Market which is operated by the East China Grid Corporation. All diversified financing objectives have been successfully achieved.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-41970	Effective	400.00	355.37	44.63	0.00



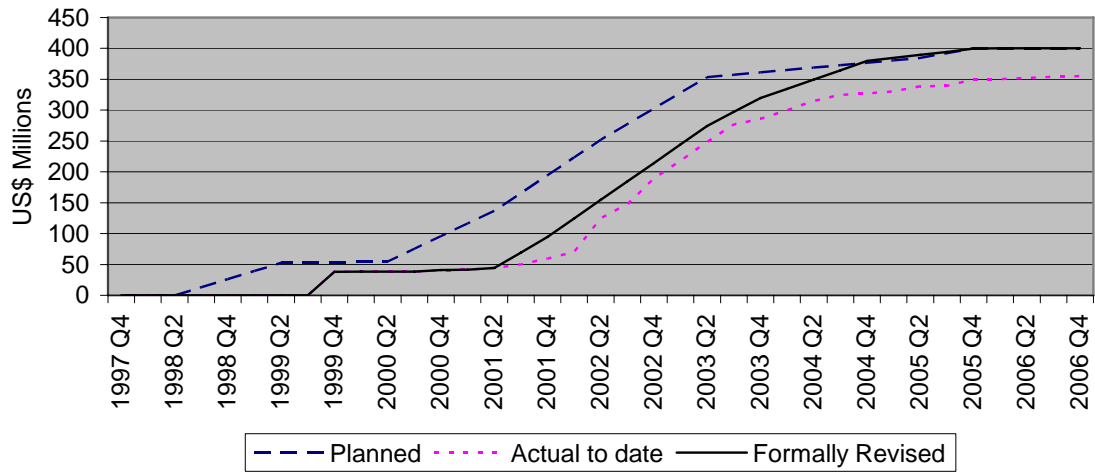

Project Name (ID): HEBEI URBAN ENVIRONMENT PROJECT (P045910)

Country: China

Board Approval Date : 06/27/2000

Midterm Review Date : 11/15/2004

Closing Date : 06/30/2007

Loan/Credit/Grant Number : IBRD-45690, JPN-26661

Sector(s): Sewerage (66%), Water supply (33%), Sub-national government administration (1%)

Theme(s): Water resources management (P), Pollution management and environmental health (P), Access to urban services and housing (P), Environmental policies and institutions (P)

Project Development Objectives:


To develop a safe environment and to sustain the long-term economic growth of urban areas in Hebei Province.

Progress toward achieving development objective(s):

Progress toward meeting the objectives is being made. The project is financing construction of wastewater treatment plants and sewer interceptors that will improve the urban environment in the three project cities of Handan, Tanshan and Shijiazhuang. Adequate supplies of safe water are being provided through construction of water production plants and associated distribution networks. Sustainability is being ensured through implementation of institutional and financial reforms of the cities' service utilities, although such reforms are somewhat behind schedule.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45690	Effective	150.00	99.96	50.04	0.00
JPN-26661	Closed	0.36	0.36	0.00	0.00

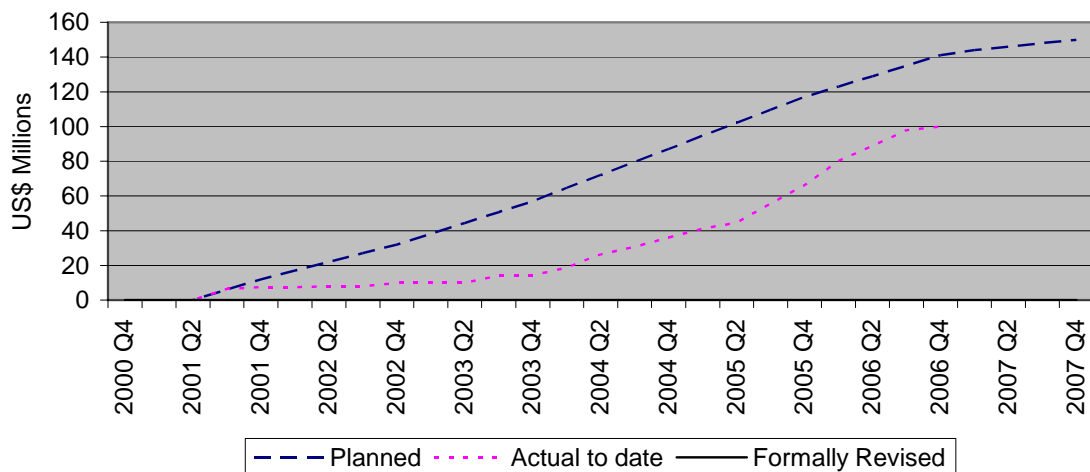

Project Name (ID): Urumqi Urban Transport Improvement Project (P045915)

Country: China

Board Approval Date : 12/19/2000

Midterm Review Date : 06/04/2004

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-45900, JPN-25107

Sector(s): Roads and highways (88%), Sub-national government administration (8%), General transportation (4%)

Theme(s): Infrastructure services for private sector development (P), Access to urban services and housing (P), Pollution management and environmental health (S), Climate change (S), Municipal governance and institution building (S)

Project Development Objectives:

To foster a multi-modal urban transport system which is planned, designed and used for the safe, efficient and healthy movement of people and goods.

Progress toward achieving development objective(s):


Progress toward meeting the development objectives has been steady, progress on objectives not related to road network development has been accelerated. The completion of the ring road has reduced traffic congestion.

Following the policy workshop in Oct. 2005, the municipality agreed to take a more comprehensive approach to develop a multi-modal urban transport system. Implementation of measures to increase the safety and efficiency of the road network and to develop a pilot public transport as a viable alternative to private car use has started. Greening to improve the environment is progressing, and recommended institutional restructure for the Motor Vehicle Emission Control Program was to be approved by the municipality. Some progress has been made on capacity strengthening.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45900	Effective	100.00	66.86	33.14	0.00
JPN-25107	Closed	0.40	0.40	0.00	0.00



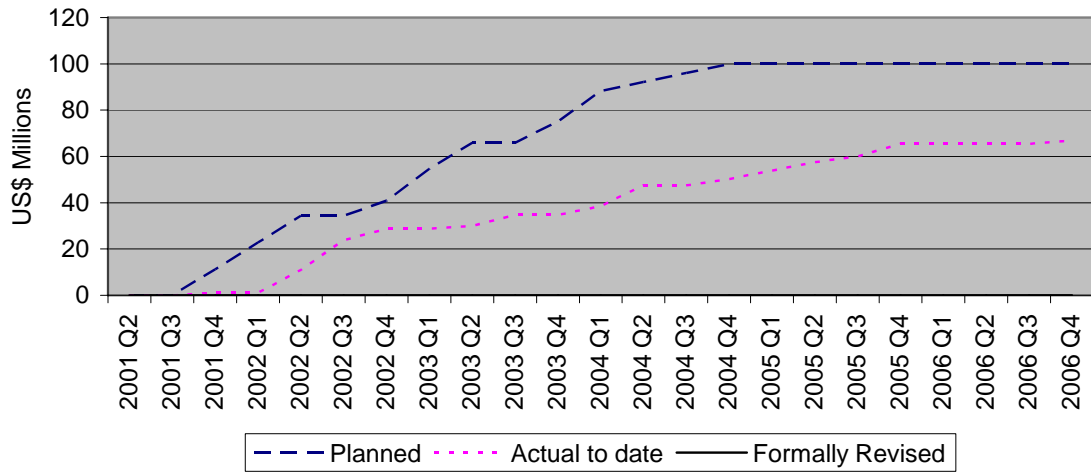

Project Name (ID): CN-Renewable Energy Development (P046829)
Country: China
Board Approval Date : 06/08/1999
Midterm Review Date : 04/23/2004
Closing Date : 06/30/2007
Loan/Credit/Grant Number : IBRD-44880, JPN-25513, JPN-51151
Sector(s): Renewable energy (100%)
Theme(s): Climate change (P), Rural services and infrastructure (P)

Project Development Objectives:

To develop a sustainable market for photovoltaic (PV) technologies and demonstration of the viability of commercial wind development in the coastal regions

Progress toward achieving development objective(s):


PV system sales continue to grow, and several participating PV companies are growing along with the market and increasing their reach (for example through exports). The Project Management Office is increasingly orienting its activities towards post-project sustainability to ensure standards and quality can be maintained (for example by establishing an industry association). The wind farm at Nanhui is now operating, and is demonstrating the benefits of a well conceived design and competitively procured project, though costs are higher than expected. The green electricity scheme, introduced in Shanghai in mid-2004, will purchase electricity from the wind farms at a premium price, thus ensuring the wind farm's financial sustainability. The demonstration effect seems to have paid off: Shanghai Wind Farm Company is now developing further wind farms in the municipality, including a self-financed extension to the Nanhui site.

Existing PV systems and the generation from the wind farms are contributing to CO2 (and other pollutant) reductions, PV costs are below end of project expectations. Wind costs have also come down though not as much as expected because of the fall in the value of the dollar, in which the project costs have been denominated, while wind equipment is largely based on Euro costs (additionally in Shanghai, the unexpectedly high cost of foundations mean at the project level the cost reductions have not been as high as expected, though they have been at the subsector level). Large-scale commercialization of the technologies is now strongly evident.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-44880	Effective	13.00	10.38	2.62	0.00
JPN-25513	Closed	0.43	0.43	0.00	0.00
JPN-51151	Effective	0.49	0.16	0.33	0.00



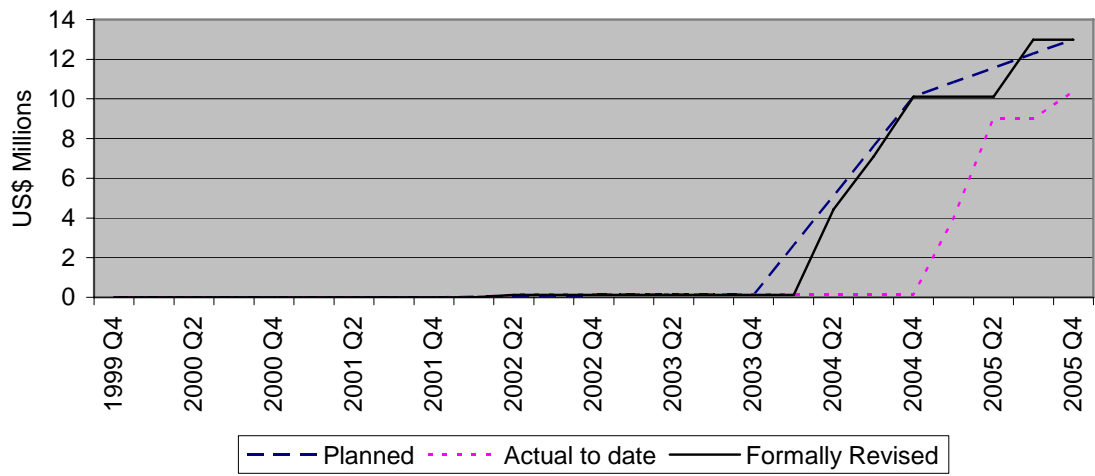

Project Name (ID): Huai River Pollution Control Project (P047345)
Country: China
Board Approval Date : 03/22/2001
Midterm Review Date : 10/19/2004
Closing Date : 06/30/2007
Loan/Credit/Grant Number : IBRD-45970, JPN-29717
Sector(s): Sewerage (100%)
Theme(s): Water resources management (P), Pollution management and environmental health (P)

Project Development Objectives:

To upgrade water quality in the Huai River Basin particularly in the provinces of Anhui and Shandong.

Progress toward achieving development objective(s):


Shandong's original program of three wastewater treatment plants and networks is complete in the municipalities of Feicheng, Heze and Ju County and in the final stages in Rizhao and at the Chengwu Paper Mill. The additional program approved in FY05 is complete in Ju County and is underway elsewhere. Wastewater companies are operating in Feicheng, Heze, Rizhao and Ju County, and wastewater tariffs have been increased to ensure financial sustainability.

In Anhui, the project financed wastewater operations in eight municipalities. Wastewater treatment plants are operating in all eight, but below capacity, as the accompanying collection network is still under construction. Full completion of all works by June 2007 will be tight. All municipalities have increased wastewater tariffs and collections have improved, but the latter should improve further. Once all works are complete, the water quality in the Basin should improve significantly. Borrower commitment to this objective remains high.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45970	Effective	105.50	59.36	46.14	0.00
JPN-29717	Closed	0.32	0.32	0.00	0.00



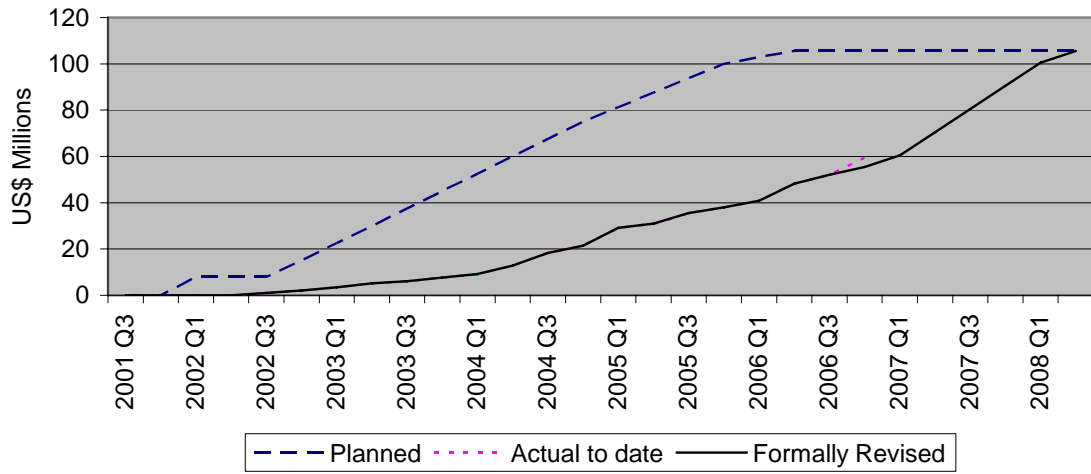

Project Name (ID): CHONGQING URBAN ENVIRONMENT PROJECT (P049436)

Country: China

Board Approval Date : 06/15/2000

Midterm Review Date : 07/23/2004

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-45610, JPN-25098, JPN-26651

Sector(s): Sewerage (74%), Solid waste management (15%), Water supply (6%), Sub-national government administration (5%)

Theme(s): Pollution management and environmental health (P), Water resources management (P), Environmental policies and institutions (P), Access to urban services and housing (P)

Project Development Objectives:

To provide a safe environmental setting for the sustainable long-term economic growth of urban areas in Chongqing Municipality.


Progress toward achieving development objective(s):

Steady progress continues with several components nearing completion. For example, two large wastewater treatment plants (Jiguanshi and Tangjiatuo) and related collection networks were finished in 2005 and are commencing operations in 2006. These works will contribute to establishing a safer urban environmental for longer term growth. Last year, with loan savings, eight new components were approved, and got underway in 2006. When completed, these will further enhance the project's benefits. Steady progress also continues on institutional and financial aspects. Chongqing Municipality raised its tariffs for wastewater services in January 2005 and progress in strengthening management and staffing continues. The new local governments coming to the project through the new components, will receive technical assistance to strengthen their performance and improve sustainability.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45610	Effective	200.00	86.11	110.19	3.70
JPN-25098	Closed	0.10	0.10	0.00	0.00
JPN-26651	Closed	0.32	0.32	0.00	0.01



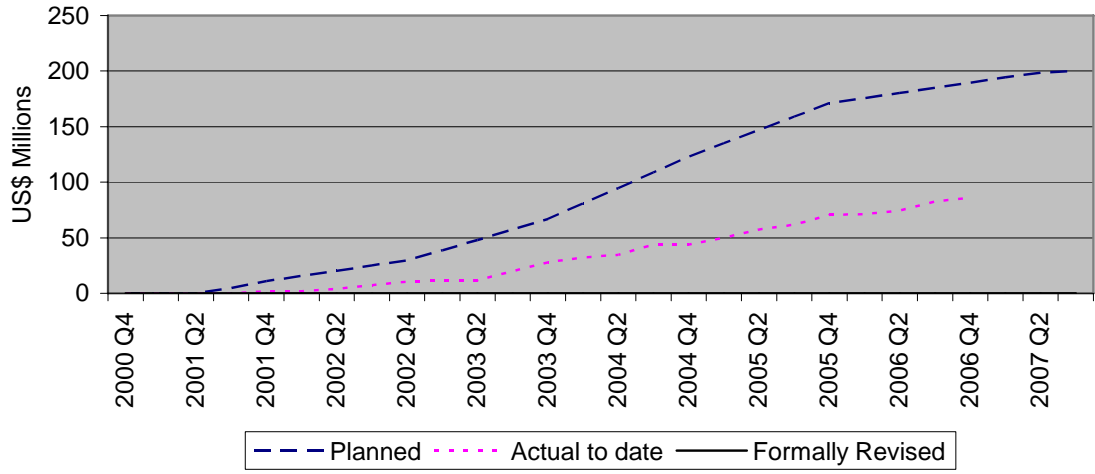

Project Name (ID): CN-Anning Valley Agric. Development (P049665)

Country: China

Board Approval Date : 01/21/1999

Midterm Review Date : 03/20/2002

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-44360, IDA-31650, JPN-25506

Sector(s): Irrigation and drainage (39%), Crops (32%), Animal production (18%), Central government administration (7%), Agricultural marketing and trade (4%)

Theme(s): Land administration and management (P), Other rural development (P)

Project Development Objectives:

The objective is to increase production, productivity, marketability and value-added of agriculture, horticulture and animal husbandry in the Anning Valley, with the specific aim of reducing the poverty of farmers in remote areas.


Progress toward achieving development objective(s):

Six of the seven components of the project have been fully completed. Only the Water Resources Development component is as yet incomplete, particularly some key canal works under the Manshuiwan sub-component. While the implementation of this sub-component has made good progress, some critical and difficult works remain to be completed under the three branch canal contracts, with overall completion now at about 90 percent. The project implementing entity expects that most, if not all, works under these contracts will be completed by the Loan Closing Date of December 31, 2006, subject to: (a) adequate counterpart funding being available; and (b) good weather conditions.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-44360	Effective	90.00	90.00	0.00	0.00
IDA-31650	Effective	31.46	28.87	0.00	0.00
JPN-25506	Closed	0.12	0.12	0.00	0.00



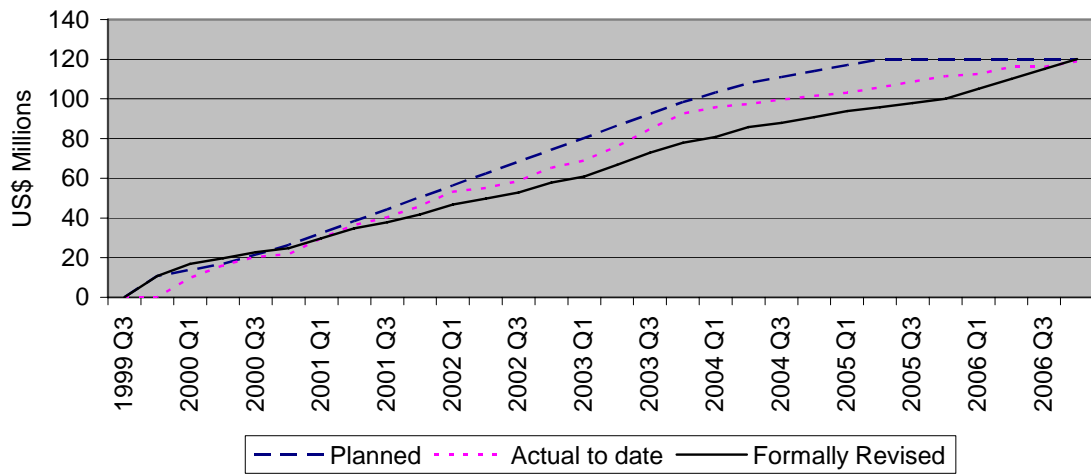

Project Name (ID): Second Fujian Highway Project (P051705)

Country: China

Board Approval Date : 06/24/1999

Midterm Review Date : 05/01/2003

Closing Date : 06/30/2007

Loan/Credit/Grant Number : IBRD-45020

Sector(s): Roads and highways (100%)

Theme(s): Rural services and infrastructure (P)

Project Development Objectives:

(a) relieve traffic congestion and improve the mobility and integration of inter-provincial trade, commerce and tourism between Fujian and Guangdong Provinces;(b) strengthen highway institutional capacity at the Fujian Provincial Transport Department and related sector institutions; (c) develop and sustain a policy dialogue in the key policy area of province-wide highway maintenance management; and (d) improve the safety of road transport.

Progress toward achieving development objective(s):

The largest investment component--the Zhangzhou-Zhao'an Expressway--was completed successfully in 2003. The current focus is on the completion of the components related to improvement to local roads (largely Class II) across the province and the treatment of black spots. The inclusion of a package of six additional roads in 2004 required the extension of the loan closing date for another two years. The technical and training activities are well advanced.

In all, the achievement of the project development objectives is feasible. Most indicators show positive trends though slightly below the values estimated at appraisal. Traffic volumes are lower than appraisal values but their rates of growth are high. Traffic accidents are within the values estimated at appraisal. Intermediate outputs (inputs related to the project components) are either complied with or within the expected percentages.


The strategic issue--not reported through the PDO or intermediate indicators--is the extent of internalization of the institutional development actions--largely those related to road management and the training activities. There is evidence of improved management of overloading and enhanced attention to road safety issues. (On the latter, a report on the treatment of black spots shows marked improvement on road safety across those spots.) More efficient and effective maintenance practices however appear to have received less consideration (as shown by the substantial delay in the completion of the highway maintenance study). This latter issue is being addressed as part of the dialogue that has taken place under the preparation of the proposed Fujian Highway Sector Investment Project. FPCD has agreed to include in this project a specific component to finance, on a



pilot basis, alternative mechanisms for the maintenance of road assets. This shows a predisposition to also move in this issue that is critical for strengthening asset management practices in the Fujian province.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45020	Effective	200.00	175.18	24.82	0.00

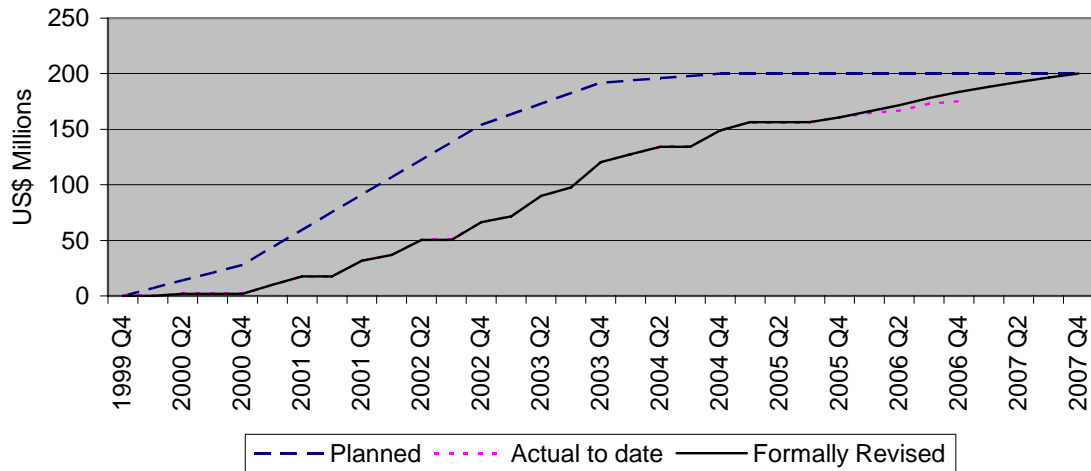

Project Name (ID): CN-Accounting Reform & Development (P051856)
Country: China
Board Approval Date : 02/23/1999
Midterm Review Date : 10/23/2003
Closing Date : 12/31/2007
Loan/Credit/Grant Number : IBRD-44420, IDA-31730
Sector(s): Tertiary education (83%), Central government administration (17%)
Theme(s): Standards and financial reporting (P), Other public sector governance (S)

Project Development Objectives:


The fundamental objective of the project is to accelerate the modernization of China's accounting professionals and accounting systems.

Progress toward achieving development objective(s):

The project continues to make good progress toward achieving its development objective. Recently China issued 38 accounting standards. It marks the establishment of a new system of Chinese Accounting Standards, which suites the development of China's market economy and convergence with international practices. These accounting standards will be effective from January 1, 2007 for listed companies. Other companies are encouraged to adopt. The new accounting standards represent convergence with International Financial Reporting Standards (IFRS).

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-44420	Effective	27.40	20.29	7.11	0.00
IDA-31730	Effective	6.03	4.02	1.64	0.00

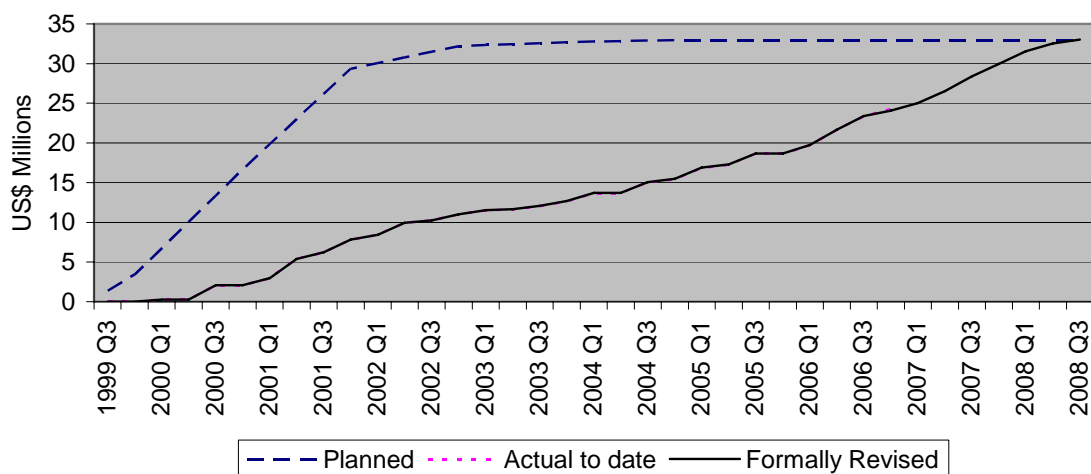

Project Name (ID): Liao River Basin Project (P051859)

Country: China

Board Approval Date : 06/19/2001

Midterm Review Date : 07/02/2004

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-46170, JPN-25912, JPN-50520

Sector(s): Sewerage (83%), Other industry (10%), Sub-national government administration (7%)

Theme(s): Water resources management (P), Pollution management and environmental health (P)

Project Development Objectives:

To assist the environmental recovery of the Liao River Basin in Liaoning Province and to enhance water quality management decision-making on the basis on an integrated river basin management approach.


Progress toward achieving development objective(s):

The project continues to make excellent progress and is on schedule for completion by December 2007. The wastewater components in Jinzhou, Panjin and Yingkou have been substantially completed and will be fully operational by December 2006. The industrial wastewater component at the Yingkou and Jincheng Paper Mills is at an advanced stage. Sub-loans under the environmental pollution control program are being made to small and medium enterprises, with over 70% of the loan allocation committed, and implementation is moving well. Institutional development efforts are also solid with adequate tariffs, but collection of wastewater tariffs, could be improved. Overall, the project's works and institutional measures are assisting with the sustainable recovery of the Liao River Basin.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46170	Effective	100.00	72.73	27.27	0.00
JPN-25912	Closed	0.76	0.76	0.00	0.00
JPN-50520	Closed	1.21	1.21	0.00	0.00



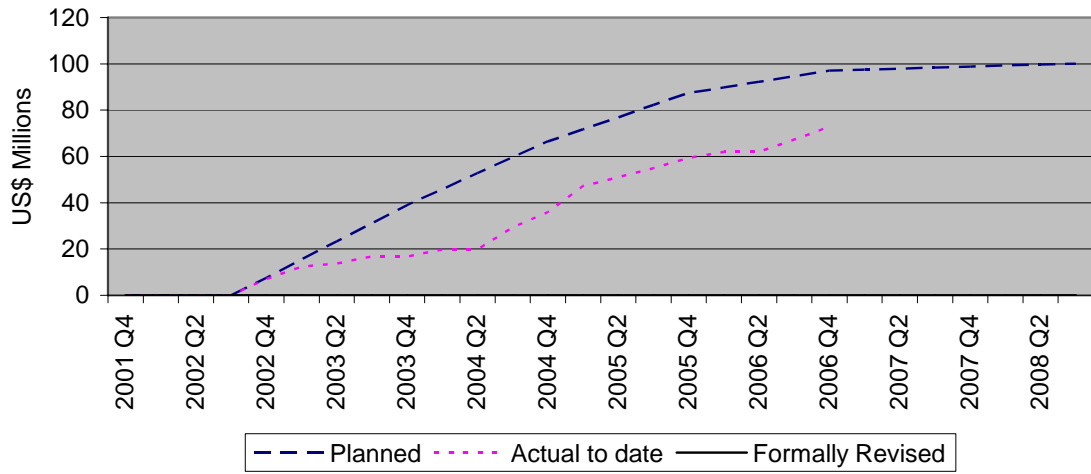

Project Name (ID): Third Inland Waterways (P056199)

Country: China

Board Approval Date : 06/21/2001

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-46210, JPN-25699

Sector(s): Power (77%), Ports, waterways and shipping (12%), General water, sanitation and flood protection (6%), Roads and highways (3%), Central government administration (2%)

Theme(s): Rural services and infrastructure (P), Climate change (S), Decentralization (S), Access to urban services and housing (S)

Project Development Objectives:

To reduce transport and energy bottlenecks by: (a) improving market access of the remote inland areas of Hunan Province; (b) providing more efficient and economic inland waterway transport; and (c) generating power to supplement the needs of the remote areas.


Progress toward achieving development objective(s):

At roughly 95% physical completion, project implementation is ahead of schedule, the quality of construction appears very good, and the projected cost at completion should be less than the original estimate. Pending final completion of the facility (consisting of a dam, shiplock and powerhouse) to plan, the objective appears achievable. Improved market access and efficient inland waterway transport are being achieved by the filling of the reservoir in 2004 and the opening of the shiplock in December that year. The powerhouse at Zhuzhou is close to commissioning with the last of the five generating units due to come on line in August 2006. Sustainability of the project will be ensured by the on-going training and TA in the areas of project management and design optimization.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46210	Effective	100.00	73.45	26.55	0.00
JPN-25699	Closed	0.80	0.72	0.00	0.08



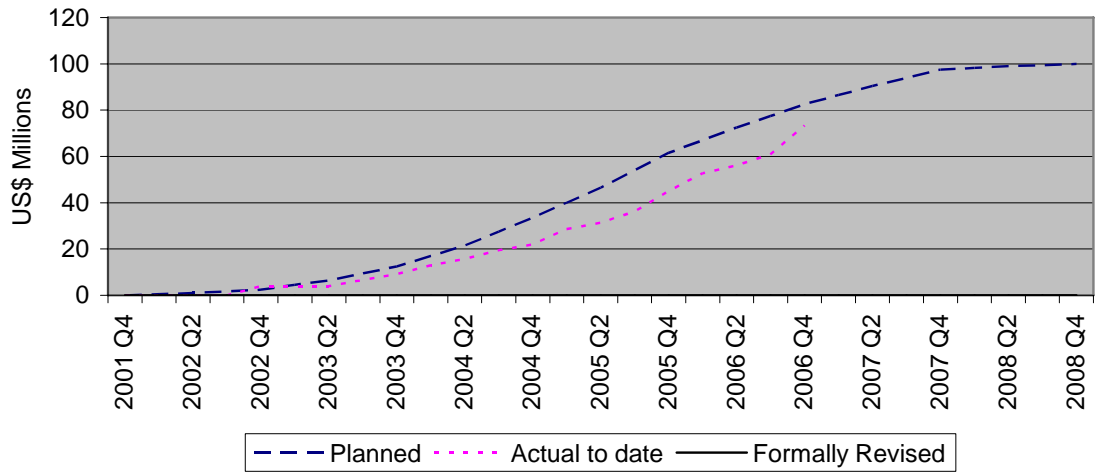

Project Name (ID): China Tongbai Pumped Storage (P056424)

Country: China

Board Approval Date : 12/22/1999

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-45290, JPN-25701

Sector(s): Power (99%), Sub-national government administration (1%)

Theme(s): Rural services and infrastructure (P), Regulation and competition policy (P), Other financial and private sector development (P), Climate change (P), Infrastructure services for private sector development (P)

Project Development Objectives:

To (a) increase peaking capacity and improve load-following capability and power quality in the Zhejiang and East China power systems; and (b) improve the operating and investment efficiency in generation by developing and implementing a competitive generation market in Zhejiang province.


Progress toward achieving development objective(s):

Progress toward achieving project objectives is steady: (a) the pumped storage power plant component is on schedule despite equipment delivery delays. Commercial operation for the unit 1 commenced in May 2006, while that for the units 2&3 expects to be in September and December 2006 respectively, and that for the unit 4 in the second quarter of 2007; (b) the transmission reinforcement component has been successfully completed and under satisfactory operation; and (c) the originally planned activities under the technical assistance component are fully or substantially complete. A few new activities (such as consultant services in IT areas and training) are being implemented as expected.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45290	Effective	320.00	179.09	40.91	100.00
JPN-25701	Closed	0.58	0.58	0.00	0.00



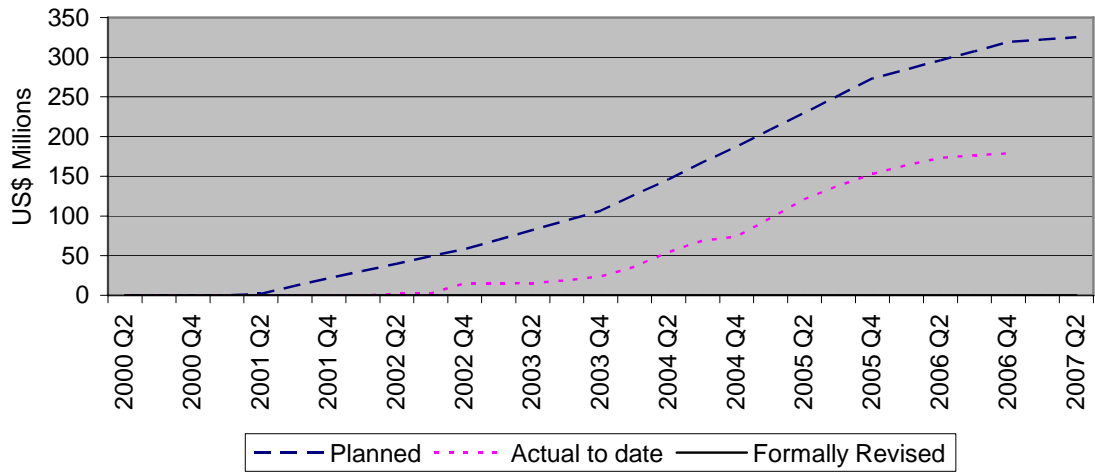

Project Name (ID): CN-Shijiazhuang Urban Transport (P056596)

Country: China

Board Approval Date : 03/27/2001

Midterm Review Date : 06/10/2004

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-46000, JPN-25415

Sector(s): Roads and highways (91%), General transportation (8%), Sub-national government administration (1%)

Theme(s): Other urban development (P), Municipal governance and institution building (S), Pollution management and environmental health (S)

Project Development Objectives:


To foster the development of an efficient and environmentally sustainable urban transport system in Shijiazhuang while providing a wider set of travel choices for users.

Progress toward achieving development objective(s):

Progress towards meeting all objectives is on track. The bicycle network has been increased, and traffic signal and junction channelization works which is to improve road network efficiency are in progress. Safety measures have been designed and ready for implementation. The operation of the Zhongshan bus way corridor has added more public transport passages over time. A kerb busway in Jianshe street was completed. Establishment of a road maintenance management system to increase quality and efficiency of maintenance has undergone testing. Additional public transport survey is on-going in order to form a public transport priority network.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46000	Effective	100.00	37.86	62.14	0.00
JPN-25415	Closed	0.38	0.38	0.00	0.00

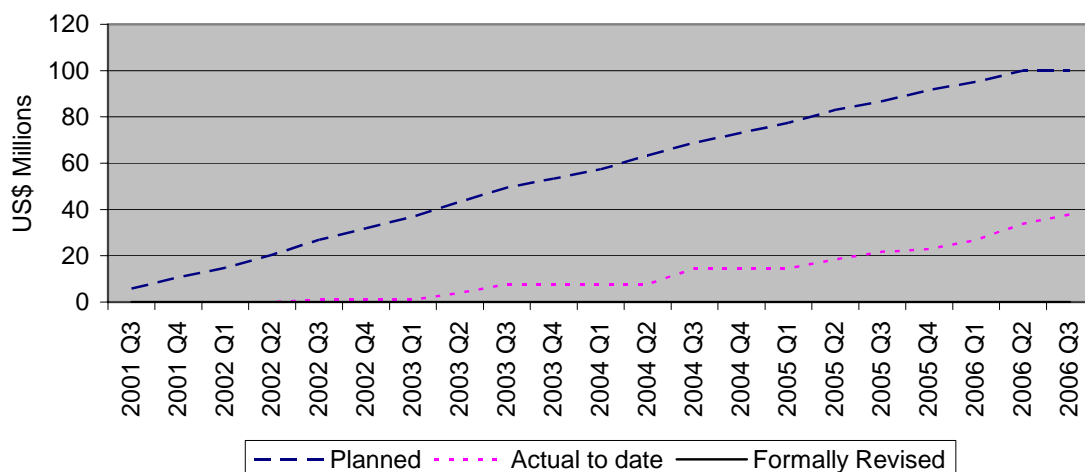

Project Name (ID): FOURTH RURAL WATER SUPPLY PROJECT (P057352)
Country: China
Board Approval Date : 06/03/1999
Midterm Review Date : 09/20/2002
Closing Date : 12/31/2006
Loan/Credit/Grant Number : IBRD-44850, IDA-32330
Sector(s): Water supply (91%), Sanitation (3%), Health (3%), Primary education (3%)
Theme(s): Rural services and infrastructure (P), Other human development (S)

Project Development Objectives:


To reduce the time and cost for people in poor rural areas to obtain clean, safe water supply, while improving related sanitation and health behaviors

Progress toward achieving development objective(s):

The project financed the construction of some 240 water supply systems, 17,000 village level sanitary latrines and about 5,000 household sanitary latrines. The safe water provided by water supply plants is improving access, leading to reduced collection times and costs, and improved health for the target beneficiaries. Latrines constructed are also improving health and are having the desired impact on health behaviors. Sustainability is now being emphasized in the final period.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-44850	Closed	16.00	14.10	1.90	0.00
IDA-32330	Effective	32.63	29.29	0.97	0.00

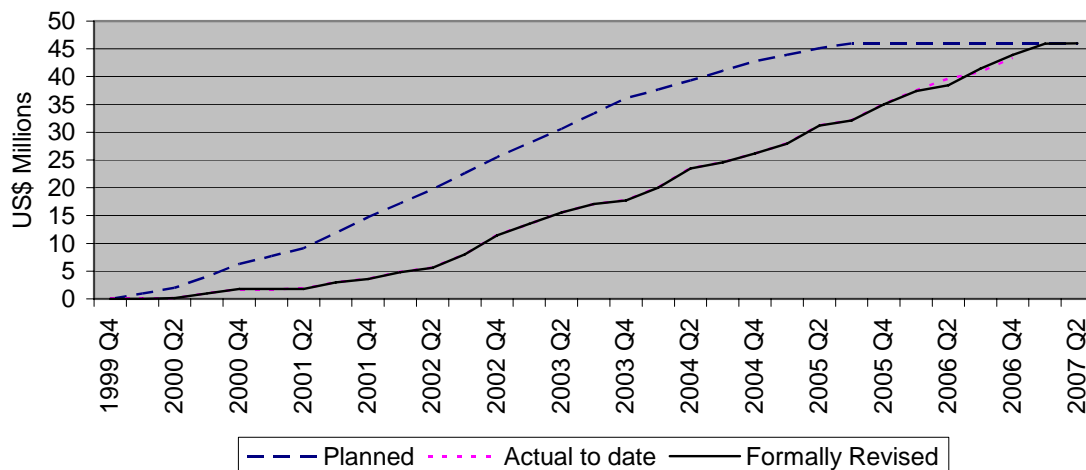

Project Name (ID): TAI BASIN URBAN ENVIRONMENT PROJECT (P057933)

Country: China

Board Approval Date : 08/03/2004

Closing Date : 12/31/2009

Loan/Credit/Grant Number : IBRD-47480, JPN-26178

Sector(s): Sewerage (90%), Flood protection (10%)

Theme(s): Water resources management (P), Pollution management and environmental health (P), Other urban development (P), Infrastructure services for private sector development (S)

Project Development Objectives:


To improve the quality of life of the rapidly increasing urban population and enhance economic competitiveness in Wuxi and Suzhou, key municipalities in the Tai Basin and the Yangtze River Delta economic region, by alleviating degradation of water resources and improving the quality of the urban environment.

Progress toward achieving development objective(s):

To increase collection and treatment of wastewater, most sewers financed by the project are now complete. Construction of a wastewater treatment plant is underway. Selective dredging is also ongoing, all of which will help improve the environment. Sustainability of services is likely to be achieved through new tariff arrangements and continued institutional strengthening.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47480	Effective	61.00	15.00	46.00	0.00
JPN-26178	Closed	0.88	0.88	0.00	0.00

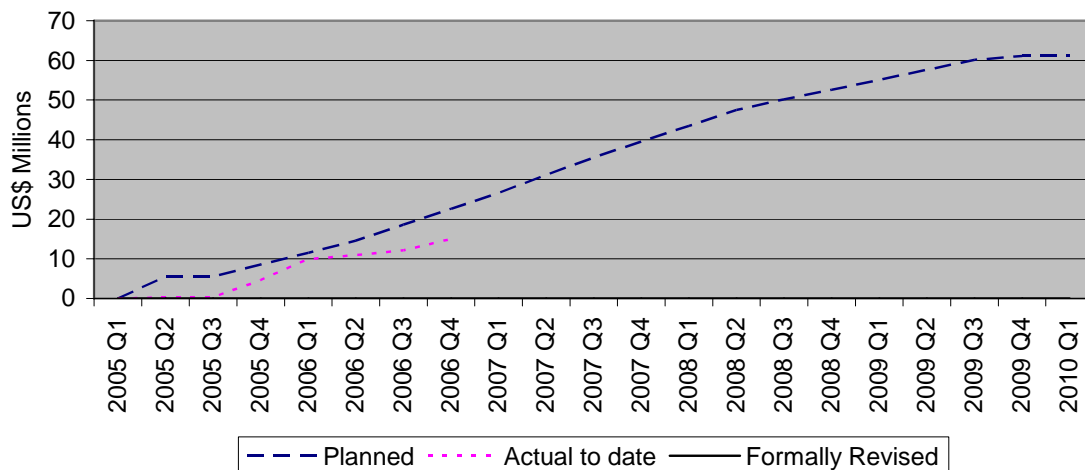

Project Name (ID): CN-Guangxi Highway (P058843)

Country: China

Board Approval Date : 03/28/2000

Closing Date : 06/30/2007

Loan/Credit/Grant Number : IBRD-45410

Sector(s): Roads and highways (97%), Sub-national government administration (3%)

Theme(s): Rural services and infrastructure (P), Infrastructure services for private sector development (P), Municipal governance and institution building (P)

Project Development Objectives:

The objective is to provide efficient, safe and cost-effective inter-provincial transport links among the land-locked interior provinces of Guizhou, Yunan, Sichuan and the city of Chongqing with Guangxi Zhuang Autonomous Region and the coastal province of Guangdong. These will help stimulate social and economic development, reduce poverty and thus improve regional disparities. Helping the Guangxi government strengthen its institutional capacity to plan, design, supervise, operate and maintain its highways.


Progress toward achieving development objective(s):

The objective of providing efficient inter-provincial transport appears achievable after the opening of the highway from Nanning to Shiren in late 2004 and the improvement of 231 km of rural roads in poor regions, also completed in late 2003. On the other hand, 2005 traffic data indicates lower than expected volumes bringing into question the cost-effectiveness of the investment. Further monitoring will determine if this lower than expected volumes will be sustained or if additional traffic is attracted to the highway. Implementation progress of the highway safety program has been slower than expected but is expected to achieve its objective of improving safety at selected accident-prone locations.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45410	Effective	200.00	175.21	5.09	19.70



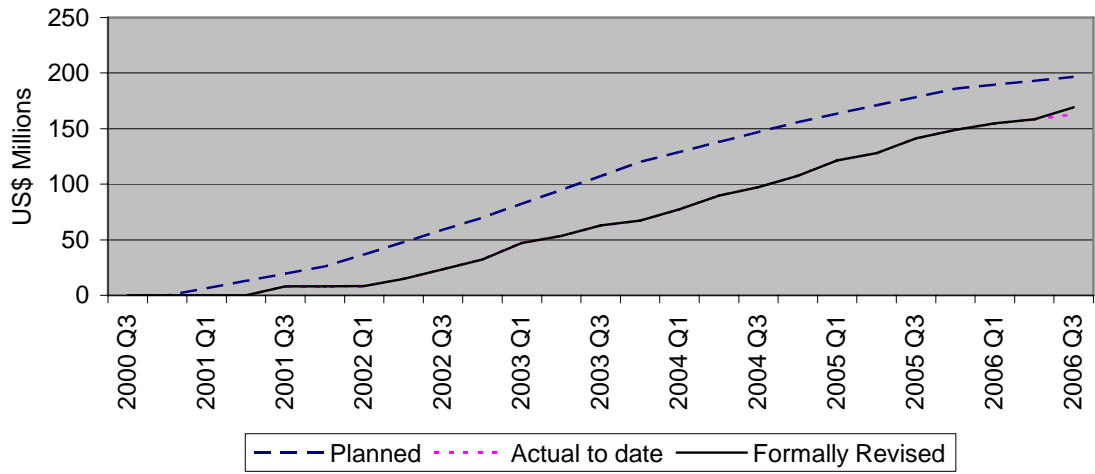

Project Name (ID): Third Henan Provincial Highway Project (P058844)

Country: China

Board Approval Date : 05/16/2000

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-45480

Sector(s): Roads and highways (98%), Sub-national government administration (2%)

Theme(s): Infrastructure services for private sector development (P), Rural services and infrastructure (P)

Project Development Objectives:


To provide a more efficient and effective transport infrastructure in support of social and economic development in Henan Province

Progress toward achieving development objective(s):

The project is on track to meeting its objectives. The Zhumadian-Xinyang Expressway is completed except for construction of a sub-communication center, and early indications are that traffic mobility and accessibility have increased. Judging from field inspections, this increased accessibility is facilitating social and economic development in rural areas. The project was extended by one year to allow for the implementation of civil work on an additional 12 Local Road in Poor Counties and completion of the procurement of goods. Institutional Development and Reform component is progressing slower than schedule in implementing results from useful studies. NDRC approved in May 2006 for the use of USD 10 million for an extended safety component which would require an second one (1) year extension.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45480	Effective	150.00	124.59	25.41	0.00

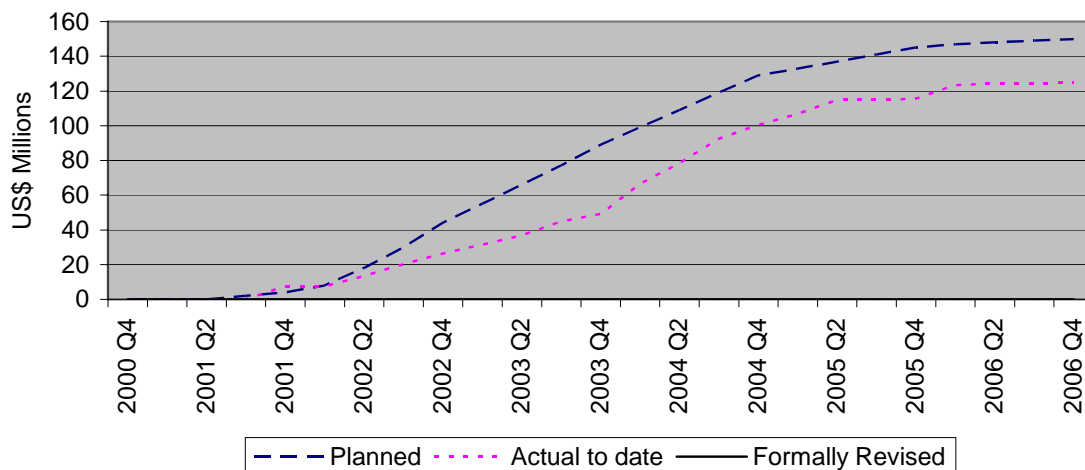

Project Name (ID): Second Jiangxi Highway Project (P058845)

Country: China

Board Approval Date : 06/05/2001

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-46080

Sector(s): Roads and highways (99%), Sub-national government administration (1%)

Theme(s): Rural services and infrastructure (P), Municipal governance and institution building (P), Access to urban services and housing (S), Other financial and private sector development (S)

Project Development Objectives:


To provide more efficient, safe and effective transport infrastructure in support of the social and economic development in Jiangxi Province.

Progress toward achieving development objective(s):

The progress towards achieving objectives is mixed. The expressway has significantly reduced travel times on interprovincial trips, as well as reduced the number of accidents on adjacent roads. However, traffic flows are lower than forecast in the corridor, especially on the expressway. The local roads program has significantly reduced the number of days roads are closed. Ongoing issues relate to construction quality and environmental problems on the expressway. Remedial actions have been developed, and the project is committed to resolving the problems.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46080	Effective	200.00	118.73	26.50	54.77

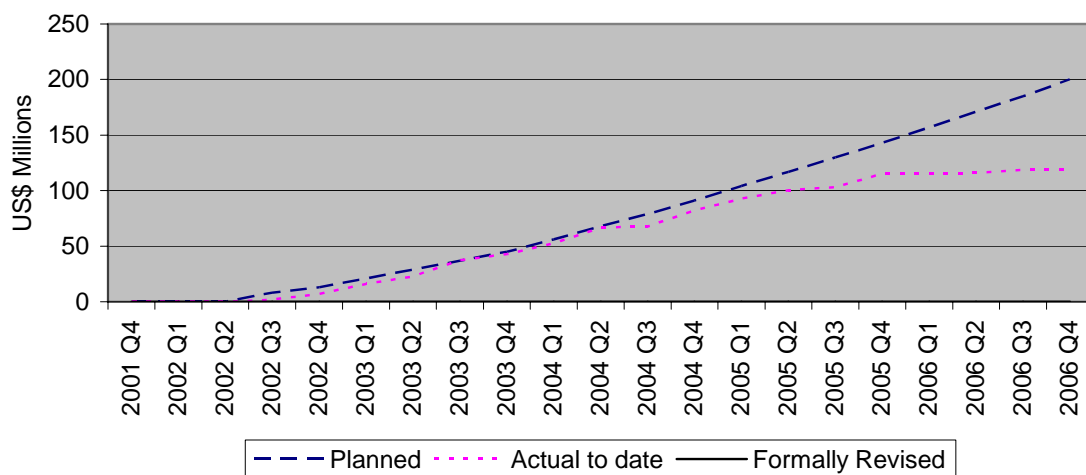

Project Name (ID): CN-National Railway Project (P058846)

Country: China

Board Approval Date : 01/29/2002

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-46480, JPN-29623

Sector(s): Railways (93%), Telecommunications (6%), Central government administration (1%)

Theme(s): Infrastructure services for private sector development (P), State enterprise/bank restructuring and privatization (P), Regulation and competition policy (S), Corporate governance (S)

Project Development Objectives:


To (a) increase the capacity of the railway network between eastern and western China; and (b) support the reform program of China Railways.

Progress toward achieving development objective(s):

The project is well on its way to achieving its objective. The Bao-Lan line, which was double-tracked and upgraded through the project, was put into operation in June 2003, one year early. It is expected that the performance indicators will support this achievement. Through working with the Bank, the Ministry of Railways has made significant movements towards reforming China Railways through restructuring and changes in administration.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46480	Effective	160.00	141.05	18.95	0.00
JPN-29623	Closed	0.81	0.45	0.00	0.36

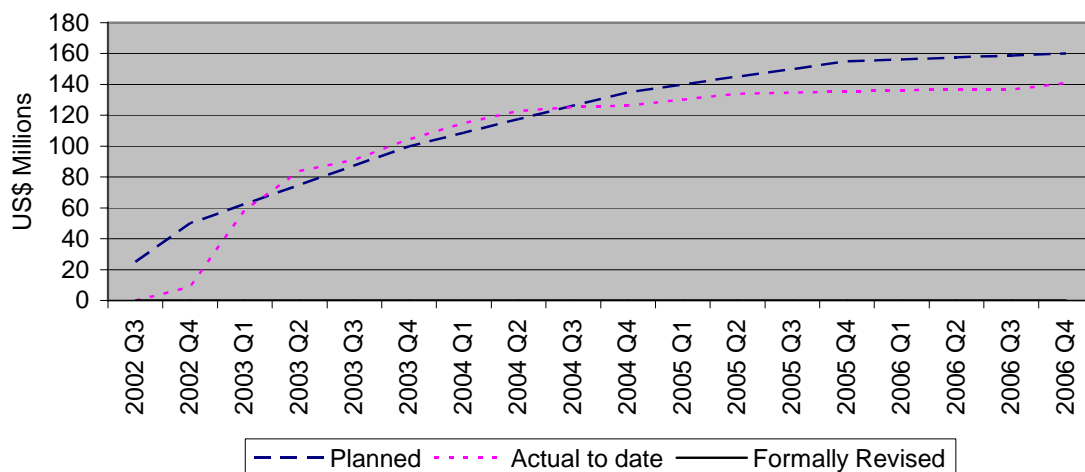

Project Name (ID): CN-3rd Xinjiang Hwy Project (P058847)

Country: China

Board Approval Date : 09/05/2002

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-71430, JPN-26427

Sector(s): Roads and highways (94%), Sub-national government administration (6%)

Theme(s): Rural services and infrastructure (P), Infrastructure services for private sector development (P), Other public sector governance (S)

Project Development Objectives:


To improve transport infrastructure and sector governance in support of social and economic development in Xinjiang Uygur Autonomous Region.

Progress toward achieving development objective(s):

Under the project's main component, the construction of the Kuitun-Sailimuhu highway was completed in the fall of 2005. Under the local roads rehabilitation component, the works accomplished to date are improving access for rural communities. The institutional component is exposing provincial staff to modern managerial approaches in the road sector. The two latter components are lagging behind schedule, but actions plans, with scheduled deliverables, to accelerate progress are being implemented. Overall, the project is on its way to meeting its objectives.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-71430	Effective	150.00	92.78	57.22	0.00
JPN-26427	Closed	0.20	0.20	0.00	0.00

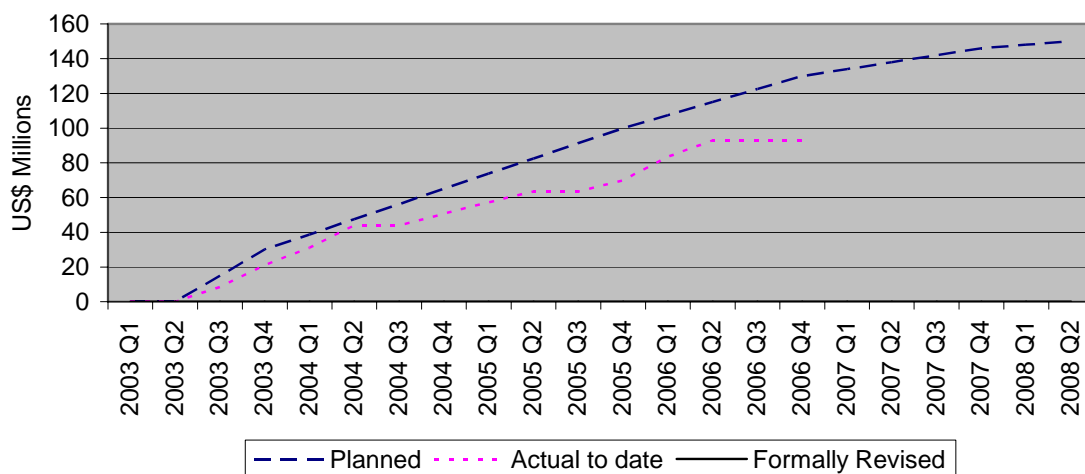

Project Name (ID): CN ODS IV PHASE OUT PRJ (P039838)

Country: China

Board Approval Date : 11/21/1997

Closing Date : 06/30/2011

Loan/Credit/Grant Number : MULT-23973, MULT-50722, WBTF-22014, WBTF-22017, WBTF-23972

Sector(s): Other industry (94%), Central government administration (6%)

Theme(s): Environmental policies and institutions (P), Pollution management and environmental health (P)

Project Development Objectives:


The key development objective of this Montreal Protocol project is the phaseout of Ozone Depleting Substances (ODS) in China.

Progress toward achieving development objective(s):

The project progressed very well in FY06 with ODS phaseout in eight sectors under implementation, including a new sector phaseout plan approved in April 2006. Preparation of the CFC phaseout plan in one additional sector, pharmaceutical aerosols, is underway. The sector plan is expected to be submitted to the November 2006 Excom meeting for approval.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-23973	Closed	0.12	0.12	0.00	0.00
MULT-50722	Closed	0.10	0.00	0.00	0.10
WBTF-22014	Closed	0.10	0.10	0.00	0.00
WBTF-22017	Effective	440.00	222.95	217.05	0.00
WBTF-23972	Closed	0.03	0.03	0.00	0.00

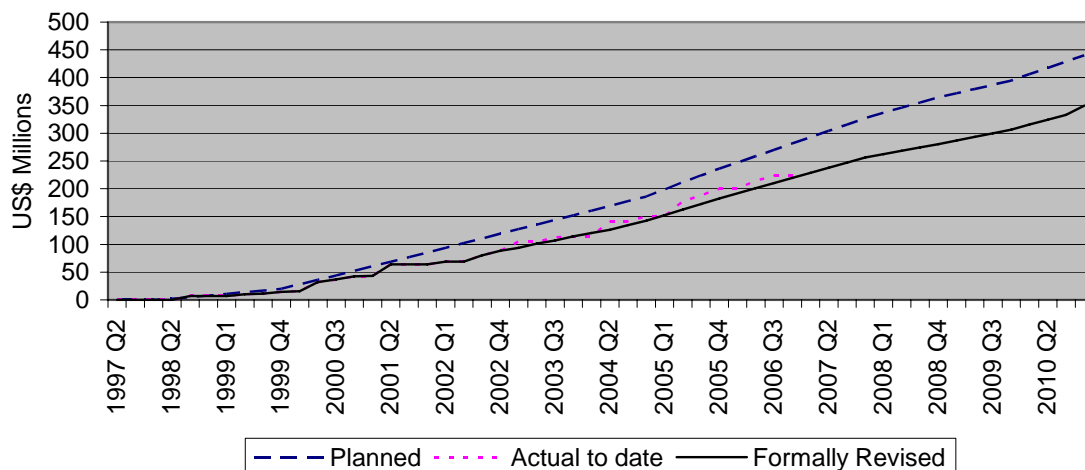

Project Name (ID): Second Tianjin Urban Development and Environment Project (P040599)

Country: China

Board Approval Date : 05/20/2003

Midterm Review Date : 08/07/2006

Closing Date : 06/30/2010

Loan/Credit/Grant Number : IBRD-46950, JPN-25106

Sector(s): Sewerage (45%), Sub-national government administration (25%), General transportation (20%), Flood protection (10%)

Theme(s): Access to urban services and housing (P), Pollution management and environmental health (P), Water resources management (S), Municipal governance and institution building (S), Infrastructure services for private sector development (S)

Project Development Objectives:

To enhance the efficiency and equity of urban wastewater management and transportation systems, and thus facilitate the sustainable development of Tianjin and serve as a model for other cities in China.


Progress toward achieving development objective(s):

Implementation has fallen behind schedule due to (a) slow land acquisition and (b) changes in counterpart funding mechanisms. An innovative "design-build-operate" contract for the Hangu wastewater treatment plant should be awarded very soon. Another innovation is the Dagu Canal Rehabilitation subproject involving the dredging of an 80-km long contaminated sewage canal and disposal to a contained landfill; this work is now underway. The water reuse component may be dropped due to questions of financial viability. Other possible design changes involve a reduction in the urban transport component, with a possible addition of a public bus component. A summer review of the proposed changes is planned, with the aim of achieving the objective of enhancing wastewater management and transportation systems in a sustainable manner.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46950	Effective	150.00	15.20	134.80	0.00
JPN-25106	Closed	0.57	0.41	0.00	0.16



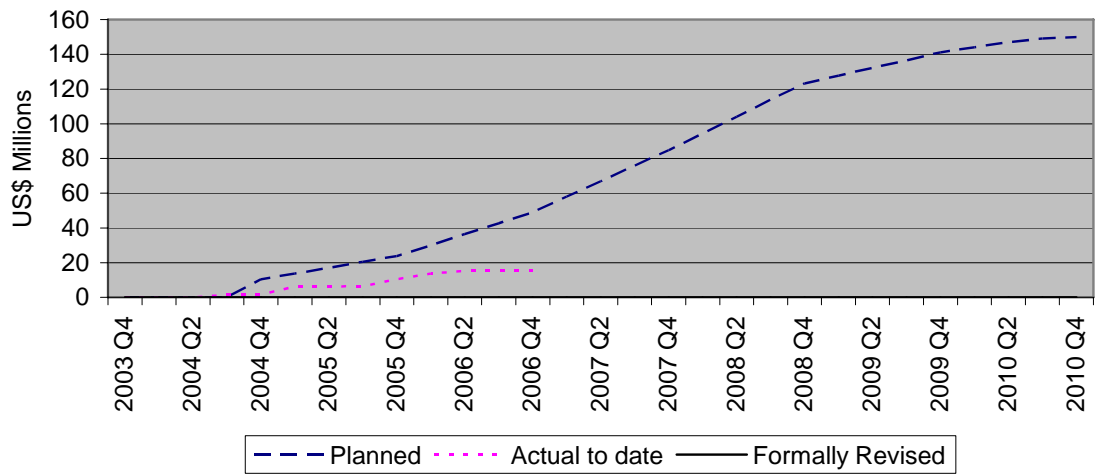

Project Name (ID): CN-Nat Hwy4/Hubei-Hunan (P041268)

Country: China

Board Approval Date : 06/17/1999

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IBRD-44930, JPN-29709

Sector(s): Roads and highways (99%), Sub-national government administration (1%)

Theme(s): Municipal governance and institution building (P)

Project Development Objectives:


The objectives are to: (a) relieve traffic congestion and improve the mobility and integration of inter-provincial trade and commerce between Hunan and Hubei Provinces; (b) strengthen highway institutional capacity at the Provincial Communications Departments and related sector institutions; (c) develop and sustain a policy dialogue in commercialization and corporatization of provincial toll road authorities and of province-wide highway maintenance management; and (d) improve the safety of road transport.

Progress toward achieving development objective(s):

The project has progressed well and all civil works are completed. The expressways are carrying a significant amount of traffic and have fostered interregional trade. In both provinces activities on institutional strengthening, capacity building, policy dialogue and road safety have essentially been completed, with only some training and equipment procurement outstanding for Hunan.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-44930	Effective	350.00	316.89	33.11	0.00
JPN-29709	Closed	0.31	0.07	0.00	0.24

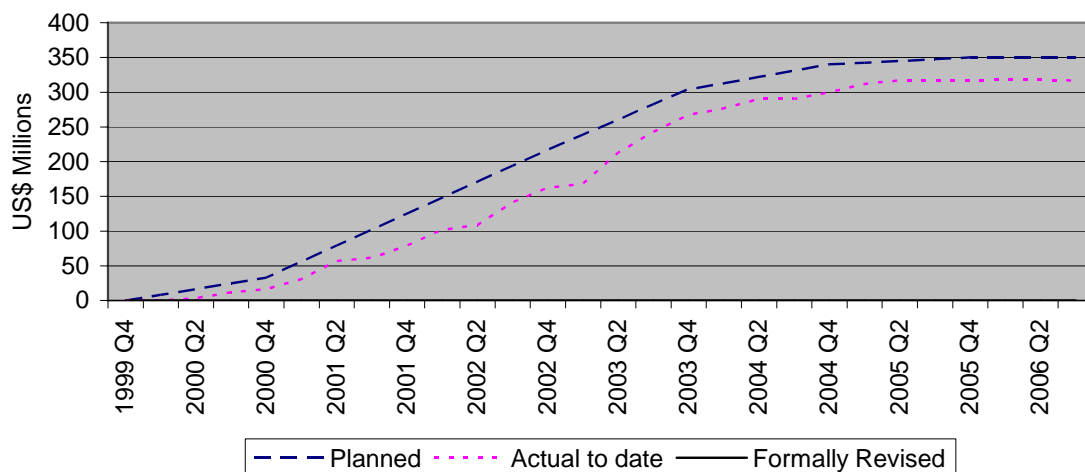

Project Name (ID): Sustainable Forestry Development Project (P064729)
Country: China
Board Approval Date : 04/16/2002
Midterm Review Date : 10/19/2005
Closing Date : 08/31/2009
Loan/Credit/Grant Number : IBRD-46590, JPN-25769
Sector(s): Forestry (100%)
Theme(s): Biodiversity (P), Rural non-farm income generation (P), Participation and civic engagement (P)

Project Development Objectives:

The project's development objectives are to: (a) ensure that viable and participatory managed systems for sustainable use of forest resources and associated biodiversity are developed and adopted in project sites to promote the sustainable development of forest resources and protect natural environments; and (b) foster improved conservation and sustainable management of biodiversity in remaining natural forest areas.


Progress toward achieving development objective(s):

With 65% of the project life elapsed, more than 83% of the planned plantations have been completed in a manner that saw greater participation of communities and the use of more efficient forest management methods. Of the 6,900 villages targeted to benefit from project activities, 4,600 villages have already benefited and are active participants in the management of the new plantations. The thirteen nature reserve management plans have been developed with a high degree of community participation. The plans have been reviewed by the Bank and adopted by the State Forestry Administration. Their implementation is in progress. In addition, 23 community resource management plans have been elaborated to foster the involvement of communities in the conservation of biodiversity and the management of natural forests.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46590	Effective	93.90	57.16	36.74	0.00
JPN-25769	Closed	0.60	0.60	0.00	0.00



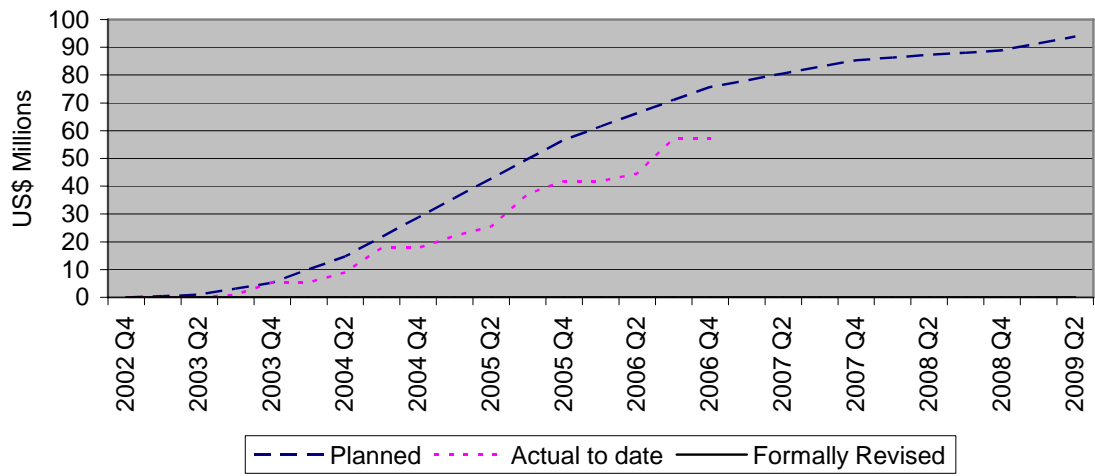

Project Name (ID): CN-Yangtze Dike Strengthening (P064730)

Country: China

Board Approval Date : 06/27/2000

Midterm Review Date : 11/18/2002

Closing Date : 06/30/2008

Loan/Credit/Grant Number : IBRD-45700, JPN-26173

Sector(s): Flood protection (97%), Central government administration (2%), Sub-national government administration (1%)

Theme(s): Land administration and management (P), Water resources management (P), Decentralization (S)

Project Development Objectives:

The objective is to protect property and life against floods along the middle reaches of the Yangtze River.

The Project was restructured during the 2006 Fiscal Year

The project was extended to provide for dike strengthening on two tributary rivers, the Jushui and Fuhuan, to the mid-Yangtze River in Wuhan Municipality, Hubei Province. The extension is consistent with the objectives of the project. The key indicators applying to the main project have been extended to the two tributary rivers covering the expanded project area, and measure: (a) the reduction in flood damage through structural and non-structural measures; and (b) establishment of self-financing institutional systems to operate and maintain flood control facilities.


Progress toward achieving development objective(s):

Further progress has been made in meeting the project's development objectives. Essentially, the dike and river bank protection works under the Changjiang Water Resources Commission, Hunan and Hubei Components are complete. All completed dike works have been functioning for three years and have been serving their designed purpose of retaining floods in the middle reach of the Yangtze River. The Flood Disaster Prevention Center is also operational as a "help desk" for the project areas and China as a whole in the fields of flood management and dike engineering. The preparation of operation, maintenance and surveillance plans are now completed and training in operation and maintenance is being undertaken. Significant improvement in the progress of construction of snail traps in Hubei province occurred during the year. The construction of the very large river model for the middle/lower Yangtze River is now virtually completed.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45700	Effective	210.00	133.33	76.67	0.00
JPN-26173	Closed	0.42	0.42	0.00	0.00



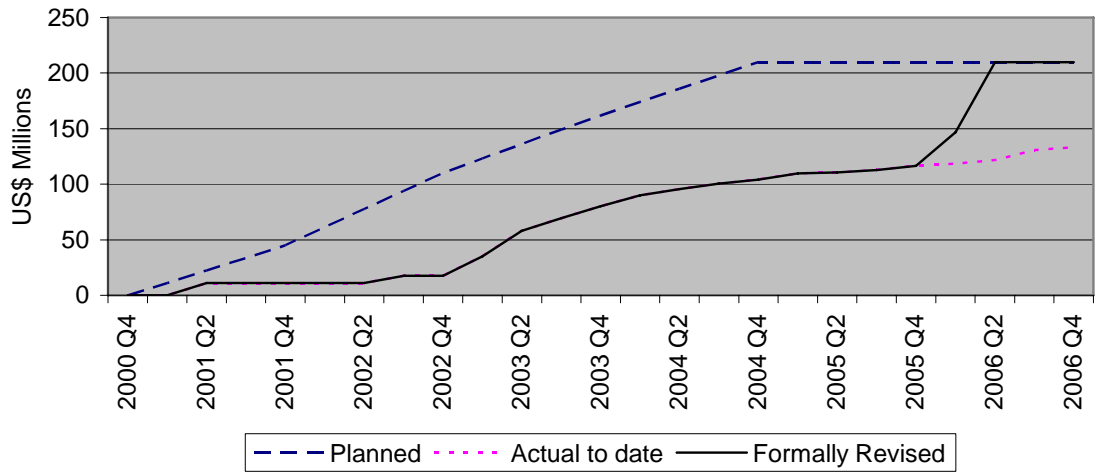

Project Name (ID): Gansu and Xinjiang Pastoral Development Project (P065035)

Country: China

Board Approval Date : 09/09/2003

Closing Date : 06/30/2010

Loan/Credit/Grant Number : IBRD-47180, JPN-26167, JPN-26739, MULT-51488

Sector(s): Animal production (50%), Agricultural marketing and trade (25%),
Agricultural extension and research (25%)

Theme(s): Land administration and management (P), Other environment and natural
resources management (P), Rural markets (P)

Project Development Objectives:

The objectives are to promote sustainable natural resource management and to increase the income of herders and farmers in the project areas. The project will empower farmer and herder households to improve the management of their grassland resources and improve forage and feed production on arable lands. More efficient and quality-focused livestock production will increase the farmers' and herders' incomes and generate a marketable surplus to improve living standards.

The global environment objective of the project is to maintain and nurture natural grassland ecosystems.

Progress toward achieving development objective(s):


The overall progress continues to be slower than planned, mainly because of continued difficulties in adequately implementing the training and applied research components. Training still fails to empower beneficiary households to manage the investments provided, and the project's impact will be severely limited unless they receive simple and relevant training.

The management information system is in place and is being used to facilitate project management, share information and generate quarterly reports. Most of the project counties are now connected to the system via broadband.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47180	Effective	66.27	24.35	41.92	0.00
JPN-26167	Closed	0.49	0.48	0.00	0.00
JPN-26739	Closed	0.51	0.46	0.00	0.04
MULT-51488	Closed	0.20	0.20	0.00	0.00



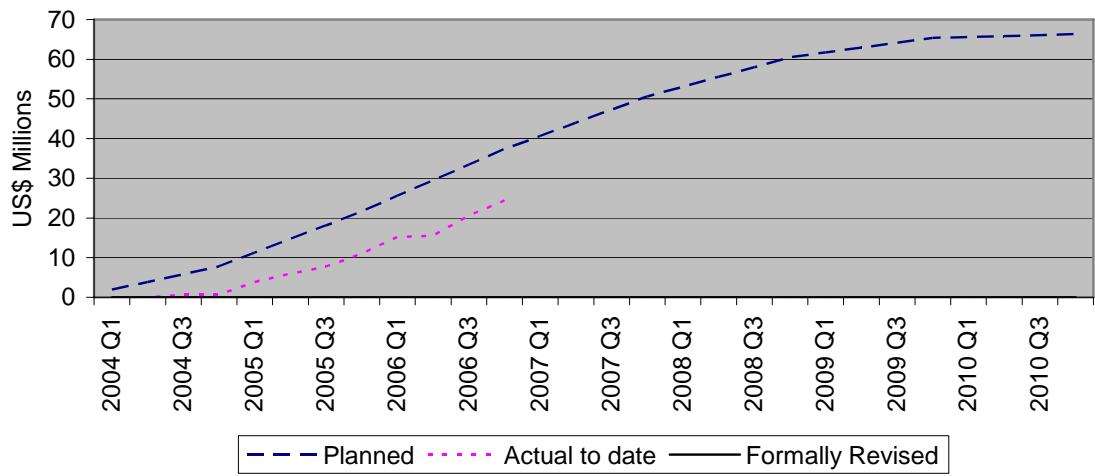

Project Name (ID): Jiangxi Integrated Agricultural Modernization Project (P065463)

Country: China

Board Approval Date : 11/20/2003

Closing Date : 06/30/2010

Loan/Credit/Grant Number : IBRD-47200, JPN-26208

Sector(s): Irrigation and drainage (50%), Agricultural extension and research (15%),
Agricultural marketing and trade (15%), Animal production (10%), Crops (10%)

Theme(s): Rural services and infrastructure (P), Rural markets (P), Other rural
development (P)

Project Development Objectives:

The project's development objective is to improve the livelihoods of rural households in project counties in Jiangxi Province through the establishment of integrated, economically and environmentally sustainable, and market-driven agricultural production systems focusing on productivity and agricultural output of high quality and value. Improved livelihoods are defined as increased income, reduced risks, increased employment (in particular of women), and improved access to irrigation and drainage, technology, information, training and markets.


Progress toward achieving development objective(s):

The adjustment process for the selection of project counties has been completed but the implementation of the project continues to be slow. Every component is significantly behind schedule. The slow implementation progress clearly puts achievement of the project development objective at risk. The main issue is related to the slow (but accelerating) implementation of the irrigation and drainage works. Agricultural activities cannot take place before the irrigation works are in place.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47200	Effective	100.00	10.67	89.33	0.00
JPN-26208	Closed	0.50	0.50	0.00	0.00



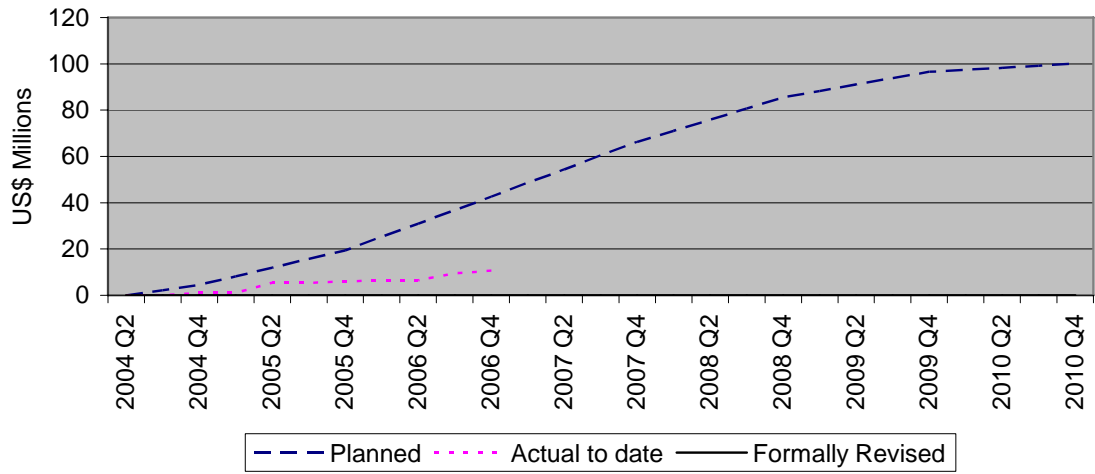

Project Name (ID): Zhejiang Urban Environment Project (P066955)

Country: China

Board Approval Date : 01/29/2004

Closing Date : 06/30/2010

Loan/Credit/Grant Number : IBRD-47240, JPN-26241, JPN-26849

Sector(s): Sewerage (35%), Roads and highways (25%), Other social services (25%), Solid waste management (10%), Water supply (5%)

Theme(s): Municipal governance and institution building (P), Pollution management and environmental health (P), Access to urban services and housing (P), Infrastructure services for private sector development (S), Other urban development (S)

Project Development Objectives:


To enhance the efficiency and equity of waste management in Ningbo (wastewater) and Hangzhou (solid waste) municipalities and the redevelopment of the historic inner city of Shaoxing and Cicheng.

Progress toward achieving development objective(s):

Construction geared toward enhancing the efficiency of waste management in Ningbo and Hangzhou are progressing well. The redevelopment of Shaoxing and Cicheng is moving ahead if somewhat slowly. Technical assistance for institutional strengthening and training, mobilized last year and this year, should accelerate progress on related matters. With some cost savings identified, additional investments to enhance achievement of objectives may be possible.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47240	Effective	133.00	24.41	108.59	0.00
JPN-26241	Closed	0.50	0.50	0.00	0.00
JPN-26849	Closed	0.79	0.79	0.00	0.00

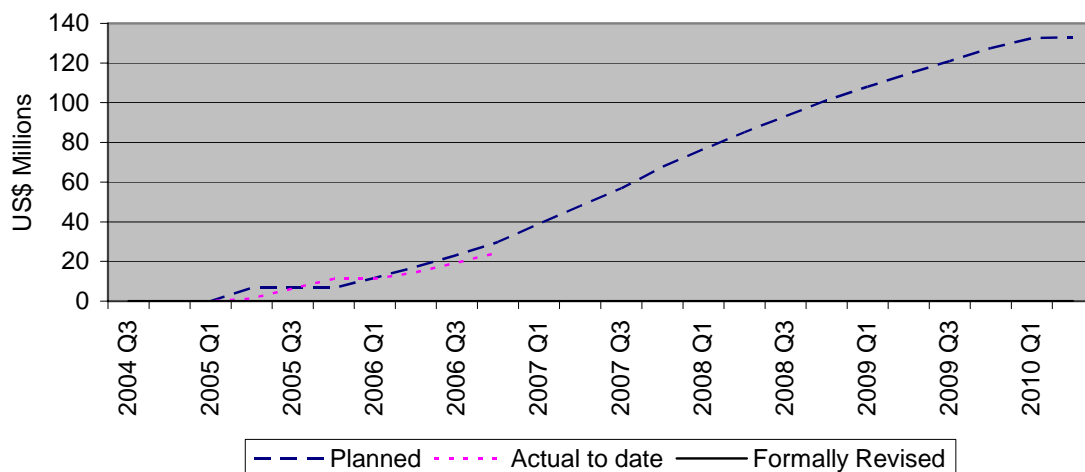

Project Name (ID): Energy Conservation Project, Phase II (P067337)

Country: China

Board Approval Date : 10/24/2002

Midterm Review Date : 05/30/2006

Closing Date : 06/30/2010

Loan/Credit/Grant Number : MULT-51678

Sector(s): District heating and energy efficiency services (91%), Non-compulsory pensions, insurance and contractual savings (7%), Central government administration (2%)

Theme(s): Climate change (P), Pollution management and environmental health (P), Other financial and private sector development (S)

Project Development Objectives:

To expand domestic investment in energy efficiency projects through the aggressive development of China's nascent Energy Management Company (EMC) industry, thereby achieving large-scale energy efficiency improvements and associated reductions in the growth of carbon dioxide emissions and other pollutants.


Progress toward achieving development objective(s):

The project has been achieving good results on its development objectives to foster energy savings through the development of China's nascent energy performance contracting industry. The number of Energy Management Companies (EMCs) operating in China has been growing rapidly during 2004-2005. Energy efficiency investments using energy performance contracting also expanded substantially. Implementation of the EMC service component by EMCA has been fully satisfactory. Implementation of the project management and monitoring component also has been satisfactory.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-51678	Effective	26.00	17.73	8.27	0.00



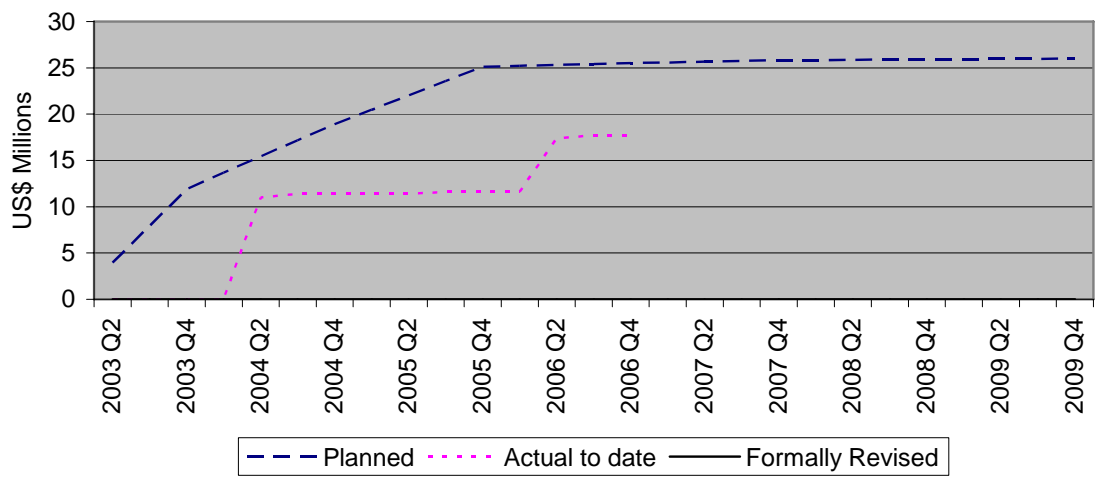

Project Name (ID): Renewable Energy Scale-up Program (CRESP) (P067828)

Country: China

Board Approval Date : 06/16/2005

Closing Date : 09/30/2010

Loan/Credit/Grant Number : IBRD-47920, JPN-26384

Sector(s): Renewable energy (100%)

Theme(s): Environmental policies and institutions (P), Climate change (P), Infrastructure services for private sector development (P), Rural services and infrastructure (S)

Project Development Objectives:


To enable commercial renewable electricity suppliers to provide energy to the electricity market efficiently, cost-effectively, and on a large scale.

Progress toward achieving development objective(s):

The project was approved on June 16, 2005 and became effective on November 30, 2005. Procurement under the Pingtan wind farm sub-component is well advanced, and a contract is now under finalization for the supply and installation of the wind turbines. The project sponsor for the Jiangsu site has informed the Bank of its intention to change the project site, and the new site is now under appraisal. Procurement is under way. The Project Management Office for implementation of the TA component is now established and has finalized the program of work. Consultant selection is now under way for the first key tasks, including the main policy development and technology improvement activities.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47920	Effective	87.00	0.44	86.57	0.00
JPN-26384	Closed	0.46	0.46	0.00	0.00

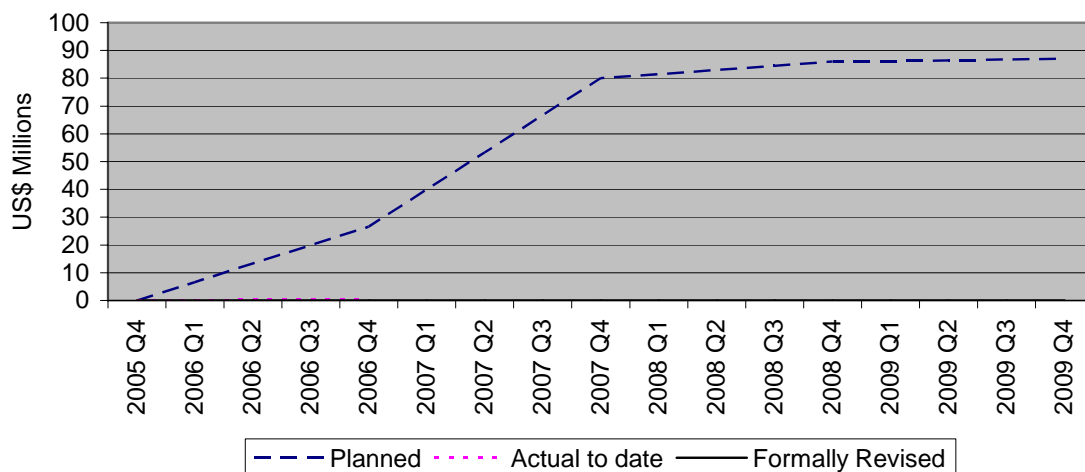

Project Name (ID): Hubei Hydropower Development in Poor Areas Project (P068049)

Country: China

Board Approval Date : 06/25/2002

Closing Date : 12/31/2008

Loan/Credit/Grant Number : IBRD-46660, JPN-26234

Sector(s): Power (97%), Other social services (3%)

Theme(s): Infrastructure services for private sector development (P), Pollution management and environmental health (P), Rural services and infrastructure (P), Poverty strategy, analysis, and monitoring (P), Other social development (S)

Project Development Objectives:

To (a) facilitate economic growth by expanding electric power generation capacity; (b) enhance the efficiency of the electricity sector; and (c) contribute to poverty alleviation efforts in poor communities


Progress toward achieving development objective(s):

Project implementation is in smooth progress. Dongping and Songshuling have successfully commissioned the targeted renewable energy generation capacity. Although the other two sub-projects will have delayed commissioning of units in several months, it is likely that the projects will deliver more than targeted renewable energy generation capacity by the end of 2006. Project companies, including the one for the new component, were established under the Chinese Company Law and are functioning properly in project financing, implementation. All relevant legal arrangements have been completed. Capacity building program for future plant operation are in progress. County Governments have committed 20% of future fiscal revenues from the project be earmarked for contribution of poverty alleviation funds, and Bank financed TA on poverty alleviation planning was completed satisfactorily.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46660	Effective	105.00	78.16	26.84	0.00
JPN-26234	Closed	0.66	0.66	0.00	0.00



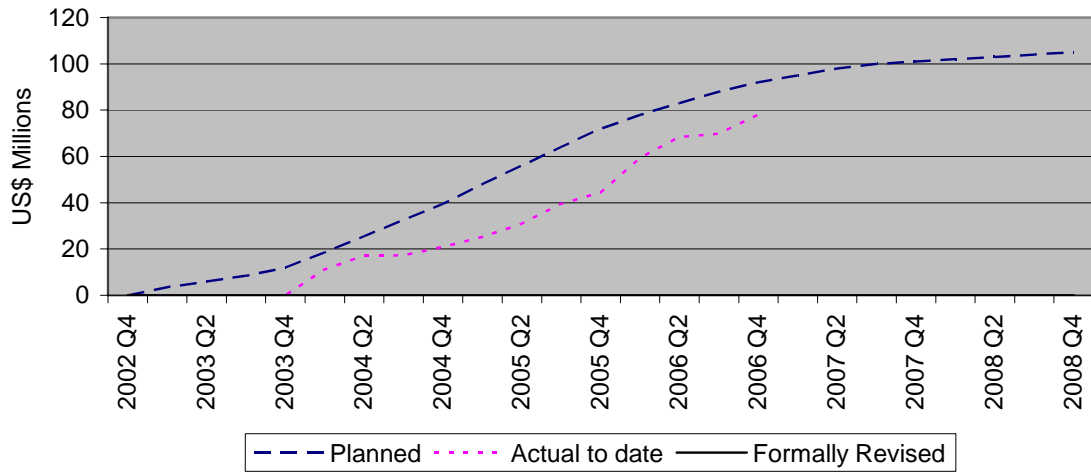

Project Name (ID): Yixing Pumped Storage Project (P068058)

Country: China

Board Approval Date : 03/20/2003

Closing Date : 12/31/2009

Loan/Credit/Grant Number : IBRD-46860, JPN-26238

Sector(s): Power (97%), Sub-national government administration (3%)

Theme(s): Infrastructure services for private sector development (P), Regulation and competition policy (P)

Project Development Objectives:

The proposed project is to increase the overall efficiency of the power sector in Jiangsu Province in two ways: (a) through the design and implementation of a far-reaching restructuring of the sector to further competition at the generation level and to provide large consumers access to generators; (b) through the construction of a pumped storage plant and associated transmission in Yixing to ease acute peaking problems and improve generation mix that would create the conditions for more flexible dispatch and improved supply reliability, an essential requirement for well-functioning competitive markets.


Progress toward achieving development objective(s):

The East China Yixing Pumped Storage Power Plant (EYESPC) continues to make satisfactory progress. The overall environmental performance has also achieved highly satisfactory results. The procurement and construction of the pumped storage power plant are being implemented according to plan. These activities would significantly strengthen the EYESPC's capacity to operate in a market oriented environment and advance its goal of becoming a world class power company with high performance standards.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46860	Effective	145.00	31.82	113.18	0.00
JPN-26238	Closed	0.48	0.48	0.00	0.01



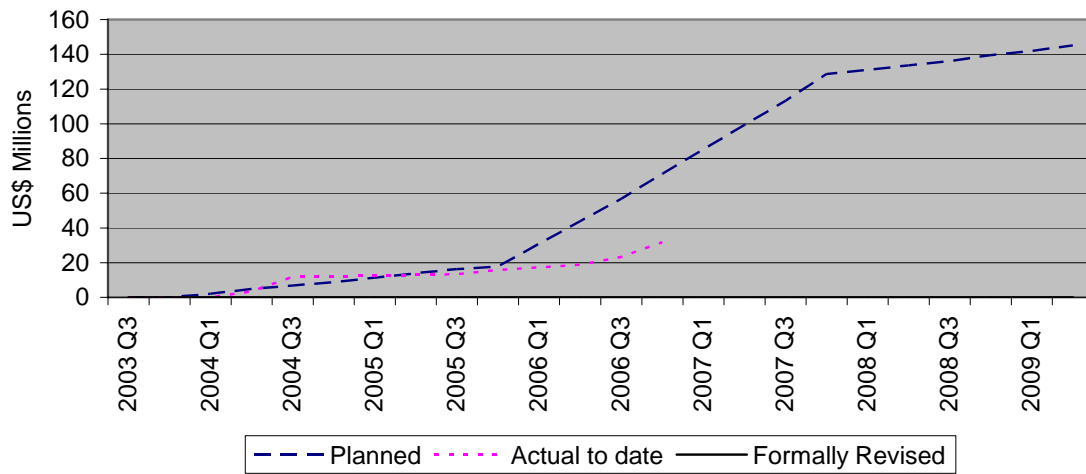

Project Name (ID): Inner Mongolia Highway and Trade Corridor (P068752)

Country: China

Board Approval Date : 02/15/2005

Closing Date : 06/30/2010

Loan/Credit/Grant Number : IBRD-47650

Sector(s): Roads and highways (99%), Sub-national government administration (1%)

Theme(s): Trade facilitation and market access (P), Administrative and civil service reform (S)

Project Development Objectives:


The main objective of the project is to sustain and promote the development of cross-border trade between China on one hand and Russia and Mongolia on the other by improving transport infrastructure and logistics. These improvements, in turn, will lower transport costs, increase income from external trade, and raise incomes in Inner Mongolia, the country's third-largest province and one of the poorest provinces of the western region.

Progress toward achieving development objective(s):

Effectiveness declared on June 21, 2005. The project is on track to meet its objectives. Construction of both the highway and border roads for trade is progressing well with the highway scheduled to open in May 2008. The quality of construction and safeguards compliance are good. There is scope for improvement on project management issues (work programming, variation orders, progress and monitoring reports, etc.). Progress of the Institutional Strengthening and Training component are satisfactory.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47650	Effective	100.00	12.49	87.51	0.00

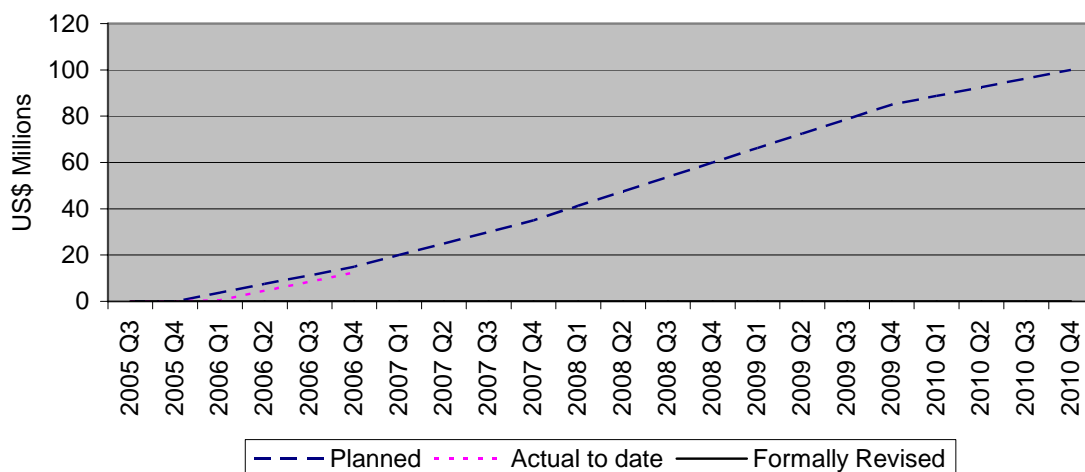

Project Name (ID): Wuhan Urban Transport Project (P069852)

Country: China

Board Approval Date : 03/09/2004

Midterm Review Date : 01/08/2007

Closing Date : 06/30/2009

Loan/Credit/Grant Number : IBRD-47270, JPN-26239

Sector(s): General transportation (96%), Sub-national government administration (4%)

Theme(s): Access to urban services and housing (P), Other urban development (P), Municipal governance and institution building (S), Pollution management and environmental health (S), Non-communicable diseases and injury (S)

Project Development Objectives:


To promote development of an integrated, efficient, and sustainable transport system for the rapid, safe and convenient movement of people and goods in Wuhan.

Progress toward achieving development objective(s):

Progress toward achieving the objectives is good. Wuhan is making good progress with implementation of investments in road infrastructure, the formulation of transport strategy, and with public transport reform. Although disbursements are lower than forecast, one-third of the infrastructure contracts by value (over \$100 million) are in progress. Much of the work envisaged at appraisal on the further development of the transport strategy for the city has been completed, and the process of hiring consultants to advise on public transport reform is underway.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47270	Effective	200.00	35.62	163.38	1.00
JPN-26239	Closed	0.76	0.73	0.00	0.02

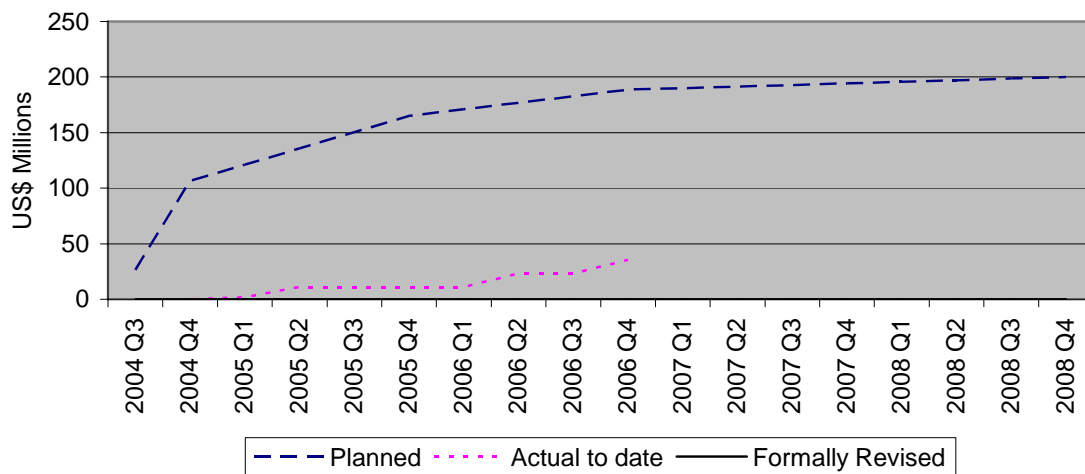

Project Name (ID): Agricultural Technology Transfer Project (P069862)

Country: China

Board Approval Date : 04/28/2005

Midterm Review Date : 10/01/2007

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-47730, JPN-26377

Sector(s): Agricultural extension and research (45%), Agricultural marketing and trade (25%), Agro-industry (20%), Information technology (5%), Other social services (5%)

Theme(s): Rural policies and institutions (P), Rural services and infrastructure (P), Other rural development (S), Export development and competitiveness (S)

Project Development Objectives:

The objective of the project is to develop and test innovative models for agricultural technology transfer and application aimed to generate additional farm income in high-value markets with a potential for scaling up. In this way, the project aims to give poor farmers the opportunity to participate in high-value agricultural markets both domestically and internationally.


Progress toward achieving development objective(s):

The loan was signed on June 7, 2005 and the project launch workshop was held July 25-28, 2005. The project has made a good start toward meeting its development objectives. Most of the implementation activities have been focused on establishing management systems, procurement activities and training. At least 70 percent of the approximately 120 sub-projects have started implementation. Monitoring baselines have been established for each sub-project.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47730	Effective	100.00	7.24	92.76	0.00
JPN-26377	Closed	0.26	0.00	0.00	0.26



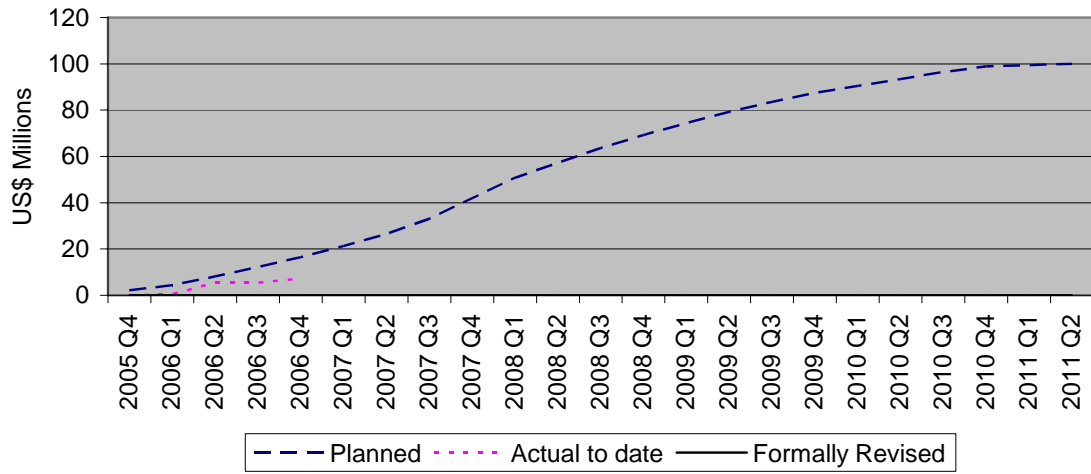

Project Name (ID): Shanghai Urban Environment Project (P070191)

Country: China

Board Approval Date : 06/17/2003

Closing Date : 03/31/2009

Loan/Credit/Grant Number : IBRD-47050, JPN-26236

Sector(s): Sewerage (73%), Solid waste management (20%), Sub-national government administration (7%)

Theme(s): Other urban development (P), Pollution management and environmental health (P), Access to urban services and housing (P), Environmental policies and institutions (P)

Project Development Objectives:

(a) To put in place some of the underpinnings and enabling conditions to pursue an integrated, metropolitan-wide approach for managing the urban environment; (b) to install, in both the city center and districts, facilities already known to be high priority to achieve metropolitan-wide environmental objectives.


Progress toward achieving development objective(s):

Sound progress with physical implementation and policy thrusts is being achieved. For objective (a), the District Financing Vehicle is now well established and represents an innovative approach to metropolitan management. The Upper Huangpu Study has been completed and is providing an enhanced basis for planning environmental improvements. For objective (b), priority investments are being implemented well, although somewhat behind schedule. Improvements include sewerage systems, a new wastewater treatment plant, and a large sanitary landfill (now complete) serving some 8 million people.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47050	Effective	200.00	54.12	145.88	0.00
JPN-26236	Closed	0.99	0.99	0.00	0.00



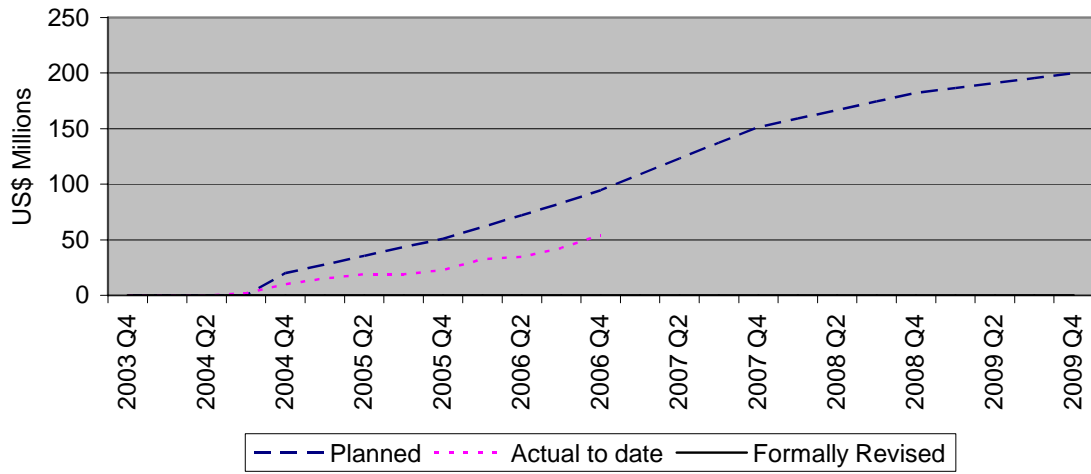

Project Name (ID): Hubei Xiaogan-Xiangfan Highway Project (P070441)

Country: China

Board Approval Date : 09/17/2002

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-46770

Sector(s): Roads and highways (90%), Sub-national government administration (10%)

Theme(s): Infrastructure services for private sector development (P), Municipal governance and institution building (S), Rural services and infrastructure (S)

Project Development Objectives:


To provide a more effective, safe and efficiently managed transport infrastructure to sustain and support socio-economic development, trade, and regional integration in Hubei province and to improve transport links to lagging western regions.

Progress toward achieving development objective(s):

The project is on track to meet its development objectives. The expressway opened in September 2005 and the quality is good. Issues remain on the interconnecting roads which the team is actively addressing. The institutional development and road sector management activities have made good progress and have had some useful results.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46770	Effective	250.00	208.29	41.71	0.00

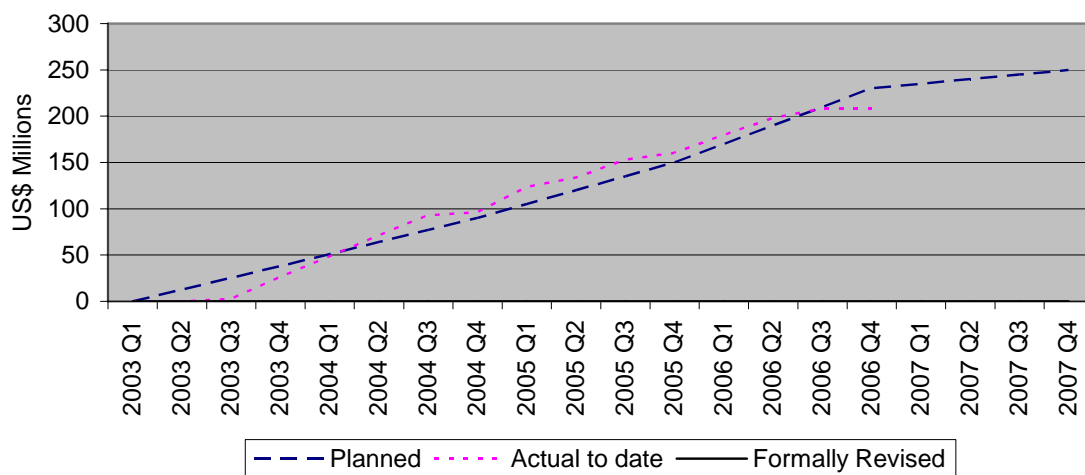

Project Name (ID): CN-Inner Mongolia Hwy Project (P070459)

Country: China

Board Approval Date : 06/06/2002

Closing Date : 03/31/2008

Loan/Credit/Grant Number : IBRD-46630

Sector(s): Roads and highways (99%), Sub-national government administration (1%)

Theme(s): Infrastructure services for private sector development (P), Rural services and infrastructure (P), Regional integration (P), Trade facilitation and market access (S)

Project Development Objectives:


The project aims to improve the efficiency, safety, and cost-effectiveness of the transport infrastructure to support the social and economic development of the Inner Mongolia Autonomous Region, and to improve accessibility to its poorer areas thus reducing social and economic disparity within the region.

Progress toward achieving development objective(s):

The project is on track to meet its objectives. Construction of the expressway, highway and road safety improvements is progressing well with the expressway opened in September 2006. The quality of construction and safeguards compliance are good. There is scope for improvement on project management issues (work programming, variation orders, progress and monitoring reports, etc.). Progress of the Institutional Strengthening and Training component are satisfactory.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46630	Effective	100.00	73.18	26.82	0.00

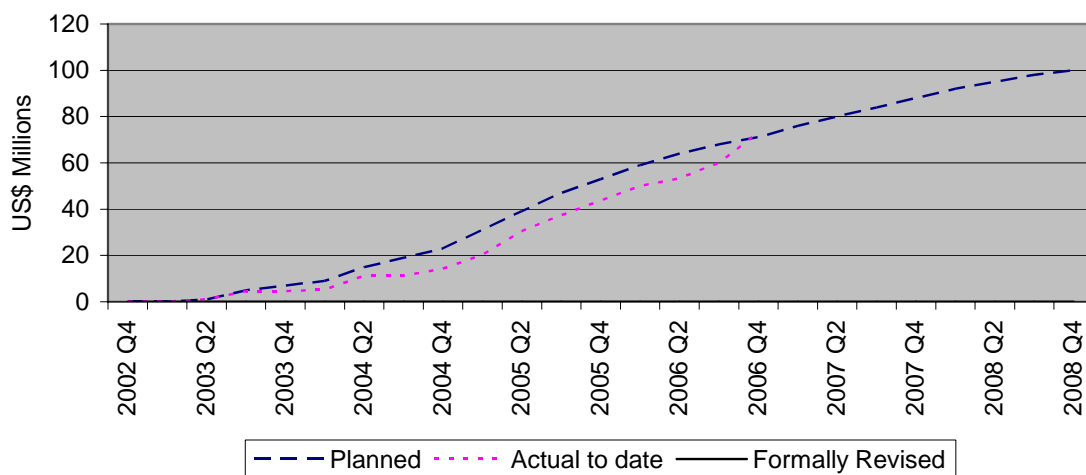

Project Name (ID): Fuzhou Nantai Island Peri-Urban Development Project (P070519)

Country: China

Board Approval Date : 12/15/2005

Midterm Review Date : 08/15/2008

Closing Date : 06/30/2011

Loan/Credit/Grant Number : IBRD-48120

Sector(s): Roads and highways (87%), General transportation (10%), Sub-national government administration (3%)

Theme(s): Other urban development (P), Environmental policies and institutions (S), Pollution management and environmental health (S), Non-communicable diseases and injury (S)

Project Development Objectives:


The objective of the project is to support sustainable peri-urban development in Fuzhou (as it expands to include Nantai Island) by providing strategic transport infrastructure and by strengthening the city's decision support system on land development and management.

Progress toward achieving development objective(s):

The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48120	Not Effective	100.00	0.00	100.00	0.00

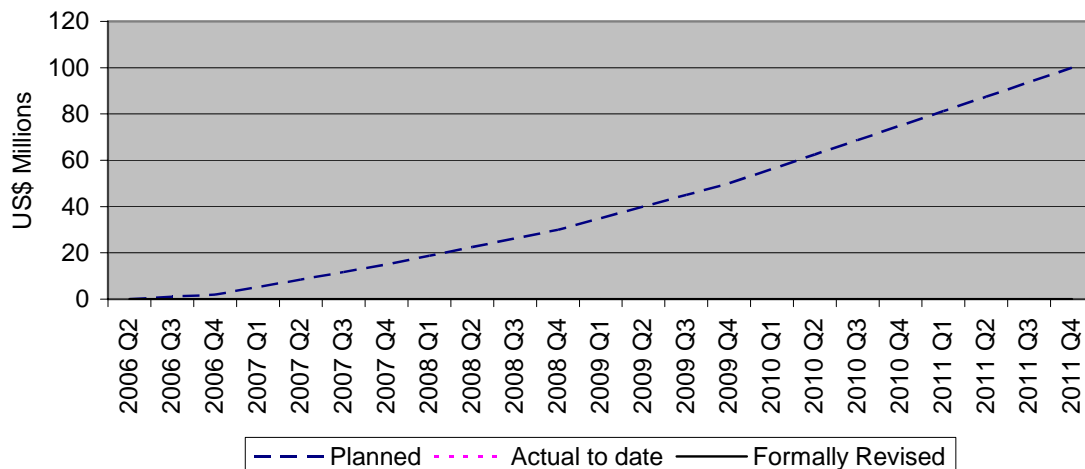

Project Name (ID): POOR RURAL COMMUNITIES DEVELOPMENT PROJECT (P071094)

Country: China

Board Approval Date : 06/21/2005

Midterm Review Date : 12/17/2008

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-73100, JPN-26424, JPN-54747

Sector(s): General agriculture, fishing and forestry (65%), Roads and highways (13%), Sub-national government administration (10%), General water, sanitation and flood protection (6%), General education (6%)

Theme(s): Participation and civic engagement (P), Rural services and infrastructure (P), Other rural development (P), Indigenous peoples (P), Education for all (S)

Project Development Objectives:


The development objective is to improve the security of livelihoods and to achieve sustained participation of the poorest rural people in project design, implementation, and monitoring and evaluation.

Progress toward achieving development objective(s):

Initial implementation has made a good start. The positive impact of the successful rollout of the participatory approach is evident in each of the three project provinces, and project plans have been kept flexible enough to accommodate beneficiaries' changing demands.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-73100	Effective	100.00	2.24	97.76	0.00
JPN-26424	Closed	0.54	0.54	0.00	0.00
JPN-54747	Effective	1.93	0.19	1.74	0.00

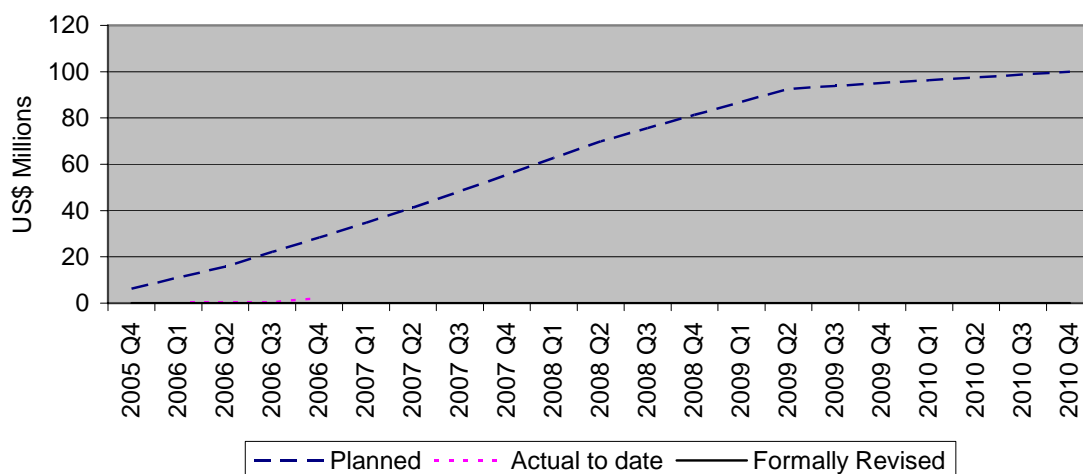

Project Name (ID): Tuberculosis Control (P071147)

Country: China

Board Approval Date : 03/21/2002

Midterm Review Date : 07/17/2006

Closing Date : 03/15/2010

Loan/Credit/Grant Number : IBRD-71070, JPN-26428

Sector(s): Health (93%), Sub-national government administration (7%)

Theme(s): Other communicable diseases (P), Child Health (S), Rural services and infrastructure (S)

Project Development Objectives:


The project's main development objectives are to achieve 70% case detection rate for smear positive TB cases and 85% cure rate.

Progress toward achieving development objective(s):

By 2004, 12 of 16 project provinces reached their targets for case finding, three achieved 80-100% of target, and only 1 performed below standard with 49%. Notwithstanding these reported achievements, there are indications that there are still many undiagnosed tuberculosis cases, and that the targets for case detection may in fact be set too low. Second, there are large variations in treatment success rates among the cities/prefectures and indications that the real cure rate may not be as high as reported. Excessive payments for additional diagnostic tests and "protective" treatment are unnecessarily increasing the cost of the program and imposing a financial burden on the poor.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-71070	Effective	104.00	46.57	57.43	0.00
JPN-26428	Closed	0.42	0.42	0.00	0.00

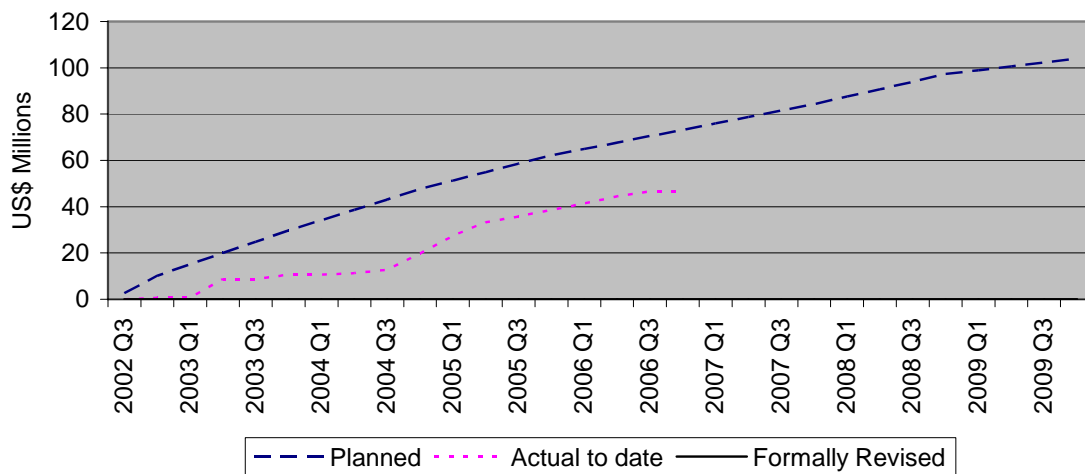

Project Name (ID): CN-GEF-Heat Reform & Bldg Energy Efficiency (P072721)

Country: China

Board Approval Date : 03/17/2005

Midterm Review Date : 05/30/2008

Closing Date : 12/31/2011

Loan/Credit/Grant Number : MULT-51792, MULT-54687

Sector(s): Housing construction (40%), District heating and energy efficiency services (32%), Sub-national government administration (17%), Central government administration (11%)

Theme(s): Climate change (P), Municipal governance and institution building (S)

Project Development Objectives:


To achieve substantial, sustained and growing increases in energy efficiency in urban residential buildings and the heating systems in China's cold climate regions.

Progress toward achieving development objective(s):

The project became effective in September 2005, and implementation has been satisfactory. The Tianjin component is re-focusing efforts on providing well prepared new subproject proposals and technical assistance. Special attention would be paid to the pipeline development for other northern cities to ensure their participation.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-51792	Closed	0.35	0.35	0.00	0.00
MULT-54687	Effective	18.00	1.80	16.20	0.00

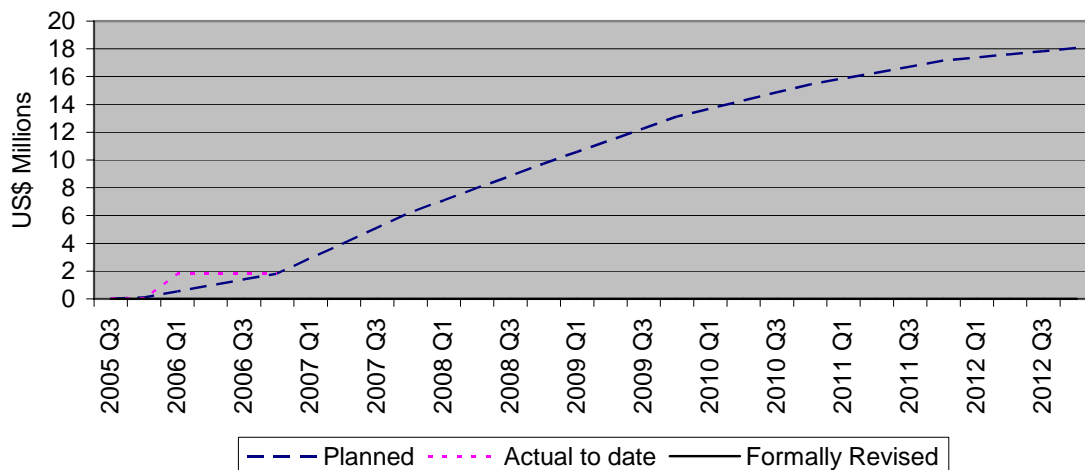

Project Name (ID): CN-Basic Education in Western Areas (P073002)

Country: China

Board Approval Date : 09/09/2003

Midterm Review Date : 10/15/2006

Closing Date : 06/30/2009

Loan/Credit/Grant Number : IBRD-71940, JPN-26772

Sector(s): Primary education (95%), Sub-national government administration (3%), Central government administration (2%)

Theme(s): Education for all (P), Participation and civic engagement (P), Gender (S), Indigenous peoples (S), Rural services and infrastructure (S)

Project Development Objectives:

Project aims toward the improved access to and completion of affordable and quality basic education for poor boys and girls in over a hundred counties in Sichuan, Gansu, Yunnan Provinces, Ningxia Hui and Guangxi Zhuang Autonomous Regions. The project promotes greater community participation in the management of school and provides training to support the implementation of the new national curriculum.


Progress toward achieving development objective(s):

School building program has achieved 80% of the targets creating a safer and more conducive environment for learning. The School Development Planning (SDP) and Participatory Teacher Training (PTT) pilots are producing initial good results. SDP has increased stakeholder participation in school management and planning while PTT helped motivate students and teachers in making a transition toward student-center learning. A policy research program is under implementation including School Mapping, Student Assistance and Rural Education Reform Pilots to explore options to address issues of access and quality. The design of Impact Evaluation is being finalized.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-71940	Effective	100.00	40.80	59.20	0.00
JPN-26772	Closed	0.51	0.51	0.00	0.00



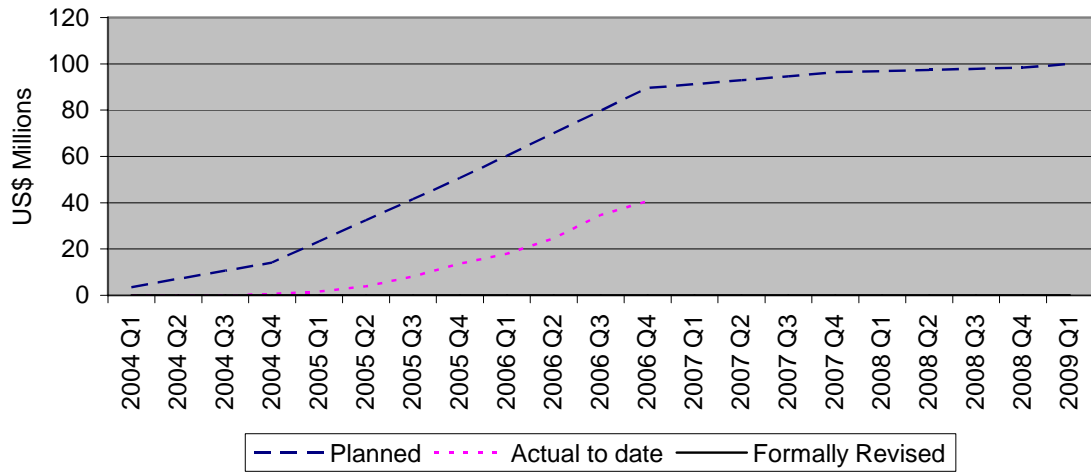

Project Name (ID): Hai Basin Integrated Water and Environment Management Project (P075035)

Country: China

Board Approval Date : 04/15/2004

Midterm Review Date : 01/31/2007

Closing Date : 06/30/2010

Loan/Credit/Grant Number : MULT-51398, MULT-53183

Sector(s): Sewerage (35%), Central government administration (35%), Sub-national government administration (15%), Irrigation and drainage (15%)

Theme(s): Water resources management (P), Pollution management and environmental health (P), Environmental policies and institutions (S)

Project Development Objectives:

The objective is to catalyze an integrated approach to water resource management and pollution control in the Hai Basin in order to improve the Bohai Sea environment. The project will: (a) improve integrated water and environment planning and management in the Hai Basin; (b) support institutional aspects related to effective local, municipal/provincial and basin-wide water and environment planning and management; (c) enhance capacity building in water and environment knowledge management and implementation; and (d) reduce waste water discharges from small cities along the rim of the Bohai Sea.


Progress toward achieving development objective(s):

Progress towards achieving the development objectives has been good. The cooperation between water and environment departments has improved since the beginning of project implementation. The project concepts and approaches are being understood and adopted to produce project outputs, which is improving integrated water and environment management in the Hai River Basin.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-51398	Closed	0.23	0.23	0.00	0.00
MULT-53183	Effective	17.00	3.43	13.57	0.00



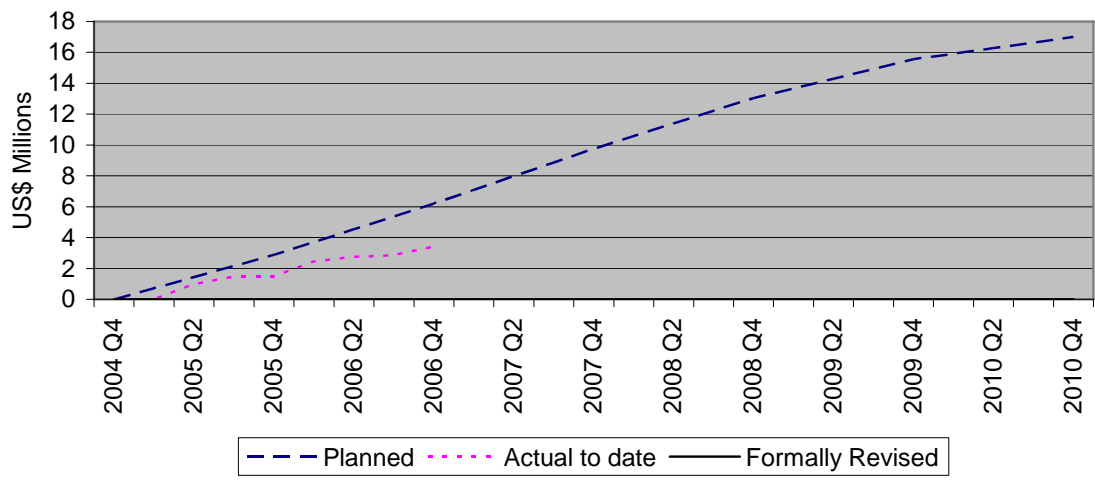

Project Name (ID): Second National Railways Project (Zhe-Gan Line) (P075602)
Country: China
Board Approval Date : 06/24/2004
Closing Date : 01/31/2008
Loan/Credit/Grant Number : IBRD-47460
Sector(s): Railways (99%), Central government administration (1%)
Theme(s): Infrastructure services for private sector development (P), Climate change (S)

Project Development Objectives:


To (a) improve services provided to customers of the railway line between Zhouzhou and Hangzhou; and (b) upgrade the quality of track maintenance on heavily used portions of China Railways' network.

Progress toward achieving development objective(s):

The Loan became effective in January 2005 and excellent progress has been made with the line scheduled to be reopened ahead of schedule in September 2006. Though it is difficult to judge until the railway line is reopened, it is expected that customer service as well as track maintenance should improve in agreement with performance indicators.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47460	Effective	200.00	125.86	73.14	1.00

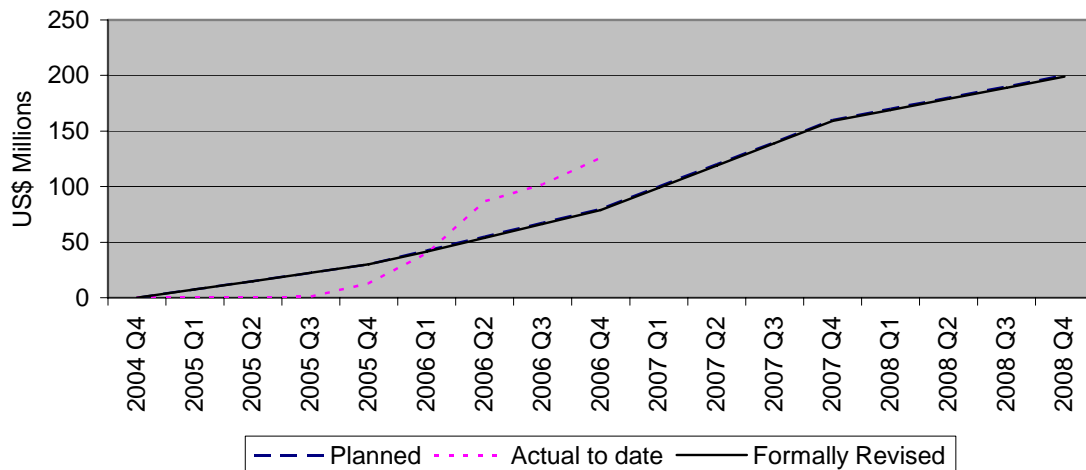

Project Name (ID): Guangdong Pearl River Delta Urban Environment Project (P075728)

Country: China

Board Approval Date : 06/08/2004

Midterm Review Date : 06/06/2007

Closing Date : 12/31/2009

Loan/Credit/Grant Number : IBRD-47420

Sector(s): Sewerage (88%), Solid waste management (7%), Sub-national government administration (5%)

Theme(s): Pollution management and environmental health (P), Other urban development (P), Other human development (S), Other financial and private sector development (S)

Project Development Objectives:

To improve the quality of the environment in key cities in the Pearl River Delta using an integrated regional planning approach to facilitate continued economic and social development.


Progress toward achieving development objective(s):

Overall implementation progress remains good with disbursements ahead of schedule. The biggest component, the Guangzhou wastewater system, is advancing smoothly, with target dates for completion of the two largest wastewater treatment plants (Liede III and Dashadi) set for mid and end-2006 respectively. Capacity strengthening of the new Guangzhou wastewater company will focus on preparing financial projections and improving management systems. A sludge management study has been completed and is being reviewed. A contract has been signed to update the Pearl River Delta wastewater master plan. To encourage water conservation and sustainability, Guangzhou authorities have approved a water tariff increase of 50%. It also has allocated funds to purchase and install water meters for some 1.16 million households. These actions will improve the quality of the environment in the Pearl River delta using an integrated approach.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47420	Effective	128.00	30.92	96.44	0.64



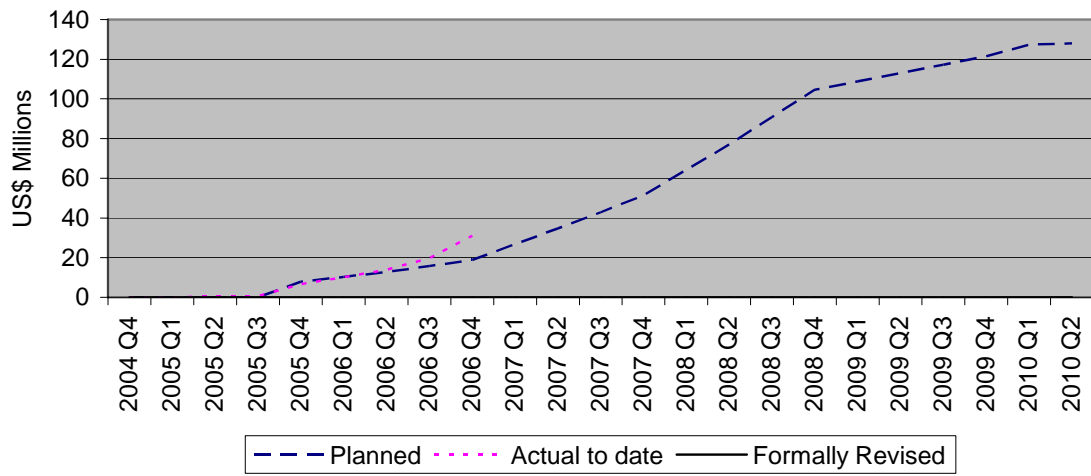

Project Name (ID): Hunan Urban Development Project (P075730)

Country: China

Board Approval Date : 09/16/2004

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-47510, JPN-50626

Sector(s): Flood protection (45%), Sewerage (27%), General transportation (20%), Mining and other extractive (5%), Other social services (3%)

Theme(s): Other urban development (P), Pollution management and environmental health (P), Climate change (S)

Project Development Objectives:


To foster greater integration in the Changsha-Zhuzhou-Xiangtan (CZT) Region of Hunan Province through priority investments addressing specific regional needs in a sustainable manner.

Progress toward achieving development objective(s):

While early implementation of project investments has been slower than expected because of changes in designs and local regulations on resettlement compensation, the majority of these issues have been resolved, and physical construction is progressing. None of these modifications or issues has materially changed the components, so the objectives should be attainable.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47510	Effective	172.00	6.86	165.14	0.00
JPN-50626	Closed	1.27	1.27	0.00	0.00

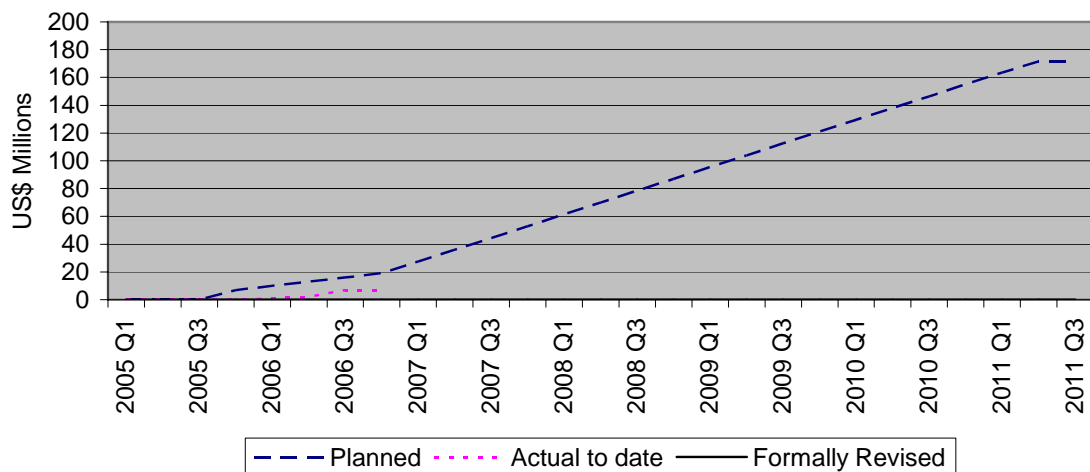

Project Name (ID): Shanghai Urban Environment APL Phase 2 (P075732)

Country: China

Board Approval Date : 07/05/2005

Closing Date : 03/31/2011

Loan/Credit/Grant Number : IBRD-48010

Sector(s): Sewerage (50%), Water supply (20%), Sub-national government administration (20%), Solid waste management (10%)

Theme(s): Pollution management and environmental health (P), Access to urban services and housing (P), Other human development (P), Environmental policies and institutions (S), Municipal finance (S)

Project Development Objectives:


To expand Shanghai's environmental management agenda in the metropolitan area

Progress toward achieving development objective(s):

The project just became effective on March 28, 2006, so it is too early to measure progress against objectives. However, key procurements are underway and implementation of the water component is well advanced under retroactive financing.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48010	Effective	180.00	0.45	179.55	0.00

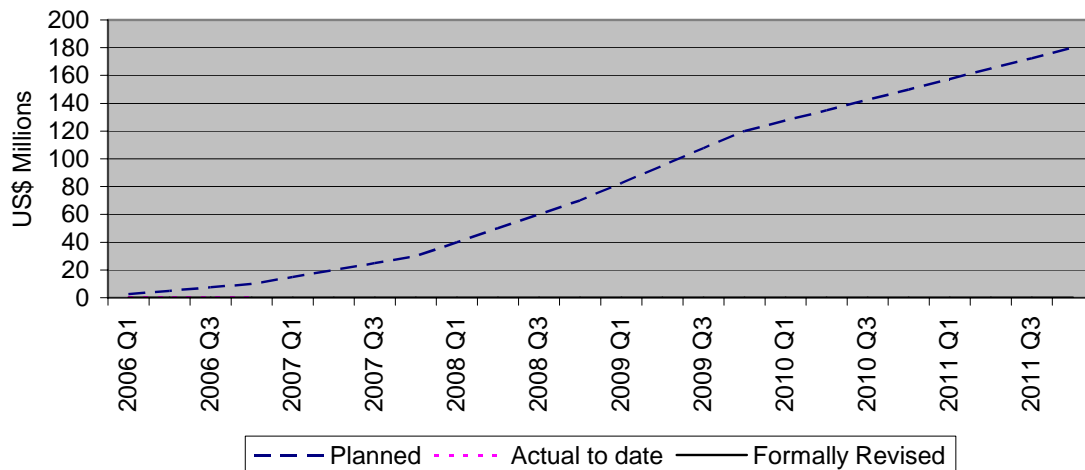

Project Name (ID): Second Anhui Highway Project (P076714)

Country: China

Board Approval Date : 06/24/2003

Midterm Review Date : 09/16/2007

Closing Date : 06/30/2009

Loan/Credit/Grant Number : IBRD-71830

Sector(s): Roads and highways (80%), Sub-national government administration (20%)

Theme(s): Regional integration (P), Rural services and infrastructure (P), Other public sector governance (S), Export development and competitiveness (S)

Project Development Objectives:

The project aims to support the social and economic development of Anhui Province by providing an efficient, safe, and cost-effective highway infrastructure and to improve transport links.


Progress toward achieving development objective(s):

The PDO and intermediate outcome indicators show values in line with those estimated at appraisal. Travel volumes on the existing highways S103 and G205 appear higher than those estimated for end of 2005 as are the travel times on the corridor, providing evidence of increased congestion and likelihood of achieving the PDO once the construction of the TTH will be completed. Travel volumes on the complementary RRIP roads are slightly lower than those reported in the PAD for 2005, but still within reasonable margins. Accidents rates appeared to have been contained as shown by the reduced or similar values compared to those reported in previous reports. They remain higher than those expected for 2005. APCD is actively seeking to address the issue and have moved forward with a proactive program of black-spot improvements, including about 5,200 spots for almost 1,800 kilometers across the province, with its own funds. Further efforts on institutional and policy actions are expected to be assessed and pursued as part of the preparation of the proposed Anhui Road Rehabilitation and Improvement Project.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-71830	Effective	250.00	109.09	140.91	0.00



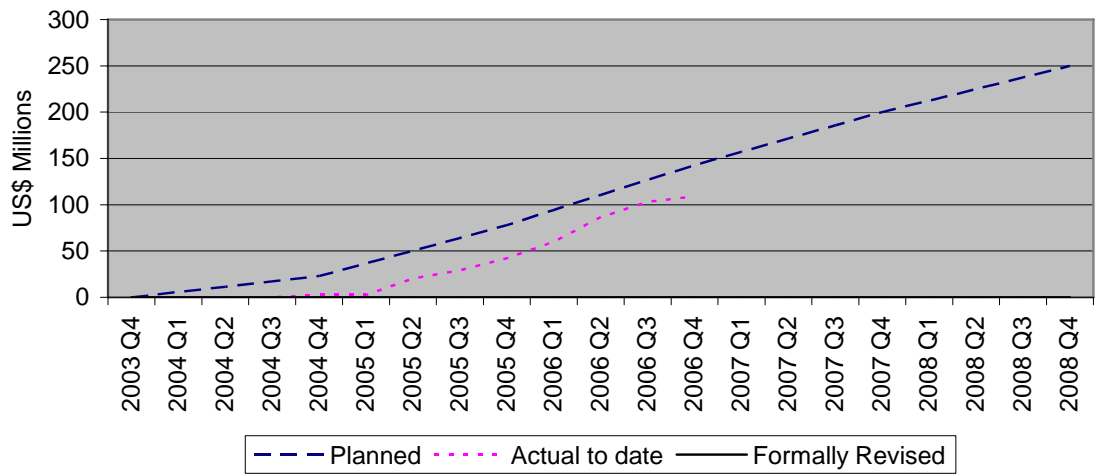

Project Name (ID): Fourth Inland Waterways Project (P077137)

Country: China

Board Approval Date : 03/25/2004

Midterm Review Date : 03/01/2007

Closing Date : 01/31/2010

Loan/Credit/Grant Number : IBRD-47280

Sector(s): Ports, waterways and shipping (65%), Renewable energy (15%), Power (10%), Sub-national government administration (10%)

Theme(s): Infrastructure services for private sector development (P), Water resources management (P), Rural services and infrastructure (S), Climate change (S)

Project Development Objectives:


To assist the Borrower in (1) improve access for poor regions of southern China by upgrading navigation conditions on the region's major east-west river and other waterways feeding traffic into the Pearl River Delta region; and (2) harness water flow in two of these rivers to generate environmentally clean electricity to help meet the growing energy demand in Guangdong and Guangxi.

Progress toward achieving development objective(s):

The Loan became effective in January 2005 and significant progress is being made in civil works though some schedule delays have occurred due to a lengthy procurement process and high water through the construction sites. Government commitment is high and counterpart funding is available.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47280	Effective	91.00	13.41	77.14	0.46

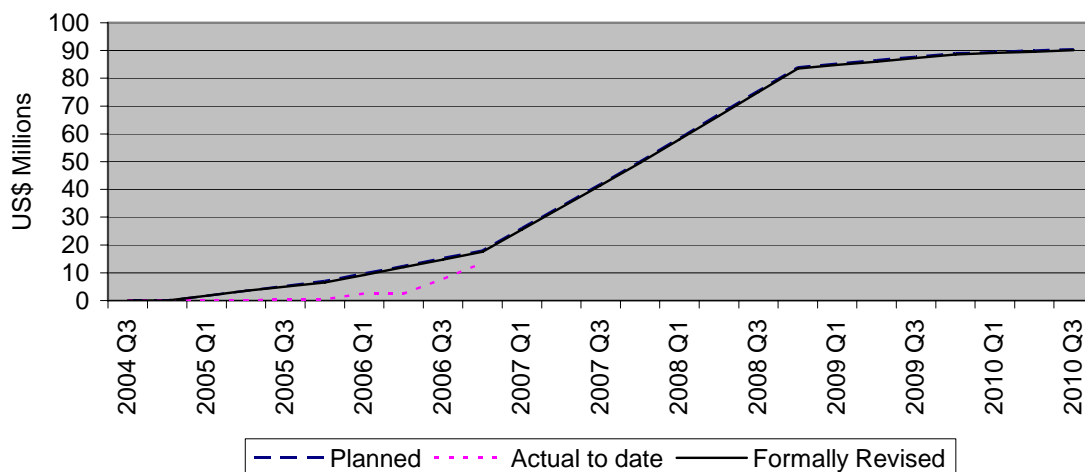

Project Name (ID): Chongqing Small Cities Infrastructure Improvement Project (P081161)

Country: China

Board Approval Date : 06/21/2005

Midterm Review Date : 06/30/2009

Closing Date : 06/30/2012

Loan/Credit/Grant Number : IBRD-47940

Sector(s): Water supply (35%), Roads and highways (33%), Flood protection (21%), Sanitation (8%), Sub-national government administration (3%)

Theme(s): Access to urban services and housing (P), Other urban development (P), Other human development (S), Pollution management and environmental health (S), Natural disaster management (S)

Project Development Objectives:


To support emerging small cities to improve the efficiency and effectiveness of infrastructure service delivery, to accommodate the rapid urban growth

Progress toward achieving development objective(s):

Although still early, implementation is off to a good start. The design and review process for the 13 subcomponents is well advanced, with nine under procurement, three under construction and one on hold. International consultants have been retained to supervise construction. Capacity building and training activities have also started. Together, the works program and capacity building efforts will support Chongqing's small cities to improve infrastructure efficiency and effectiveness.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47940	Effective	180.00	2.90	177.10	0.00

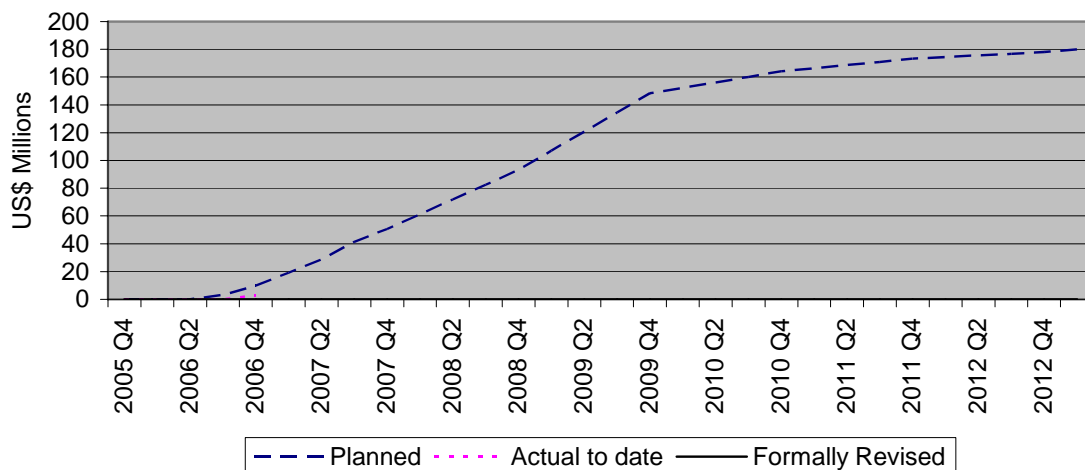

Project Name (ID): Changjiang/Pearl River Watershed Rehabilitation Project (P081255)

Country: China

Board Approval Date : 06/27/2006

Closing Date : 06/30/2012

Loan/Credit/Grant Number : IBRD-48320, JPN-52802

Sector(s): Forestry (23%), Crops (22%), Irrigation and drainage (20%), Animal production (20%), Flood protection (15%)

Theme(s): Other environment and natural resources management (P), Water resources management (S), Rural services and infrastructure (S), Land administration and management (S), Other rural development (S)

Project Development Objectives:

The project's development objective is to assist the Borrower to improve farmer livelihoods and protect the environment in poor and highly degraded watersheds of the Changjiang and Pearl River Basins by promoting an integrated and replicable model of sustainable rural development.

Progress toward achieving development objective(s):

The Loan was approved on June 27, 2006, the formal project launch is expected at the end of September, 2006.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48320	Not Effective	100.00	0.00	100.00	0.00
JPN-52802	Closed	0.50	0.50	0.00	0.00



Project Name (ID): LIUZHOU ENVIRONMENT MANAGEMENT PROJECT (P081346)

Country: China

Board Approval Date : 05/24/2005

Midterm Review Date : 01/31/2008

Closing Date : 06/30/2011

Loan/Credit/Grant Number : IBRD-47810

Sector(s): Sewerage (88%), Sanitation (5%), Solid waste management (5%), Sub-national government administration (2%)

Theme(s): Pollution management and environmental health (P), Access to urban services and housing (P), Municipal governance and institution building (S)

Project Development Objectives:


To sustainably improve the environmental conditions in Liuzhou through improved wastewater treatment, sanitation control and solid waste management

Progress toward achieving development objective(s):

Effectiveness was declared on November 9, 2005. Consultants were hired to assist the Project Management Office and other agencies in implementing the municipal sanitation, solid waste management and institutional development components. Recent achievements include selection of 11 solid waste collection points; selection of sites for 18 public toilets and approval of land use plans for 16 of them; and revision of the financial model for the Liuzhou Municipal Wastewater Treatment Company. These preliminary actions will ultimately contribute to improving the city's environment in a sustainable manner.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47810	Effective	100.00	3.50	96.50	0.00

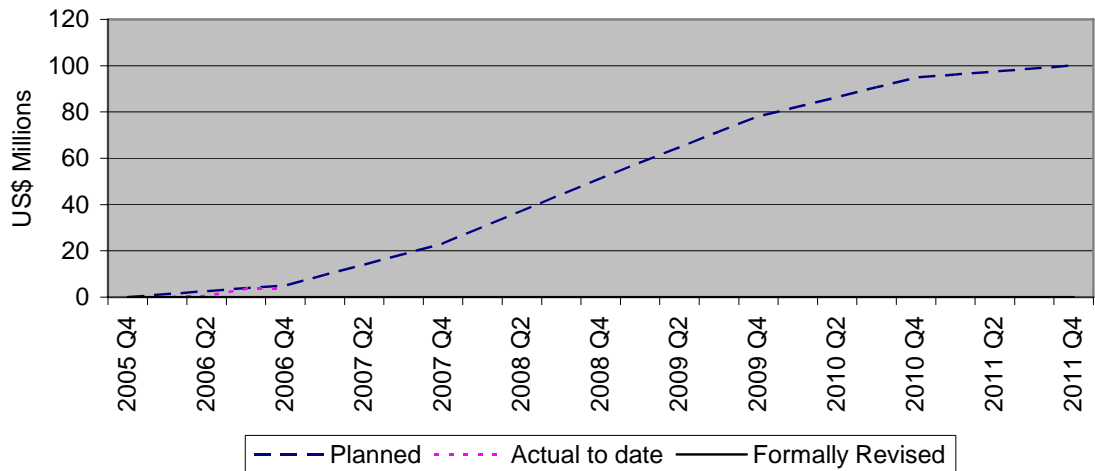

Project Name (ID): HENAN TOWNS WATER SUPPLY AND SANITATION PROJECT (P081348)

Country: China

Board Approval Date : 06/27/2006

Closing Date : 06/30/2013

Loan/Credit/Grant Number : IBRD-48290

Sector(s): Water supply (77%), Sanitation (9%), Sewerage (9%), Sub-national government administration (5%)

Theme(s): Access to urban services and housing (P), Pollution management and environmental health (P), Municipal governance and institution building (S), Regulation and competition policy (S), Water resources management (S)

Project Development Objectives:


To help create or expand water supply and wastewater management services and improve the planning, regulatory, and operational capacity of sector institutions.

Progress toward achieving development objective(s):

The project was just approved on June 27, 2006.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48290	Not Effective	150.00	0.00	150.00	0.00

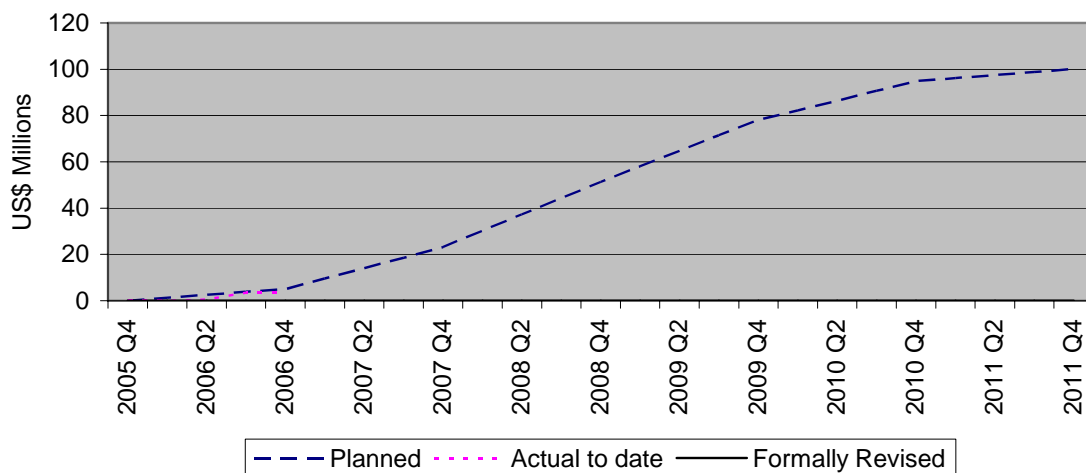

Project Name (ID): Hubei Shiman Highway Project (P081749)

Country: China

Board Approval Date : 06/24/2004

Closing Date : 06/30/2009

Loan/Credit/Grant Number : IBRD-47450

Sector(s): Roads and highways (97%), Sub-national government administration (3%)

Theme(s): Infrastructure services for private sector development (P), Rural services and infrastructure (P), Administrative and civil service reform (P), Trade facilitation and market access (S), Non-communicable diseases and injury (S)

Project Development Objectives:

The main objective of the project is to support socioeconomic development of Hubei province by enhancing its access to other provinces, particularly the western region of China, improving local mobility within poor, remote western parts of the province, and strengthening governance of the provincial road sector.

Progress toward achieving development objective(s):

The project is progressing well with the construction. Most tunnels are now through and many of the structures are completed. They are online for opening the expressway at the end of 2007. The local road improvements have been completed, but there are some construction quality problems currently being addressed. Overall, the PDOs should be achieved. The progress on the institutional strengthening studies is mixed and the project is putting resources into improving these studies.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47450	Effective	200.00	73.61	125.39	1.00



Project Name (ID): Demonstration of alternatives to Chlordane and Mirex in Termite Control Project (P082992)

Country: China

Board Approval Date : 06/29/2006

Closing Date : 00/00/0000

Loan/Credit/Grant Number : MULT-53075

Sector(s): Housing construction (64%), Central government administration (16%), Sub-national government administration (16%), Petrochemicals and fertilizers (4%)

Theme(s): Pollution management and environmental health (P), Environmental policies and institutions (S), Other environment and natural resources management (S), Other human development (S)

Project Development Objectives:

The project development objective (PDO) is to mitigate environmental and health risks associated with chlordane and mirex in termite control by (a) demonstrating the elimination of their use through the introduction of integrated pest management in selected area, and (b) preparing a national replication program for complete phase-out of chlordane and mirex in China.

Progress toward achieving development objective(s):

The project was approved on June 29, 2006 and launched at a workshop in July 2006. The Grant Agreement was also signed by China MOF in July 2006.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-53075	Closed	0.28	0.27	0.01	0.00



Project Name (ID): PCB Management and Disposal Demonstration Project (P082993)

Country: China

Board Approval Date : 12/15/2005

Closing Date : 00/00/0000

Loan/Credit/Grant Number : MULT-53076

Sector(s): Other industry (57%), Solid waste management (33%), Sub-national government administration (6%), Central government administration (4%)

Theme(s): Pollution management and environmental health (P), Environmental policies and institutions (S), Other environment and natural resources management (S)

Project Development Objectives:


The development objective of this project is that China will implement policies and measures to identify and demonstrate environmentally-sound and cost-effective policies, procedures and techniques for safely managing and disposing of China's unique temporarily stored PCBs and associated PCB-contaminated wastes.

Progress toward achieving development objective(s):

The project was approved on Dec. 15, 2005 and was launched at a workshop in January 2006. The Grant Agreement was signed by MOF in March 2006 (the Bank signed it on January 3, 2006). The project was effective on June 29, 2006.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-53076	Closed	0.29	0.29	0.00	0.00

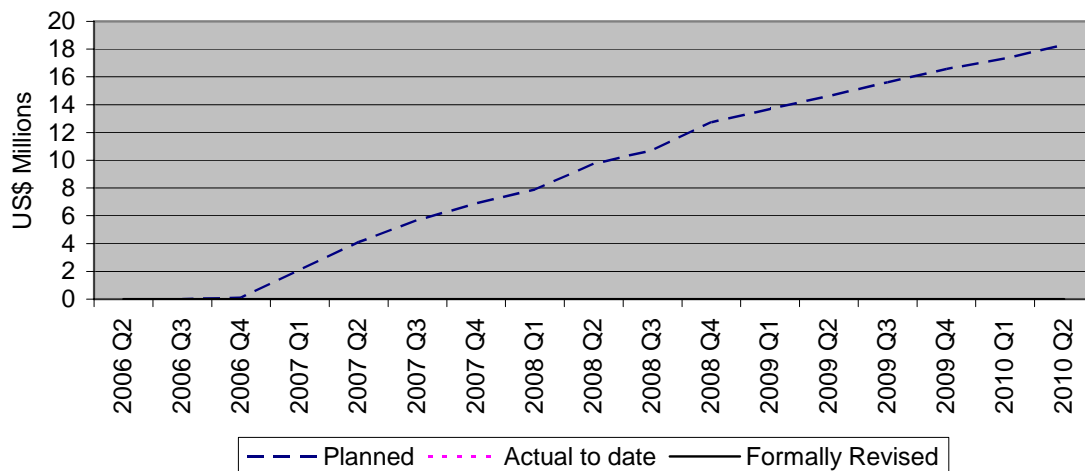

Project Name (ID): Irrigated Agriculture Intensification Loan III (P084742)

Country: China

Board Approval Date : 10/11/2005

Midterm Review Date : 06/30/2008

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-48030

Sector(s): Irrigation and drainage (68%), Agricultural extension and research (12%), General public administration (11%), Forestry (5%), General agriculture, fishing and forestry (4%)

Theme(s): Other rural development (P), Rural services and infrastructure (P), Rural policies and institutions (S), Environmental policies and institutions (S)

Project Development Objectives:

The objectives are to: (a) increase water and agricultural productivity in low- and medium-yield farm land areas; (b) raise farmers' incomes and strengthen their competitive capacity under post-WTO conditions; and (c) demonstrate and promote sustainable participatory rural water resources management and agro-ecological environmental management in the Huang-Huai-Hai River Basin area.


Progress toward achieving development objective(s):

The loan was approved on October 11, 2005. The Project Launch Workshop (PLW) was held from March 16-19, 2006 in Beijing. Staff from all the provinces/counties attended and received training on the project components, project management and topics related to project implementation. The PLW was very well organized, highly successful and much appreciated by the provinces/counties. The project started implementation under retro-active financing in April 2005 and is making satisfactory start-up progress. Although physical progress so far is limited, procurement procedures are under way and are almost complete in all provinces, and the main implementation work is expected to start on schedule. Pilot Water User Associations, Farmers Associations and organic/green crop production have been organized at initial sites in most provinces.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48030	Effective	200.00	20.50	179.50	0.00



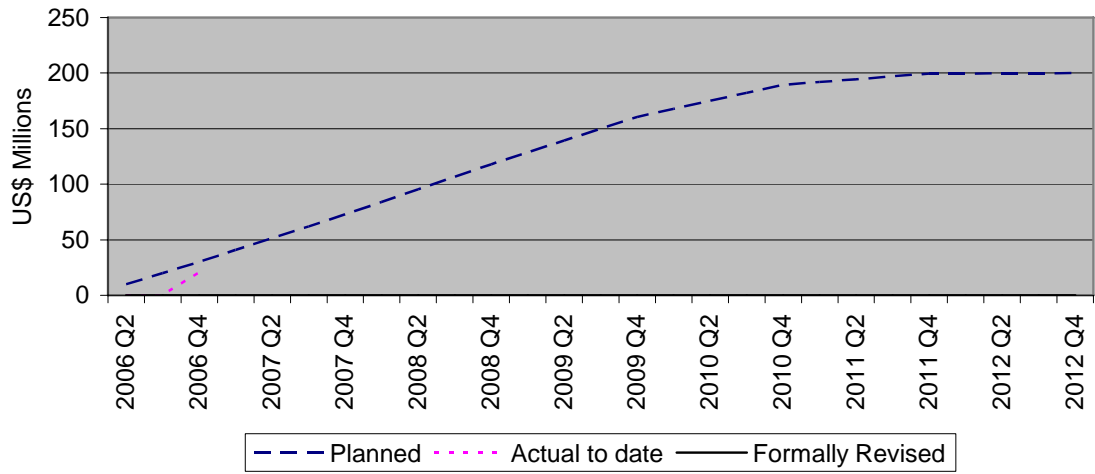

Project Name (ID): China Economic Reform Implementation Project (P085124)

Country: China

Board Approval Date : 04/11/2006

Midterm Review Date : 12/31/2008

Closing Date : 12/31/2011

Loan/Credit/Grant Number : IBRD-48200

Sector(s): Central government administration (65%), Sub-national government administration (30%), Banking (5%)

Theme(s): Analysis of economic growth (P), Public expenditure, financial management, and procurement (S), Improving labor markets (S), Biodiversity (S), Indigenous peoples (S)

Project Development Objectives:


The project development objective is to assist the GOC in implementing its reform and development agenda by significantly increasing the adoption and use of sound reform and development strategies, policies and implementation plans through a series of technical assistance subprojects tailored to address specific challenges through institutional capacity building at the national and sub-national levels.

Progress toward achieving development objective(s):

Loan Agreement and Trust Fund Agreement were signed on June 21, 2006. Overall, the project has started its implementation smoothly towards achieving the PDO.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48200	Not Effective	20.00	0.00	20.00	0.00

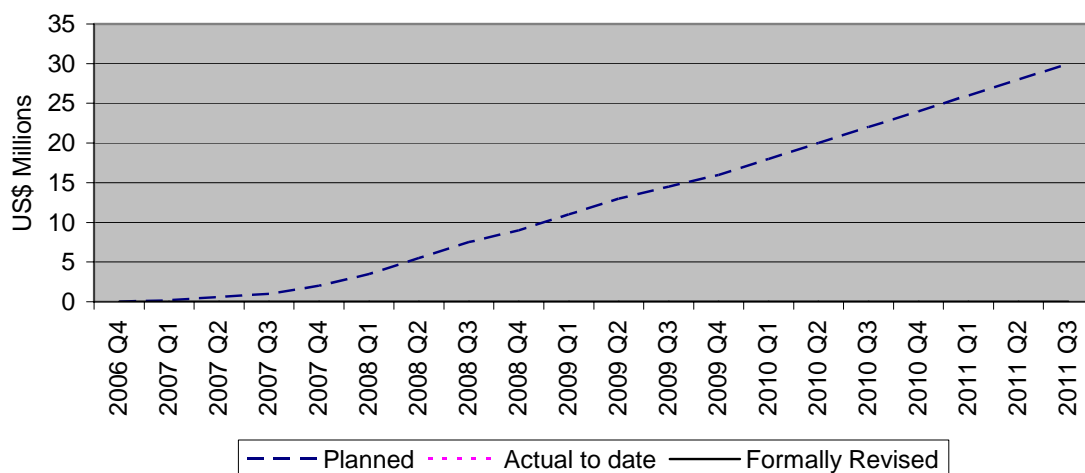

Project Name (ID): China: Fifth Inland Waterways (P085333)

Country: China

Board Approval Date : 10/11/2005

Closing Date : 06/30/2011

Loan/Credit/Grant Number : IBRD-48040

Sector(s): Ports, waterways and shipping (50%), Renewable energy (35%), Sub-national government administration (15%)

Theme(s): Infrastructure services for private sector development (P), Other rural development (P), Water resources management (S), Administrative and civil service reform (S)

Project Development Objectives:

The project's development objective is to enhance the standard of living in the Han River region by developing its potential water resources, including:

(a) increasing the waterway transport capacity along the Han River and its cost-effectiveness; and


(b) ensuring the availability of sustainable hydropower and water resources for use in the Xiangfan area and the Tangdong farmland region.

Progress toward achieving development objective(s):

The Project became effective in December 2005 and significant progress has been made to date. Though it is early, it is likely that the Project will be able to meet its development objective.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48040	Effective	100.00	7.22	92.78	0.00

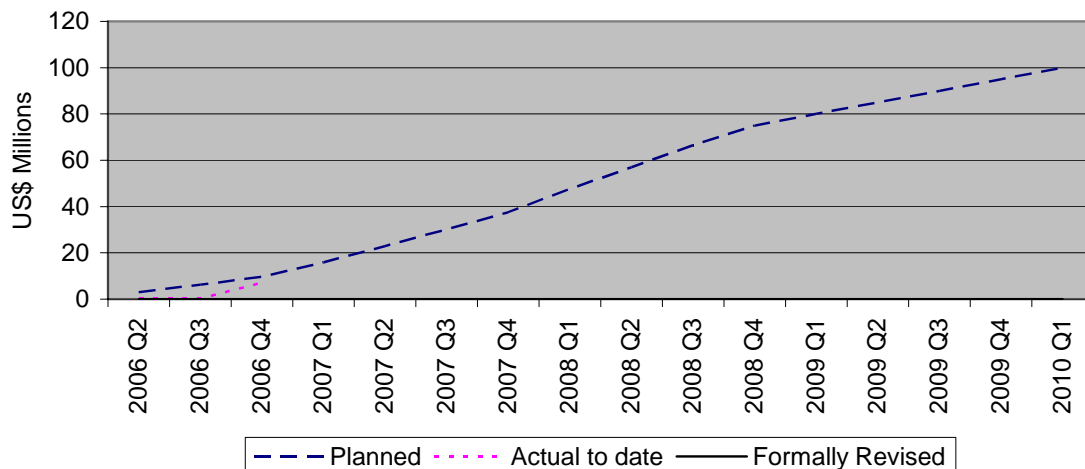

Project Name (ID): CN-Ningbo Water and Environment Project (P086505)

Country: China

Board Approval Date : 03/17/2005

Midterm Review Date : 12/03/2007

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-47700

Sector(s): Water supply (55%), Sewerage (45%)

Theme(s): Pollution management and environmental health (P), Water resources management (P), Municipal governance and institution building (S)

Project Development Objectives:


To facilitate the expansion and quality of water and wastewater services in Ningbo City and Cixi City in an economically efficient and environmentally sustainable manner.

Progress toward achieving development objective(s):

The project is progressing reasonably well. Work on the Ningbo city water supply component is going well as is the Cixi wastewater component. Procurement is underway for consultants to provide assistance on water supply planning and to make operational improvements to the distribution system. Both Cixi and Ningbo are expected to increase water and wastewater tariffs in July 2006 to maintain sustainability. With the ongoing works and institutional progress, the project is facilitating expansion and quality of water and wastewater in Ningbo and Cixi in a sustainable manner.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47700	Effective	130.00	9.54	120.46	0.00

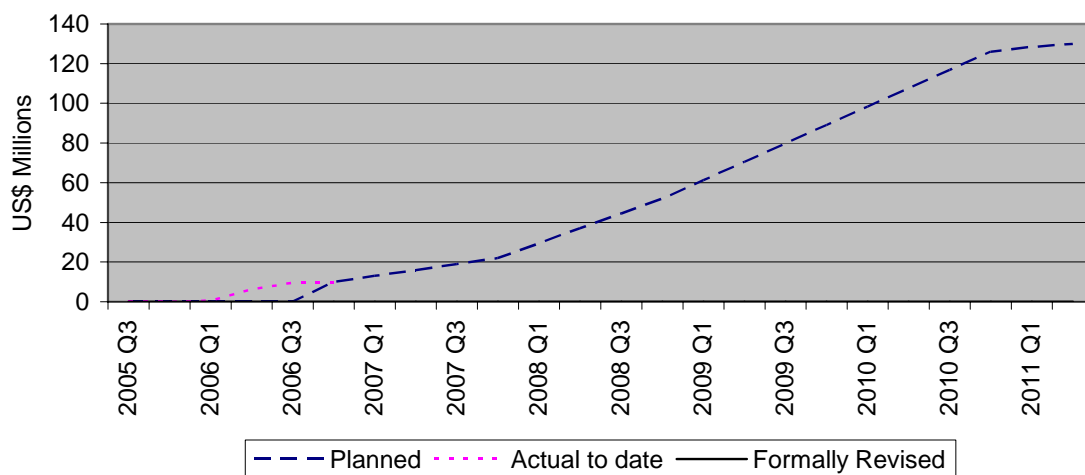

Project Name (ID): CN-Heilongjiang Dairy (P086629)

Country: China

Board Approval Date : 01/24/2006

Midterm Review Date : 12/31/2008

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-48150

Sector(s): Animal production (69%), Agricultural extension and research (27%), Crops (3%), Sub-national government administration (1%)

Theme(s): Other rural development (P), Rural services and infrastructure (P), Technology diffusion (S), Rural policies and institutions (S), Climate change (S)

Project Development Objectives:

The objectives of the project are to: (a) improve the financial viability of existing and new dairy operations in selected areas of Heilongjiang province; and (b) demonstrate innovative technologies to reduce green-house gas emissions and increase carbon sequestration.


Progress toward achieving development objective(s):

The Loan was approved on January 24, 2006. Project implementation started in earnest soon after approval, particularly in the construction of civil works, permitted by the retroactive financing provisions in the Loan and Italian Grant Agreements. Work was initiated on six of the seven planned demonstration farms and on six of the planned 50 new dairy parks. The identification of beneficiary households continues and tender documents for the procurement of dairy cattle from national and international sources are under preparation. A training and technical assistance program for 2006 was prepared (along with a multi-year program) and submitted to the Bank, which reviewed and cleared the documents.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48150	Not Effective	100.00	0.00	100.00	0.00



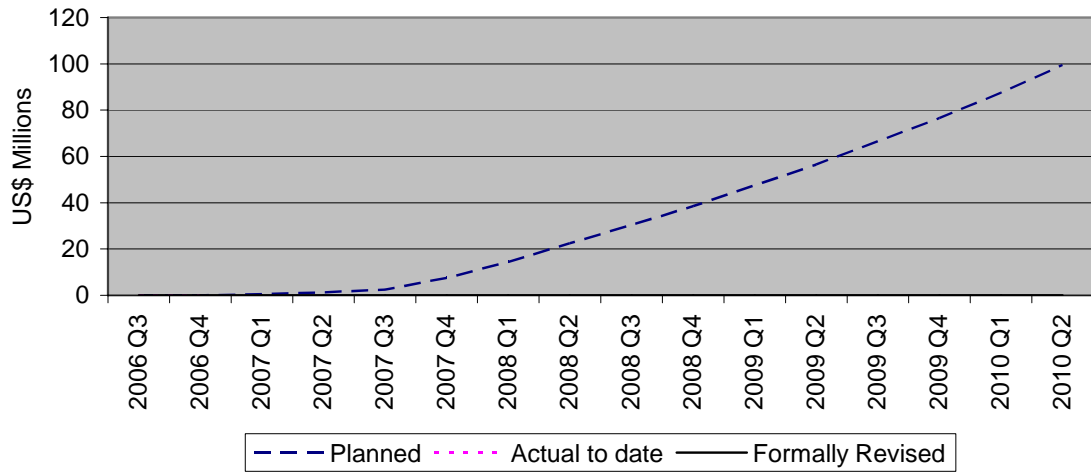

Project Name (ID): China-GEF-Ningbo Water and Environment Project (P090336)

Country: China

Board Approval Date : 06/29/2006

Closing Date : 09/01/2006

Loan/Credit/Grant Number : MULT-55469

Sector(s): General water, sanitation and flood protection (100%)

Theme(s): Pollution management and environmental health (P), Biodiversity (S), Water resources management (S)

Project Development Objectives:


To reduce land-based pollution along the Cixi coast and the East China Sea, promote the replication of innovative low cost wastewater treatment techniques, and encourage coastal zone conservation

Progress toward achieving development objective(s):

The grant was just approved on June 29, 2006.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-55469	Effective	0.25	0.20	0.05	0.00

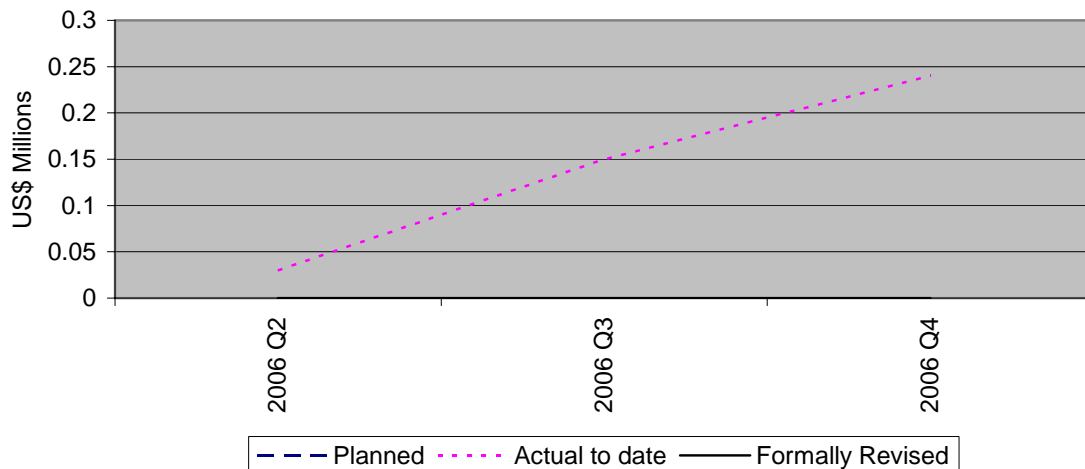

Project Name (ID): Third Jiangxi Highway Project (P093906)

Country: China

Board Approval Date : 06/27/2006

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-48300

Sector(s): Roads and highways (97%), Sub-national government administration (3%)

Theme(s): Infrastructure services for private sector development (P), Trade facilitation and market access (P), Non-communicable diseases and injury (S), Rural services and infrastructure (S)

Project Development Objectives:

The project development objective is to improve east-west passenger and freight flows in Jiangxi province by investing in the construction of an expressway, enhancing local roads, and strengthening highway management.

Progress toward achieving development objective(s):

The project was approved at the end of June and is not yet effective.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48300	Not Effective	200.00	0.00	200.00	0.00



Project Name (ID): Follow Up to CRESP Phase I (P096158)

Country: China

Board Approval Date : 02/07/2006

Midterm Review Date : 04/02/2007

Closing Date : 09/30/2010

Loan/Credit/Grant Number : IBRD-48160

Sector(s): Renewable energy (100%)

Theme(s): Climate change (P), Infrastructure services for private sector development (P), Environmental policies and institutions (P), Rural services and infrastructure (S)

Project Development Objectives:

The project development objective is to demonstrate early success in large-scale renewable energy investments with participating local developers in one pilot autonomous region and one pilot province.

Progress toward achieving development objective(s):

The project became effective on June 16, 2006.

Implementation in Zhejiang has been under way for several months under retroactive financing arrangements and is on target to meet the intermediate indicators of 28MW of new or rehabilitated small hydro by 2007. Further market development, funded by GEF funds from China Renewable Energy Scale-up Program (CRESP - P067625) is now being planned.

The wind farm component in Huitengxile is expected to start procurement in July. As for Zhejiang, the market development tasks are funded under CRESP and are under planning. It is too early to judge on the contribution of this component towards the PDO.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48160	Not Effective	86.33	0.00	86.33	0.00



Project Name (ID): Liaoning Medium Cities Infrastructure Project (P099992)

Country: China

Board Approval Date : 06/27/2006

Closing Date : 12/31/2011

Loan/Credit/Grant Number : IBRD-48310

Sector(s): Roads and highways (70%), General transportation (16%), Sanitation (14%)

Theme(s): Other urban development (P), Access to urban services and housing (S),
Municipal governance and institution building (S)

Project Development Objectives:

The objective of the Project is to assist the Borrower's Project Cities in enhancing: (i) the performance and quality of their existing urban transport infrastructure in terms of mobility, access, and safety; (ii) the efficiency and effectiveness of their urban public transport and road maintenance services; and (iii) the responsiveness of their urban transport systems to the needs of population without access to private motorized vehicles.

Progress toward achieving development objective(s):

The project just got approved and was not yet effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48310	Not Effective	218.00	0.00	218.00	0.00

