

STATUS OF PROJECTS IN EXECUTION – FY07
SOPE
CHINA

Operations Policy and Country Services
OCTOBER 10, 2007



Introduction

The Status of Projects in Execution (SOPE) Report for FY07 provides information on all IBRD/IDA projects that were active as of June 30, 2007. The World Bank has issued a SOPE Report every year as an internal communication to the Board of Executive Directors. In accordance with the Bank's revised disclosure policy, since FY02, the SOPE Report is available to the public.

The report is intended to bridge the gap in information available to the public between the Project Appraisal Document or Program Document, disclosed after the Bank approves a project, and the Implementation Completion Report, disclosed after the project closes.

In addition to the project progress description, the FY07 SOPE report¹ contains project level comparisons of disbursement estimates and actual disbursements, and a table showing the loan/credit/grant amount and disbursements to date.

¹ Notes:

- Amounts and Graphs for loans/credits/grants in currencies other than U.S. dollars may not match exactly due to exchange rate fluctuations over the life of the project.
- Disbursement graphs are not included for Development Policy Operations, which provide quick-disbursing financing to support policy and institutional reforms. For these operations, funds are disbursed in one or more stages (tranches), released when the borrower complies with agreed prior actions.
- Projects which are not yet effective may not have a planned disbursement schedule and thus will not include a graph.



Country: China

Project Name (ID): Third ODS Phaseout (P003409)

Country: China

Board Approval Date : 06/22/1995

Closing Date : 12/31/2010

Loan/Credit/Grant Number : WBTF-22452, WBTF-20738, WBTF-22002

Sector(s): Other industry(97%), Banking(2%), Central government administration(1%)

Theme(s): Pollution management and environmental health(P), Environmental policies and institutions(S)

Project Development Objectives:

The objective of the project is to establish an efficient and flexible institutional mechanism to prepare, appraise, finance and implement a large number of sub-projects in support of China's total Ozone Depleting substances (ODS) phase-out program.

Progress toward achieving development objective(s):

China is one of the largest remaining ODS producers and consumers. Completed sub-projects in the project have achieved their targeted phase-out. The remaining sub-projects under implementation are expected to achieve their target phase-out as well.


All activities and disbursement in the project have been completed with the ODS phase-out of total 19,062 metric tons of ODS. The early completion of the project resulted from a shift from the individual sub-project modality in ODS III to a sector-wide, performance-based approach in ODS IV; all sub-projects originally anticipated to be included in ODS III are now financed under ODS IV in different sector plans. This phase-out helps China to meet its 2005 obligation of 50% phase-out and 2007 commitment of 85% phase-out under the Montreal Protocol.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
WBTF-22452	Closed	0.14	0.11	0.00	0.03
WBTF-20738	Closed	0.69	0.65	0.00	0.04
WBTF-22002	Effective	120.10	88.51	31.59	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

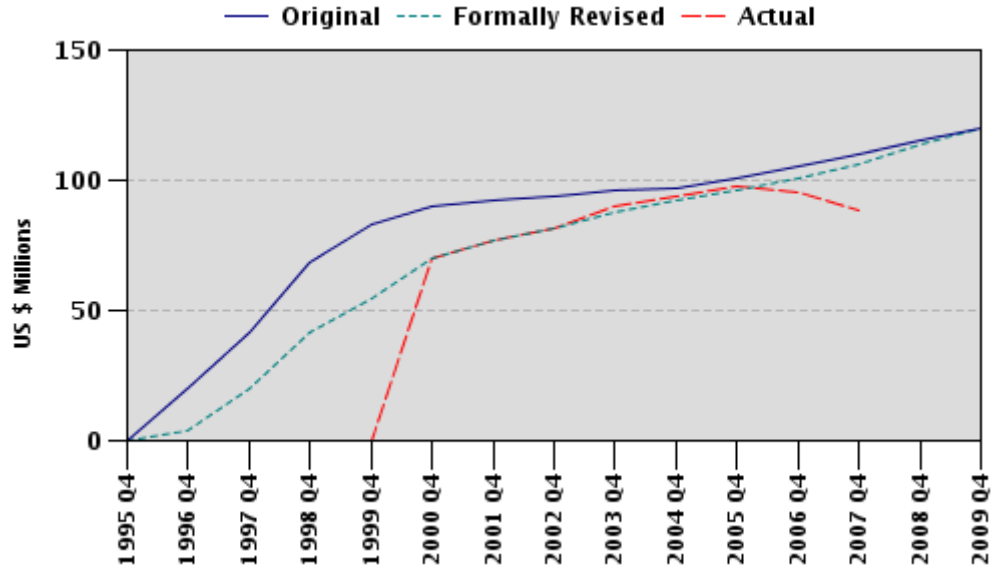

Project Name (ID): Sustainable Coastal Resources Development (P003539)

Country: China

Board Approval Date : 05/19/1998

Midterm Review Date : 11/13/2001

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-43220, JPN-29734

Sector(s): Animal production(70%), Other domestic and international trade(20%),
Central government administration(10%)

Theme(s): Water resource management(P), Export development and competitiveness(P),
Biodiversity(S)

Project Development Objectives:

The objectives are: (a) to promote the sustainable development of the country's coastal resources; (b) to reduce pressure on coastal fishery resources; and (c) to improve the quality of aquatic products.

Progress toward achieving development objective(s):


Project implementation continues to show progress in all areas, with most of the planned investments and related activities on track to being completed prior to the Loan's Closing Date of December 31, 2007. The development objectives of the project, particularly related to coastal zone management, are being realized as most provincial governments are now placing an increased emphasis on investments to protect marine biodiversity and on standards for seafood processing.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-43220	Effective	100.00	84.89	13.05	2.06
JPN-29734	Closed	0.40	0.40	0.00	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

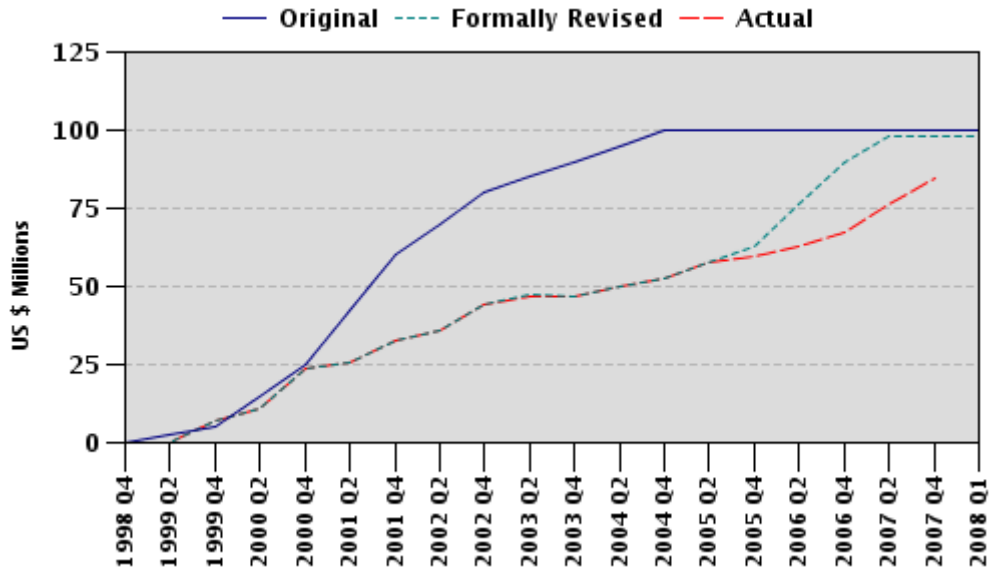

Project Name (ID): Guangzhou City Transport (P003614)

Country: China

Board Approval Date : 05/29/1998

Midterm Review Date : 06/15/2001

Closing Date : 12/31/2007

Loan/Credit/Grant Number : JPN-25202, IBRD-43290

Sector(s): Roads and highways(75%), General transportation sector(25%)

Theme(s): Access to urban services and housing(P), Municipal governance and institution building(P), Pollution management and environmental health(P), Other urban development(P)

Project Development Objectives:


To improve the accessibility of the city center of Guangzhou by promoting the efficient use of the urban transport system in an environmentally sustainable way.

Progress toward achieving development objective(s):

The project was extended till 12/31/2007. The road network service has improved with the completion of GIRR and Guangfo Radial road, traffic management program has been strengthened and has become a good example for other cities in China.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-25202	Closed	0.31	0.27	0.00	0.05
IBRD-43290	Effective	200.00	133.22	46.78	20.00

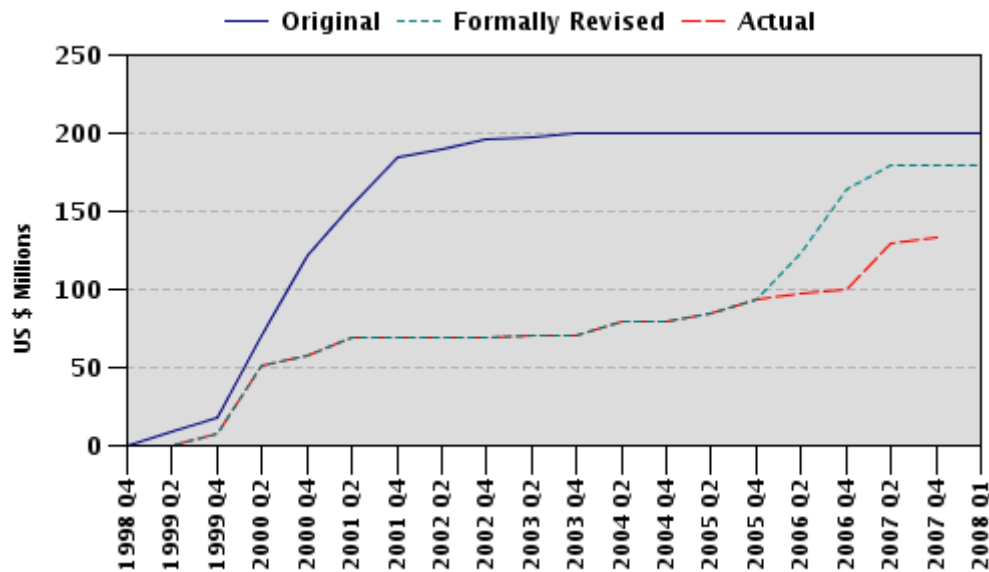

Project Name (ID): GUANGXI URBAN ENVMT (P036414)

Country: China

Board Approval Date : 06/16/1998

Midterm Review Date : 11/02/2001

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-43480, IDA-30970, JPN-29733

Sector(s): Sewerage(76%), Water supply(13%), Solid waste management(5%), Agro-industry(4%), General transportation sector(2%)

Theme(s): Water resource management(P), Pollution management and environmental health(P), Environmental policies and institutions(P), Access to urban services and housing(P)

Project Development Objectives:

To (a) improve the quality of major water bodies, in particular Chaoyang stream and Yongjiang in Nanning and Lijiang and its tributaries in Guilin; (b) regulate the flow of the Lijiang; (c) improve institutional and financial capacity for environmental protection, environmental services and water resource management; (d) pilot a participatory approach to environmental improvement in poor neighborhoods; and (e) implement pilot schemes for control of sugar refinery pollution.

Progress toward achieving development objective(s):


Good progress has been made on improving the quality of water bodies including construction of a wastewater treatment plant, pumping stations, and laying of sewer mains and drains. To regulate the flow of the Lijiang River, reforestation work and rehabilitation and construction work over 37 km of embankments have been completed. The institutional and financial capacity of the two project sewerage companies continues to improve, with projections that both will make a profit in 2006. The pilot participatory approach to environmental improvements has been successful with over 47,000 beneficiaries. The sugar refineries have installed pollution control facilities to minimize and treat highly polluting stillage.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-43480	Effective	72.00	44.44	14.08	13.48
IDA-30970	Effective	22.58	19.23	1.40	0.00
JPN-29733	Closed	0.15	0.15	0.00	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

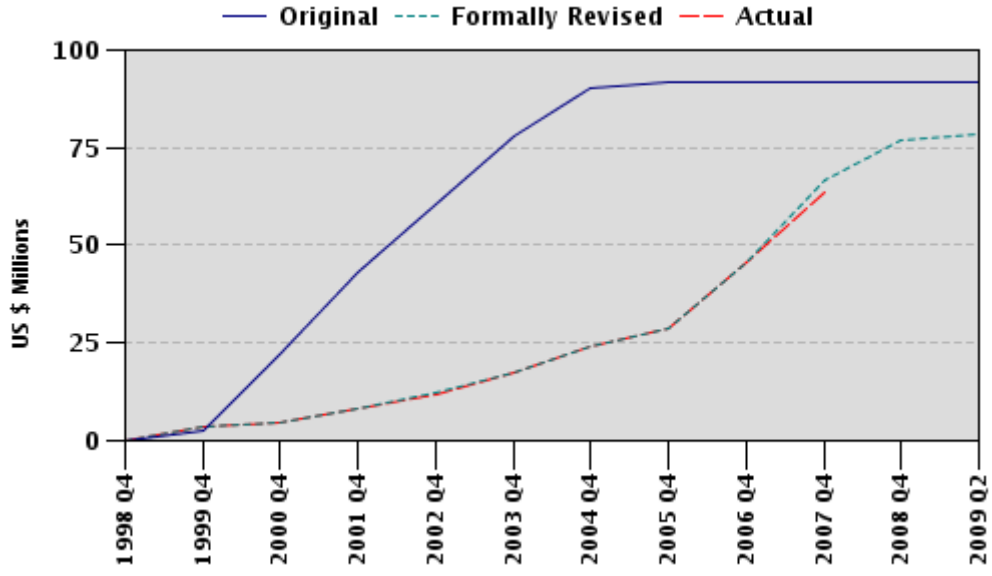

Project Name (ID): Health IX (P036953)

Country: China

Board Approval Date : 05/04/1999

Midterm Review Date : 04/09/2004

Closing Date : 06/30/2008

Loan/Credit/Grant Number : JPN-26233, JPN-53812, JPN-25401, IDA-32010, IBRD-44620, AUSL-23612

Sector(s): Health(94%), Sub-national government administration(6%)

Theme(s): Child health(P), HIV/AIDS(P), Population and reproductive health(S), Health system performance(S), Participation and civic engagement(S)

Project Development Objectives:

The objectives of the project are to reduce maternal and child morbidity and mortality and improve child development, prevent and control HIV/AIDS and sexually transmitted diseases, and assure the supply of safe blood.

Progress toward achieving development objective(s):


All project provinces have continued to see improvements in key MCH indicators, including maternal mortality, under-five mortality, and hospital delivery rates, although there have been considerable differences in progress across project provinces. Available data also indicate progress in both HIV/AIDS and STI prevention, and nearly all project localities have reached 100% voluntary unpaid blood donation (VUBD). These achievements reflect improved technical guidelines and standards, health education and behavior change activities, expanded coverage of priority interventions in the target populations.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26233	Closed	0.40	0.40	0.00	0.00
JPN-53812	Effective	0.66	0.31	0.35	0.00
JPN-25401	Closed	0.10	0.10	0.00	0.00
IDA-32010	Effective	55.77	40.95	10.75	0.00
IBRD-44620	Effective	10.00	4.70	4.90	0.40
AUSL-23612	Closed	1.70	1.16	0.00	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

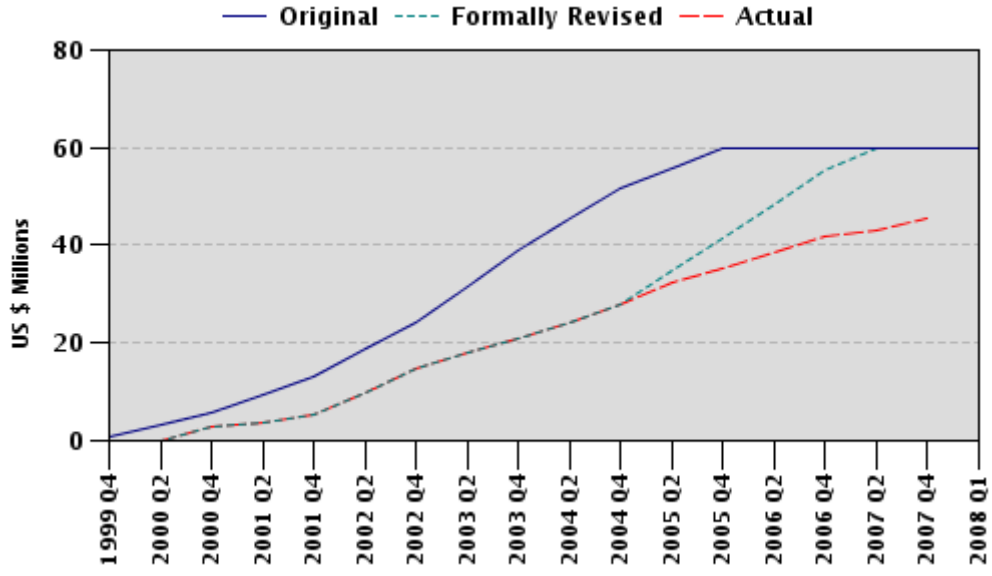

Project Name (ID): BEIJING ENVIRONMENT II (P042109)

Country: China

Board Approval Date : 06/20/2000

Midterm Review Date : 11/08/2002

Closing Date : 03/31/2009

Loan/Credit/Grant Number : JPN-27034, IBRD-45660

Sector(s): Sewerage(49%), District heating and energy efficiency services(48%), Other industry(2%), Sub-national government administration(1%)

Theme(s): Climate change(P), Pollution management and environmental health(P), Environmental policies and institutions(P), Other urban development(P), Water resource management(P)

Project Development Objectives:

Visible and sustained alleviation of air and water pollution in Beijing

The project was restructured, or received Additional Financing during FY 07

The project had substantial savings from the boiler conversion component because market forces provided the financing to convert coal-burning boilers to cleaner fuels. The main goal of the restructuring was to reallocate savings from that component to the wastewater management component to deepen achievement of the project's objective of improving water quality in Beijing.

Progress toward achieving development objective(s):


Good progress was made in fiscal year 2007. Implementation of the original program for wastewater is nearing completion, with three wastewater treatment plants now constructed and operating smoothly. Procurement of air quality monitoring equipment is also near completion, as is development of an Air Quality Management Decision Support System. Under the new components, much procurement has already been done and works are getting under way. The works under the original program and those financed from loan savings will allow the project to meet its objective of alleviating air and water pollution in Beijing.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-27034	Closed	0.64	0.51	0.00	0.13
IBRD-45660	Effective	349.00	154.13	168.36	26.51



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

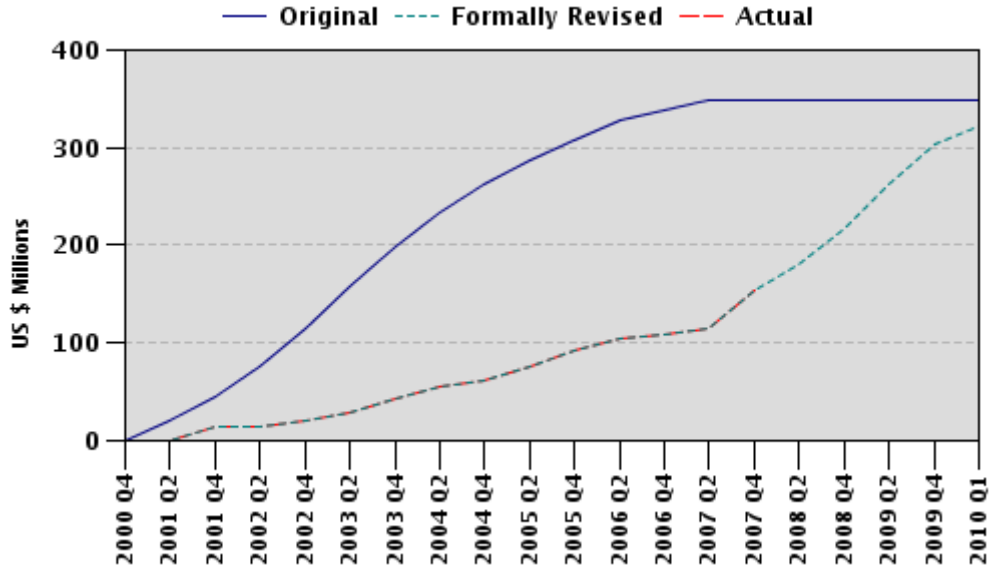

Project Name (ID): Tec Coop Credit IV (P042299)

Country: China

Board Approval Date : 05/18/1999

Closing Date : 10/31/2007

Loan/Credit/Grant Number : UK-53180, IDA-32120, IBRD-44730

Sector(s): Central government administration(50%), Sub-national government administration(50%)

Theme(s): Macroeconomic management(P), Analysis of economic growth(P), Other rural development(P), Other social protection and risk management(P)

Project Development Objectives:

The objective of the project is to provide continued support to the Government of China in its economic and structural reform effort, help capacity building and improve the project preparation.

Progress toward achieving development objective(s):


The performance of the borrower and other project implementing agencies is rated as satisfactory in the latest ISR. As of end of June, 2007, the project has financed 38 subprojects under its Part A and 3 subprojects under its Part B, with SDR25.18 million IDA credit and US\$2.06 million IBRD loan allocated, respectively. All subprojects except for seven under Part A have completed implementation or are expected to complete implementation by Oct. 31, 2007. All completed and ongoing subprojects have achieved, or are expected to achieve, designed objectives in a satisfactory manner. The Project Management Office located in the International Department of Ministry of Finance and most Subproject Management Offices have demonstrated strong leadership and adequate capacity in project implementation. The borrower has requested an extension of the closing date to Dec. 31, 2009. This is now being processed internally.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
UK-53180	Closed	3.19	2.93	0.00	0.07
IDA-32120	Effective	38.95	27.49	9.76	0.00
IBRD-44730	Effective	10.00	0.98	3.18	5.84



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

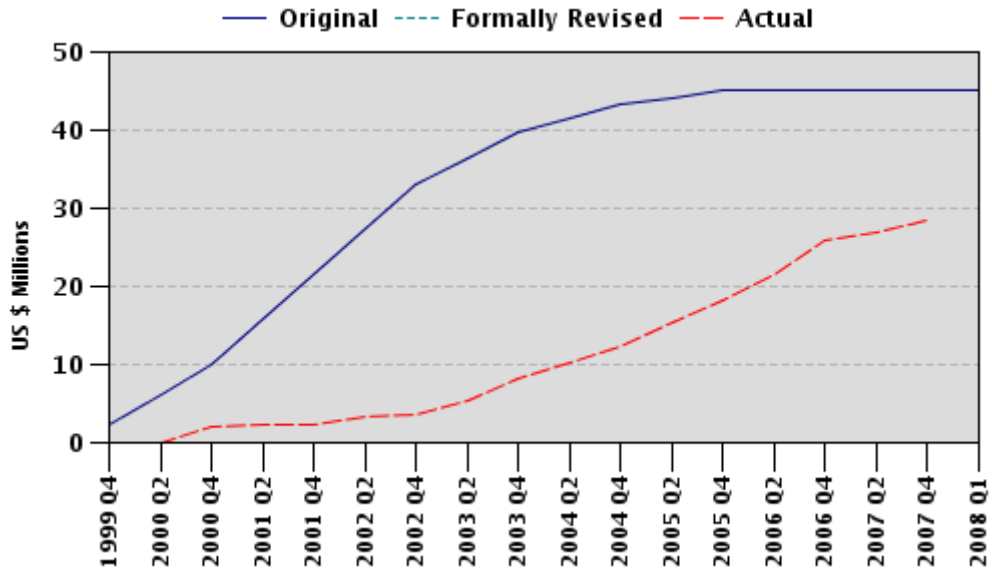

Project Name (ID): HEBEI URBAN ENVIRONMENT (P045910)

Country: China

Board Approval Date : 06/27/2000

Midterm Review Date : 11/15/2004

Closing Date : 06/30/2008

Loan/Credit/Grant Number : JPN-26661, IBRD-45690

Sector(s): Sewerage(66%), Water supply(33%), Sub-national government administration(1%)

Theme(s): Water resource management(P), Pollution management and environmental health(P), Access to urban services and housing(P), Environmental policies and institutions(P)

Project Development Objectives:

To develop a safe environment and to sustain the long-term economic growth of urban areas in Hebei Province.

Progress toward achieving development objective(s):


Progress toward building the infrastructure necessary to provide a safe environment in urban areas in Hebei has been solid. Implementation of the original components has been completed except for the interceptors for the main trunk sewer in the Shijiazhuang wastewater component, which should be completed by end 2007. All facilities are performing as expected. Progress on institutional issues has also been strong. All companies are meeting financial covenants except one where approval of a tariff increase is awaited. There are loan savings in the project, and the borrower has requested that the savings be used to finance additional components in order to enhance achievement of objectives.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26661	Closed	0.36	0.36	0.00	0.00
IBRD-45690	Effective	150.00	116.22	33.78	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

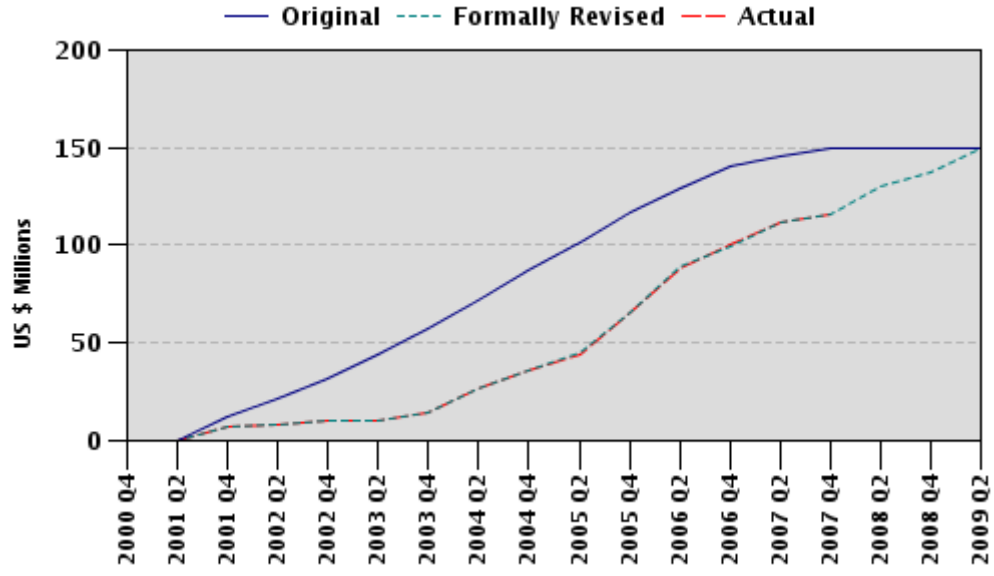

Project Name (ID): Urumqi Urban Transport (P045915)

Country: China

Board Approval Date : 12/19/2000

Midterm Review Date : 06/04/2004

Closing Date : 12/31/2007

Loan/Credit/Grant Number : JPN-25107, IBRD-45900

Sector(s): Roads and highways(88%), Sub-national government administration(8%), General transportation sector(4%)

Theme(s): Infrastructure services for private sector development(P), Access to urban services and housing(P), Pollution management and environmental health(S), Climate change(S), Municipal governance and institution building(S)

Project Development Objectives:


To foster a multi-modal urban transport system which is planned, designed and used for the safe, efficient and healthy movement of people and goods.

Progress toward achieving development objective(s):

There has been progress made for the project in accordance with the updated project implementation plan. Nevertheless, the activities related to public transport, environment and institutional strengthening may be delayed.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-25107	Closed	0.40	0.40	0.00	0.00
IBRD-45900	Effective	100.00	67.83	32.17	0.00

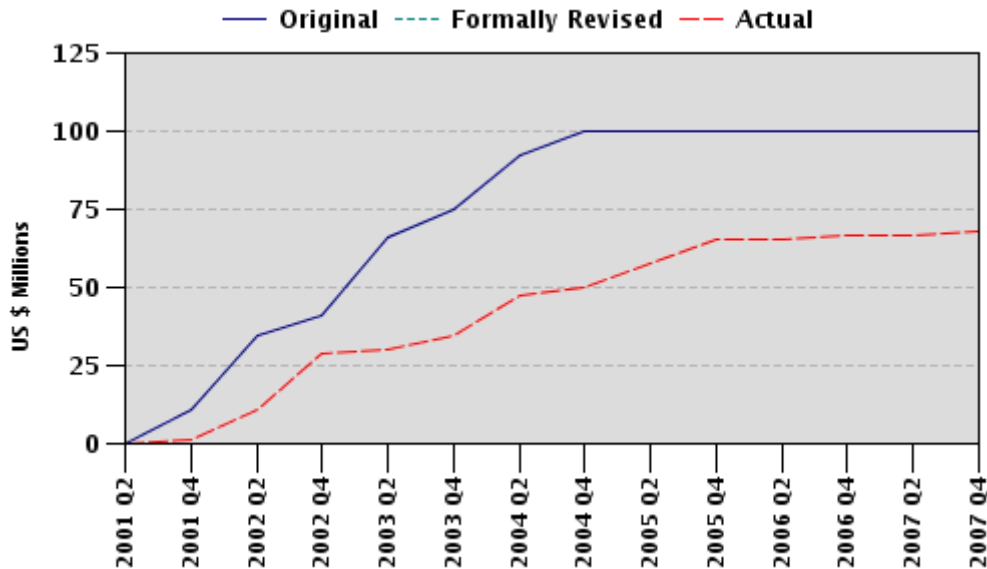

Project Name (ID): HUAI RIVER POLLUTION CONTROL (P047345)

Country: China

Board Approval Date : 03/22/2001

Midterm Review Date : 10/19/2004

Closing Date : 06/30/2008

Loan/Credit/Grant Number : IBRD-45970, JPN-29717

Sector(s): Sewerage(100%)

Theme(s): Water resource management(P), Pollution management and environmental health(P)

Project Development Objectives:

To upgrade water quality in the Huai River Basin particularly in the provinces of Anhui and Shandong.

Progress toward achieving development objective(s):


In Shandong, works such as wastewater treatment plants, collection sewers and pumping stations have been successfully completed and commissioned. Their operations will help upgrade the water quality in the Shandong portion of the Huai Basin. Similar works in Anhui are somewhat behind schedule due to slow procurement and land acquisition delays which have now been resolved. Most of the remaining components in Anhui will be completed by loan closing with the possible exception of commissioning of a wastewater treatment plant. In terms of sustainability, five out of eight wastewater companies are financially viable. Viability will be strengthened when the sewer network is completed and if self-supply water users such as state-owned industries are required to connect to the sewer network.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-45970	Effective	105.50	85.73	19.77	0.00
JPN-29717	Closed	0.32	0.32	0.00	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

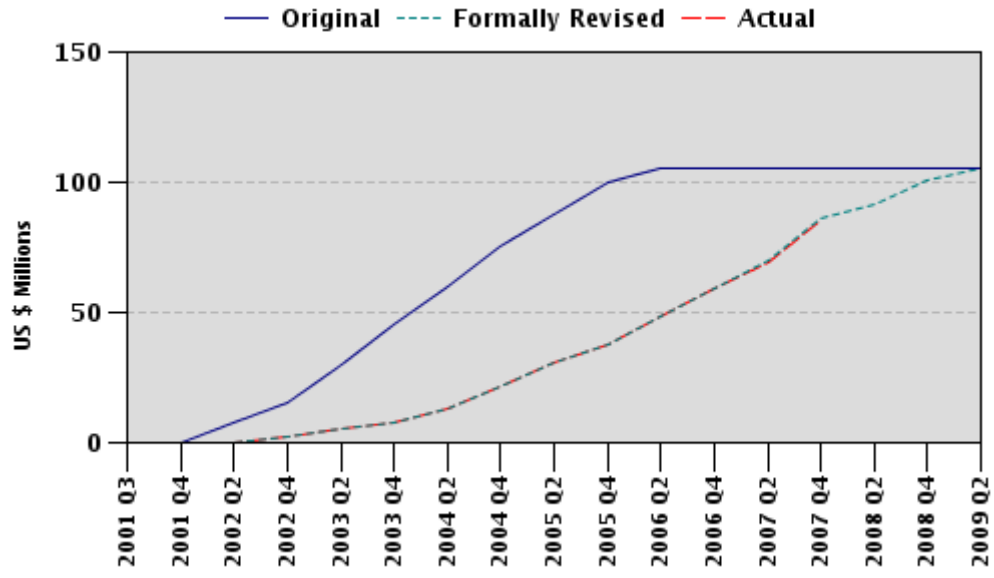

Project Name (ID): CHONGQING URBAN ENVMT (P049436)

Country: China

Board Approval Date : 06/15/2000

Midterm Review Date : 07/23/2004

Closing Date : 12/31/2007

Loan/Credit/Grant Number : JPN-26651, JPN-25098, IBRD-45610

Sector(s): Sewerage(74%), Solid waste management(15%), Water supply(6%), Sub-national government administration(5%)

Theme(s): Pollution management and environmental health(P), Water resource management(P), Environmental policies and institutions(P), Access to urban services and housing(P)

Project Development Objectives:

To provide a safe environmental setting for the sustainable long-term economic growth of urban areas in Chongqing Municipality.

Progress toward achieving development objective(s):


Progress toward meeting the objectives in fiscal year 2007 was generally good. Two wastewater treatment plants and related interceptor pipes have been completed but the plants are operating somewhat below capacity. Additional secondary connections should increase their efficiency. Except for the procurement of solid waste transport equipment, the solid waste component is complete. For the additional components added in 2005, good progress is also being made with 22 out of 46 contracts under way. These works will reduce the pollution load from the urban sector and expand the supply of safe water. Steady advances also continue on institutional and financial aspects to enhance sustainability. A one-year extension of the loan closing date may be necessary to complete the additional program started in 2005.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26651	Closed	0.32	0.32	0.00	0.01
JPN-25098	Closed	0.10	0.10	0.00	0.00
IBRD-45610	Effective	200.00	108.90	61.60	29.50



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

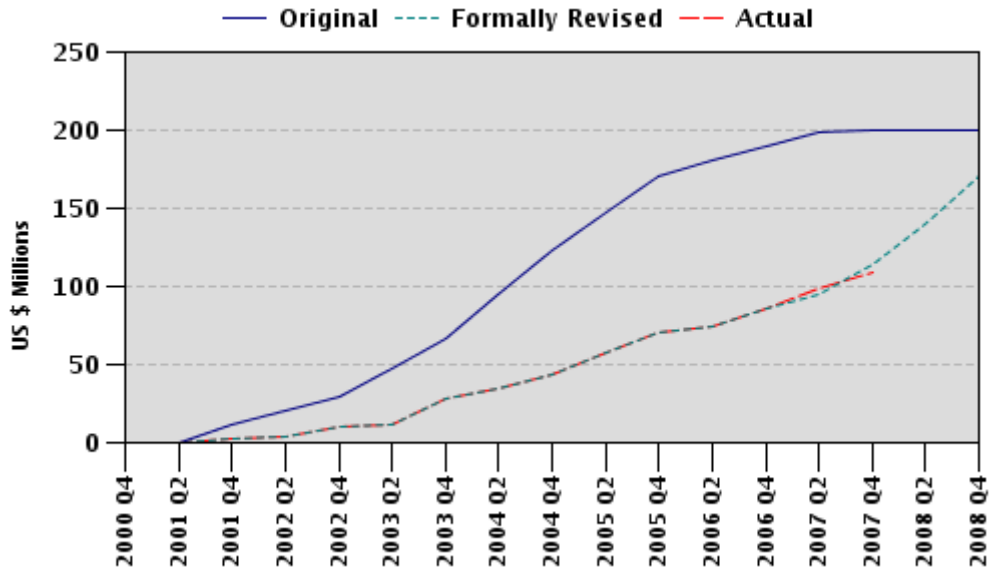

Project Name (ID): Accounting Reform and Development (P051856)

Country: China

Board Approval Date : 02/23/1999

Midterm Review Date : 10/23/2003

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IDA-31730, IBRD-44420

Sector(s): Tertiary education(83%), Central government administration(17%)

Theme(s): Standards and financial reporting(P), Other public sector governance(S)

Project Development Objectives:


The fundamental objective of the project is to accelerate the modernization of China's accounting professionals and accounting systems.

Progress toward achieving development objective(s):

The project continues to make progress toward the project development objective during FY07. Since the issuance of 2006 Chinese Accounting Standards (CAS) converged with International Financial Reporting Standards (IFRS), the project has set up training courses to disseminate the 2006 CAS and carried out massive training. In addition to training on CAS, the National Accounting Institutes have trained over 200,000 person-days in other areas such as degree courses. Guidelines for application of 2006 CAS, and CPA firm partnership culture guidelines have also been developed during the year.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-31730	Effective	6.21	4.15	1.56	0.00
IBRD-44420	Effective	27.40	22.78	4.62	0.00

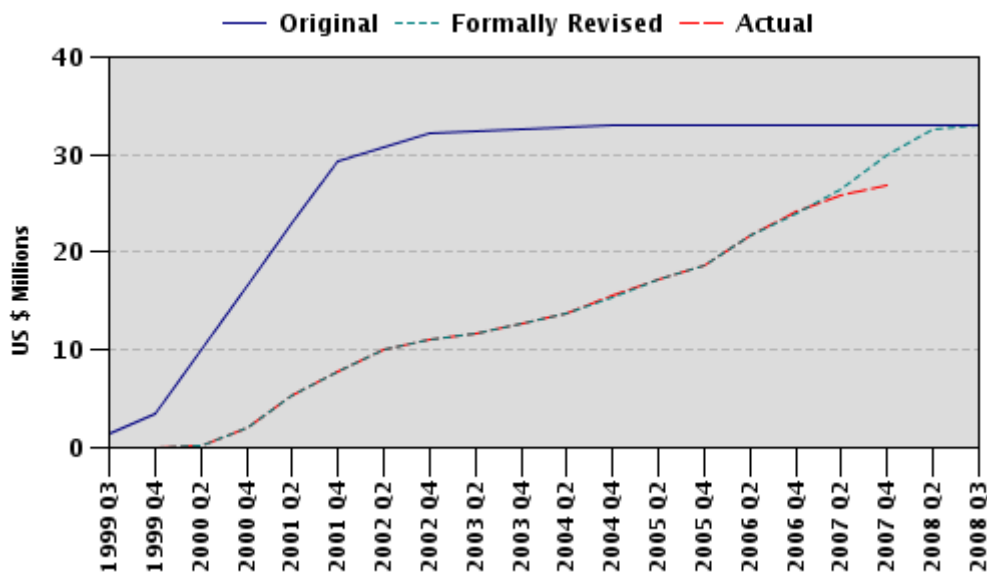

Project Name (ID): LIAO RIVER BASIN (P051859)

Country: China

Board Approval Date : 06/19/2001

Midterm Review Date : 07/02/2004

Closing Date : 12/31/2007

Loan/Credit/Grant Number : JPN-50520, JPN-25912, IBRD-46170

Sector(s): Sewerage(83%), Other industry(10%), Sub-national government administration(7%)

Theme(s): Water resource management(P), Pollution management and environmental health(P)

Project Development Objectives:

To assist the environmental recovery of the Liao River Basin in Liaoning Province and to enhance water quality management decision-making on the basis on an integrated river basin management approach.

Progress toward achieving development objective(s):


Overall progress toward meeting the objectives is reasonable. Works such as the construction of municipal wastewater treatment plants (WWTP) in Panjin, Yingkou and Jinzhou, are well underway or complete and will assist with the environmental recovery of the Liao River Basin. The two paper mills, however, are both seeing industrial wastewater management problems. Yingkou Paper Mill authorities were originally going to use funds from the North European Development Fund to construct its WWTP; however such funds are no longer available so the plant has not been constructed. Equipment to enhance decision-making has been procured, but there is a gap between data collection and the analysis required to inform decision-making. This shortcoming needs to be addressed in the coming period. Presently the financial sustainability of the wastewater companies is being assured through a combination of tariffs and municipal government subsidies. The longer-term goal is to eliminate those operational subsidies.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-50520	Closed	1.21	1.21	0.00	0.00
JPN-25912	Closed	0.76	0.76	0.00	0.00
IBRD-46170	Effective	100.00	85.53	14.47	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

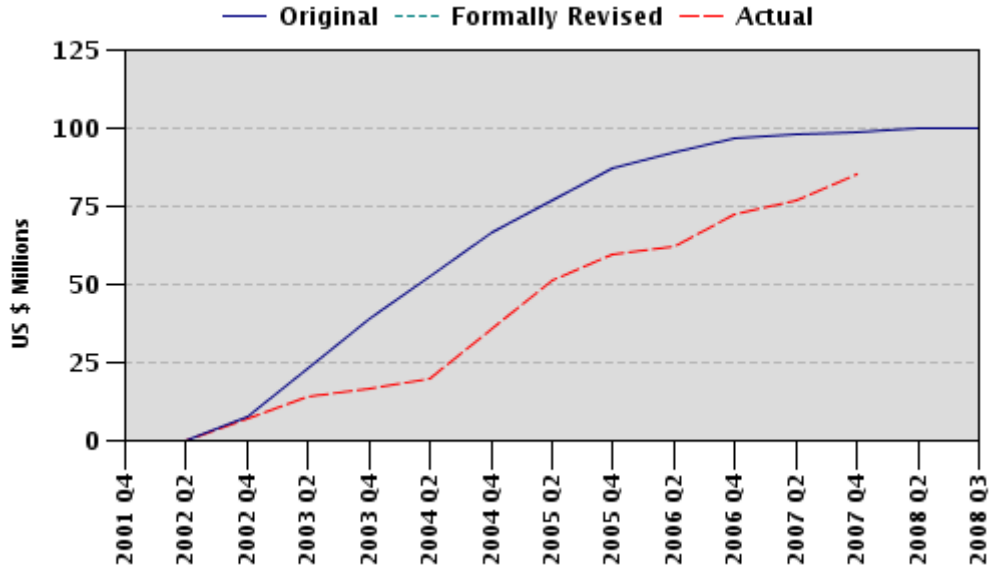

Project Name (ID): 3rd Inland Waterways (P056199)

Country: China

Board Approval Date : 06/21/2001

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-46210, JPN-25699

Sector(s): Power(77%), Ports, waterways and shipping(12%), General water, sanitation and flood protection sector(6%), Roads and highways(3%), Central government administration(2%)

Theme(s): Rural services and infrastructure(P), Climate change(S), Decentralization(S), Access to urban services and housing(S)

Project Development Objectives:


To reduce transport and energy bottlenecks by: (a) improving market access of the remote inland areas of Hunan Province; (b) providing more efficient and economic inland waterway transport; and (c) generating power to supplement the needs of the remote areas.

Progress toward achieving development objective(s):

The Project with the exception of residual overseas training is essentially complete. The data required for the ICR is being prepared. It is expected the Project will close on the original closing date of Dec. 31, 2007. Further measurement of performance indicators is required, nonetheless, it is expected that Project development objective will be achieved.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46210	Effective	100.00	92.33	7.67	0.00
JPN-25699	Closed	0.80	0.72	0.00	0.08

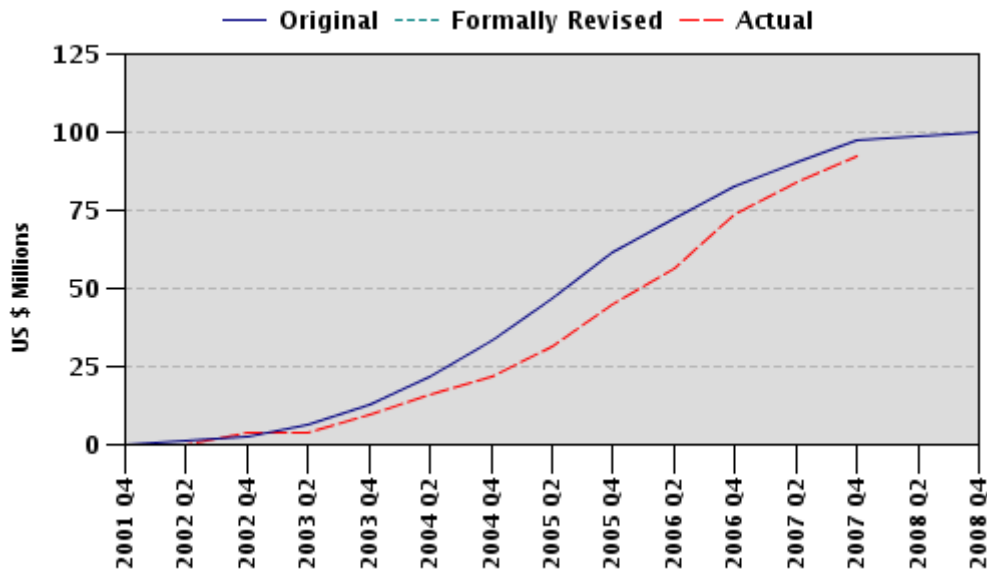

Project Name (ID): Tongbai Pumped Storage (P056424)

Country: China

Board Approval Date : 12/22/1999

Closing Date : 12/31/2007

Loan/Credit/Grant Number : JPN-25701, IBRD-45290

Sector(s): Power(99%), Sub-national government administration(1%)

Theme(s): Rural services and infrastructure(P), Regulation and competition policy(P), Other financial and private sector development(P), Climate change(P), Infrastructure services for private sector development(P)

Project Development Objectives:

To (a) increase peaking capacity and improve load-following capability and power quality in the Zhejiang and East China power systems; and (b) improve the operating and investment efficiency in generation by developing and implementing a competitive generation market in Zhejiang province.

Progress toward achieving development objective(s):


Progress toward achieving project objectives is steady: (a) the pumped storage power plant component has been completed; all the four units were commissioned ahead of schedule and are now under satisfactory operation; (b) the transmission reinforcement component has been successfully completed and under satisfactory operation; and (c) the originally planned activities under the power sector restructuring and power market development component are fully complete. A few new activities (such as consultant services in IT areas and training/study tours) are being implemented as planned and should be completed soon.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-25701	Closed	0.58	0.58	0.00	0.00
IBRD-45290	Effective	320.00	189.31	30.69	100.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

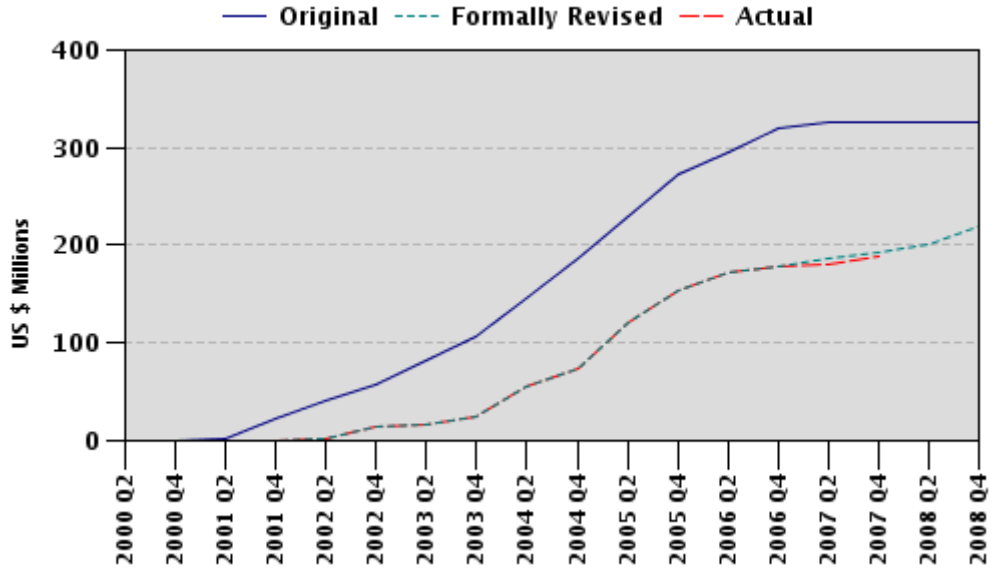

Project Name (ID): Shijiazhuang Urban Transport (P056596)

Country: China

Board Approval Date : 03/27/2001

Midterm Review Date : 06/10/2004

Closing Date : 12/31/2008

Loan/Credit/Grant Number : JPN-25415, IBRD-46000

Sector(s): Roads and highways(91%), General transportation sector(8%), Sub-national government administration(1%)

Theme(s): Other urban development(P), Municipal governance and institution building(S), Pollution management and environmental health(S)

Project Development Objectives:

To foster the development of an efficient and environmentally sustainable urban transport system in Shijiazhuang while providing a wider set of travel choices for users.

Progress toward achieving development objective(s):


A reasonable functional hierarchy road network especially high capacity road network has been established using both local and Bank financing over the last five years. Along with the road construction, reasonable wider bicycle and pedestrian lanes have been established and preserved. With the implementation of the ATC system and two phases of junction channelization, the road system became more efficient. With the introduction of Zhongshan Bus Lane and enlarged computer management system for SPTC and other large improvement financed locally, bus mode share has increased from 4% in 1998 to 10% at the end of 2006. Overall institutional capacity has been strengthened.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-25415	Closed	0.38	0.38	0.00	0.00
IBRD-46000	Effective	100.00	53.96	46.04	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

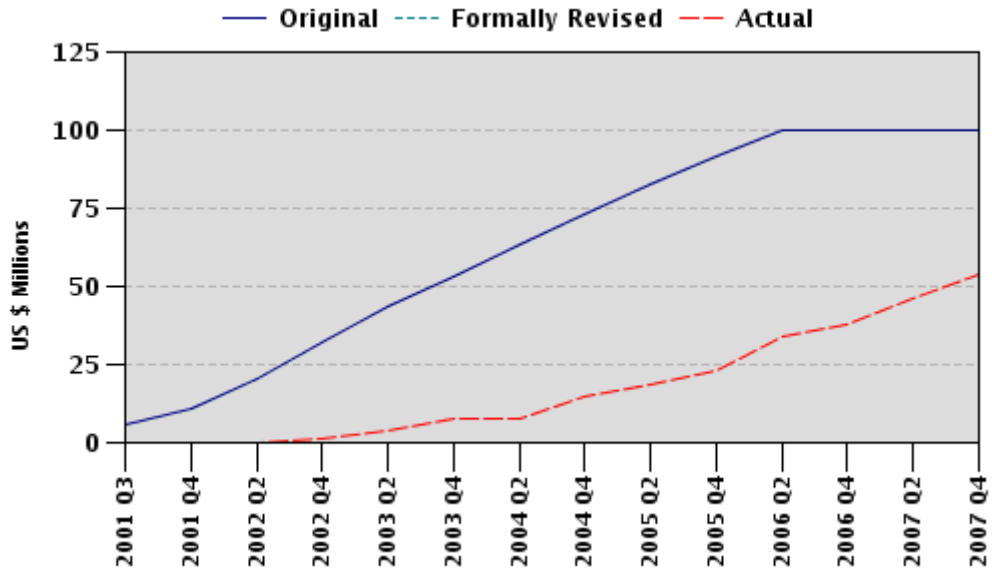

Project Name (ID): TAI BASIN URBAN ENVMT (P057933)

Country: China

Board Approval Date : 08/03/2004

Closing Date : 12/31/2009

Loan/Credit/Grant Number : IBRD-47480, JPN-26178

Sector(s): Sewerage(90%), Flood protection(10%)

Theme(s): Water resource management(P), Pollution management and environmental health(P), Other urban development(P), Infrastructure services for private sector development(S)

Project Development Objectives:

To improve the quality of life of the rapidly increasing urban population and enhance economic

competitiveness in Wuxi and Suzhou, key municipalities in the Tai Basin and the Yangtze River Delta

economic region, by alleviating degradation of water resources and improving the quality of the urban

environment.

Progress toward achieving development objective(s):


Progress on installing the infrastructure necessary to prevent the degradation of water resources and to improve the environment in the project areas has been very good. The first phase wastewater treatment plant (WWTP) in Huishan is completed and the plant is operating normally. Contracts for WWTP expansions in Suzhou have been awarded and should commence in the latter half of 2007. The Wuzhong wastewater component is not likely to proceed following changes in the District masterplan. Alternative works consistent with the project objectives are being identified for possible financing with the loan savings from this component. Institutional reforms are also progressing well in Wuxi, with both wastewater companies corporatized. However, the Suzhou Drainage Department has not yet been corporatized, and this reform is to be accelerated.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47480	Effective	61.00	26.82	34.18	0.00
JPN-26178	Closed	0.88	0.88	0.00	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

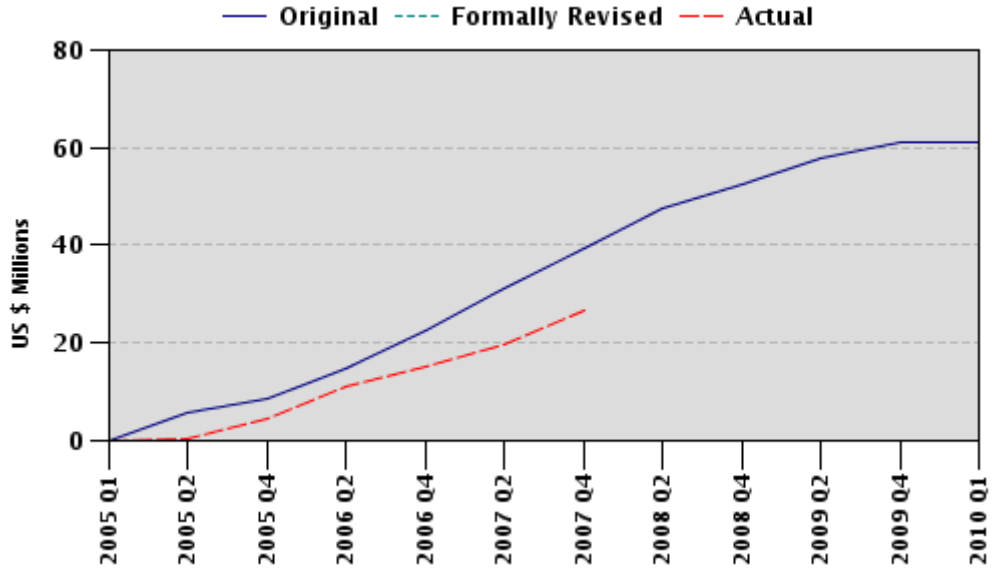

Project Name (ID): National Railway Project (P058846)

Country: China

Board Approval Date : 01/29/2002

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-46480, JPN-29623

Sector(s): Railways(93%), Telecommunications(6%), Central government administration(1%)

Theme(s): Infrastructure services for private sector development(P), State enterprise/bank restructuring and privatization(P), Regulation and competition policy(S), Corporate governance(S)

Project Development Objectives:


To (a) increase the capacity of the railway network between eastern and western China; and (b) support the reform program of China Railways.

Progress toward achieving development objective(s):

The physical implementation has been completed. The technical assistance is underway and progress is good. Preparation of the ICR is underway. The early completion of the physical construction of the line has led to early realization of the first part of the Project Development Objective as supported by measurement of the performance indicators. Substantial progress has been made by the Ministry of Railways towards realizing the principal elements of institutional reform.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46480	Effective	160.00	153.44	1.56	5.00
JPN-29623	Closed	0.81	0.45	0.00	0.36

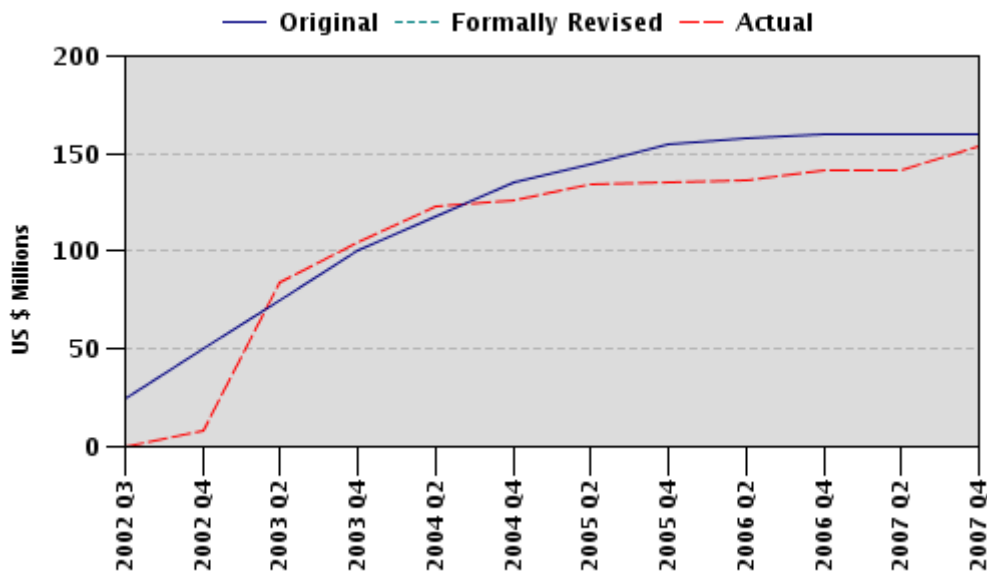

Project Name (ID): 3rd Xinjiang Hwy Project (P058847)

Country: China

Board Approval Date : 09/05/2002

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-71430, JPN-26427

Sector(s): Roads and highways(94%), Sub-national government administration(6%)

Theme(s): Rural services and infrastructure(P), Infrastructure services for private sector development(P), Other public sector governance(S)

Project Development Objectives:


To improve transport infrastructure and sector governance in support of social and economic development in Xinjiang Uygur Autonomous Region.

Progress toward achieving development objective(s):

Under the project's main component, the construction of the Kuitun-Sailimuhu highway was completed in the fall of 2005. Under the local roads rehabilitation (LRRP) component, the works accomplished to date are improving access for rural communities. The institutional component is exposing provincial staff to modern managerial approaches in the road sector. The LRRP and institutional components are lagging behind schedule, and a one-year loan extension is currently being processed. The revised actions plans, with scheduled deliverables are being implemented. Overall, the project is on the right track to meeting its objectives.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-71430	Effective	150.00	130.84	19.16	0.00
JPN-26427	Closed	0.20	0.20	0.00	0.00

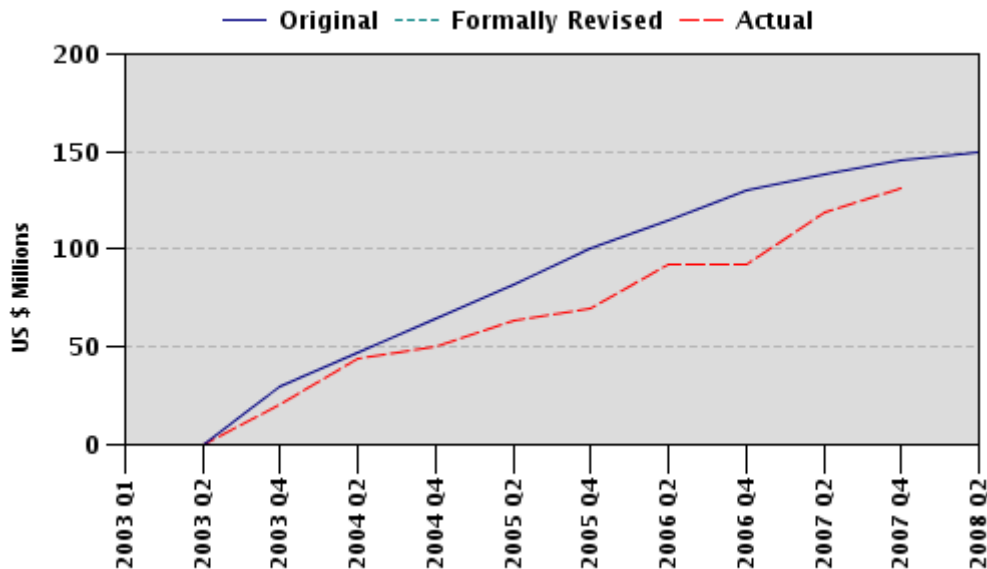

Project Name (ID): CN ODS IV PHASE OUT PRJ (P039838)

Country: China

Board Approval Date : 11/21/1997

Closing Date : 06/30/2011

Loan/Credit/Grant Number : WBTF-23972, WBTF-22017, WBTF-22014, MULT-50722, MULT-23973

Sector(s): Other industry(94%), Central government administration(6%)

Theme(s): Environmental policies and institutions(P), Pollution management and environmental health(P)

Project Development Objectives:

The objective of the project is to phase out the production and consumption of Ozone Depleting Substances (ODS) to enable China to fulfill its obligation under the Montreal Protocol. The global development objective of fully reversing the damage to the Ozone layer will only be met as a result of all global actions taken from 1987 and the process will take sixty to seventy years to complete.

Progress toward achieving development objective(s):


China is one of the largest remaining ODS producers and consumers. Through a combination of regulatory measures, public information and financial assistance to enterprises, China has developed a large ODS phase-out program. All the sectors taken up in China have successfully met their annual production and consumption targets on schedule. Annual phase-out targets for all sector plans have been met in FY2007 and in previous years.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
WBTF-23972	Closed	0.03	0.03	0.00	0.00
WBTF-22017	Effective	440.00	275.11	164.89	0.00
WBTF-22014	Closed	0.10	0.10	0.00	0.00
MULT-50722	Closed	0.10	0.00	0.00	0.10
MULT-23973	Closed	0.12	0.12	0.00	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

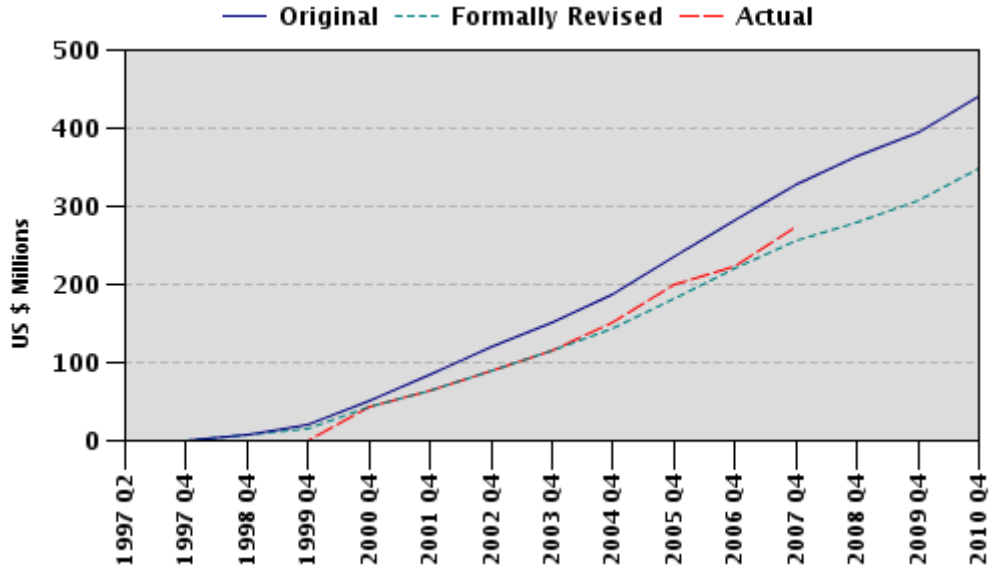

Project Name (ID): TIANJIN URB DEV II (P040599)

Country: China

Board Approval Date : 05/20/2003

Midterm Review Date : 09/09/2006

Closing Date : 06/30/2011

Loan/Credit/Grant Number : JPN-25106, IBRD-46950

Sector(s): Sewerage(45%), Sub-national government administration(25%), General transportation sector(20%), Flood protection(10%)

Theme(s): Access to urban services and housing(P), Pollution management and environmental health(P), Water resource management(S), Municipal governance and institution building(S), Infrastructure services for private sector development(S)

Project Development Objectives:

To enhance the efficiency and equity of urban wastewater management and transportation systems, and thus facilitate the sustainable development of Tianjin and serve as a model for other cities in China.

The project was restructured, or received Additional Financing during FY 07

The goals of the restructuring were to (a) cancel the water reuse component as changing circumstances undermined its financial feasibility; (b) drop the Daguanlu Interchange following a postponement in preparation of the Tianjin transportation masterplan; and (c) use the savings from (a) and (b) above (some \$17 million) to upgrade roads and drains simultaneously in Beicang and Nanjiaowai and build a bus parking depot under the bus priority corridors component.

Progress toward achieving development objective(s):


Progress toward achieving the project objectives was slow in FY07 as the above restructuring was being discussed, prepared and approved in April 2007. Implementation of the restructured project is set to take off in FY08 as the planning and design for the road and drainage works in Beicang and Nanjiaowai have proceeded rapidly. An environmental monitor for the Dagu Canal has been contracted, and sediment landfill construction and canal dredging should start in FY08. For the Shuanglin wastewater treatment plant (WWTP), land acquisition is still pending and the engineering design needs to be adjusted to meet higher national discharge standards. For the Hangu WWTP, a design-build-operate contract is awaiting government approval. These works will eventually enhance wastewater management and transportation in Tianjin. To ensure sustainability, an executive summary of proposed drainage sector reforms is underway and should be ready by October 2007. A transportation study to support planning and a public bus system is underway as well.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-25106	Closed	0.57	0.41	0.00	0.16
IBRD-46950	Effective	150.00	21.24	128.76	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

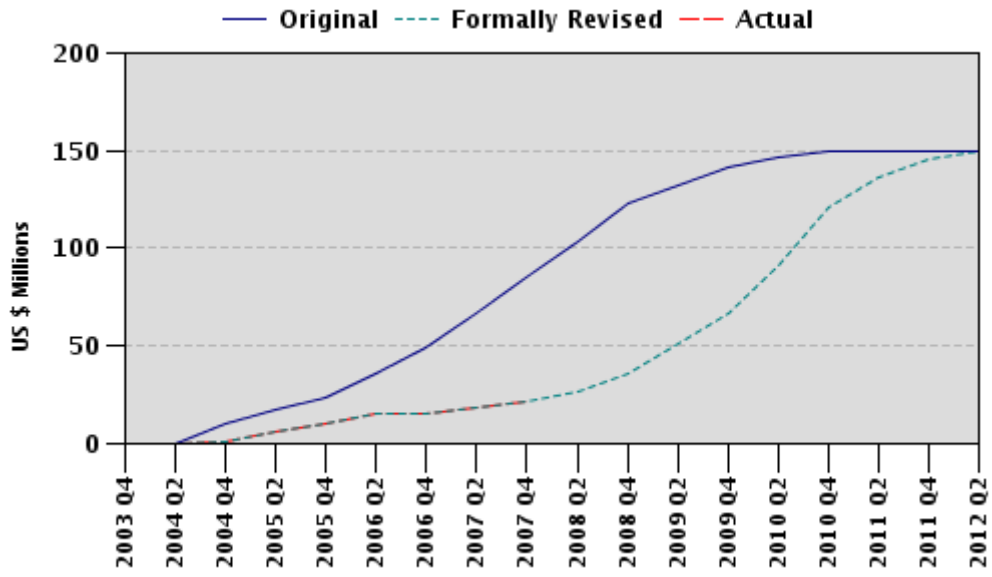

Project Name (ID): Sustainable Forestry Development (P064729)

Country: China

Board Approval Date : 04/16/2002

Midterm Review Date : 10/19/2005

Closing Date : 08/31/2009

Loan/Credit/Grant Number : JPN-25769, IBRD-46590

Sector(s): Forestry(100%)

Theme(s): Biodiversity(P), Rural non-farm income generation(P), Participation and civic engagement(P)

Project Development Objectives:

The objective is to develop and adopt viable, participatory, and locally managed systems for conservation, management and sustainable use of forest resources and associated biodiversity in project sites to promote the sustainable development of forest resources and protect natural environments. The global environmental objective is to foster improved conservation and sustainable management of biodiversity in remaining natural forest areas.

Progress toward achieving development objective(s):


The project is on course to achieve or exceed its development objective and targets. With 73% of the project's implementation period having elapsed since Board approval, nearly 90 percent of physical project targets have been achieved and participatory systems for the sustainable use of forest resources and biodiversity are being utilized.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-25769	Closed	0.60	0.60	0.00	0.00
IBRD-46590	Effective	93.90	71.46	22.44	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

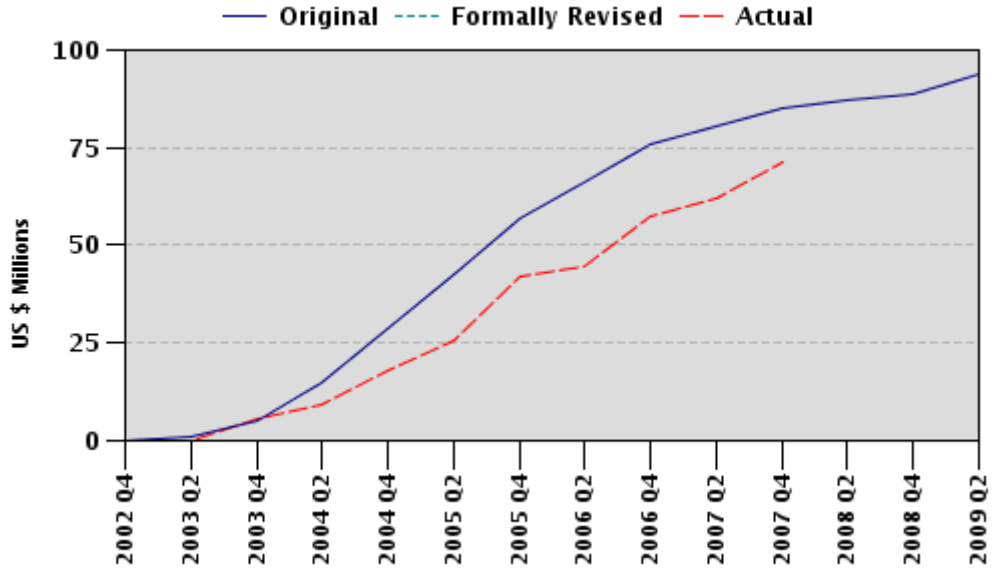

Project Name (ID): Yangtze Dike Strengthening (P064730)

Country: China

Board Approval Date : 06/27/2000

Midterm Review Date : 11/18/2002

Closing Date : 06/30/2008

Loan/Credit/Grant Number : JPN-26173, IBRD-45700

Sector(s): Flood protection(97%), Central government administration(2%), Sub-national government administration(1%)

Theme(s): Land administration and management(P), Water resource management(P), Decentralization(S)

Project Development Objectives:

The objective is to enhance the protection of the river bank against erosion and to improve key sections of the main dikes of the mid-Yangtze River and thereby protect property and life against floods.

Progress toward achieving development objective(s):


The majority of civil works for river bank and dike construction on the main river course have been completed in both Hubei and Hunan provinces, and recent floods have shown the works to perform well. In addition, the completion of: (a) the Yangtze River physical model; and (b) the OandM manual and accompanying training of staff in modern OandM methods mean that the Institutional Development component is well on the way to achieving its goals. The Closing Date of the Loan was extended by 1.5 years to June 30, 2008 to include additional dikes strengthening on two tributary rivers of the main stream Yangtze River in the vicinity of Wuhan City. Additional dike works, again on tributary rivers in the vicinity of Huanggang City, will be added in FY08. Both additions support the achievement of the original objective.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26173	Closed	0.42	0.42	0.00	0.00
IBRD-45700	Effective	210.00	138.90	71.10	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

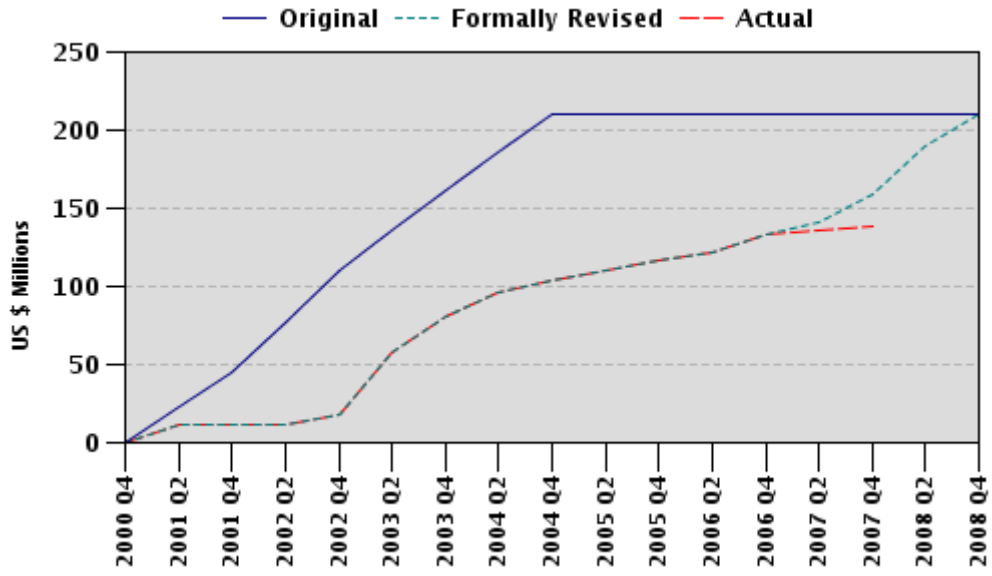

Project Name (ID): Gansu and Xinjiang Pastoral Development (P065035)

Country: China

Board Approval Date : 09/09/2003

Closing Date : 06/30/2010

Loan/Credit/Grant Number : MULT-51488, JPN-26739, JPN-26167, IBRD-47180

Sector(s): Animal production(50%), Agricultural marketing and trade(25%), Agricultural extension and research(25%)

Theme(s): Land administration and management(P), Other environment and natural resources management(P), Rural markets(P)

Project Development Objectives:

The objective of the project is to promote sustainable natural resource management and to increase the income of herders and farmers in the project areas. The global environment objective of the project is to maintain and nurture natural grassland ecosystems.

Progress toward achieving development objective(s):


Project implementation progress has improved significantly with close to 60% of the project completed at mid-term. Positive impacts are being seen in terms of increased price being fetched on the market for project livestock and livestock products compared with non-project livestock and livestock products. Main challenge and implementation priority remains to establish a system of effective knowledge transfer and learning to and among farmers and herders.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-51488	Closed	0.20	0.20	0.00	0.00
JPN-26739	Closed	0.51	0.46	0.00	0.04
JPN-26167	Closed	0.49	0.48	0.00	0.00
IBRD-47180	Effective	66.27	38.25	28.02	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

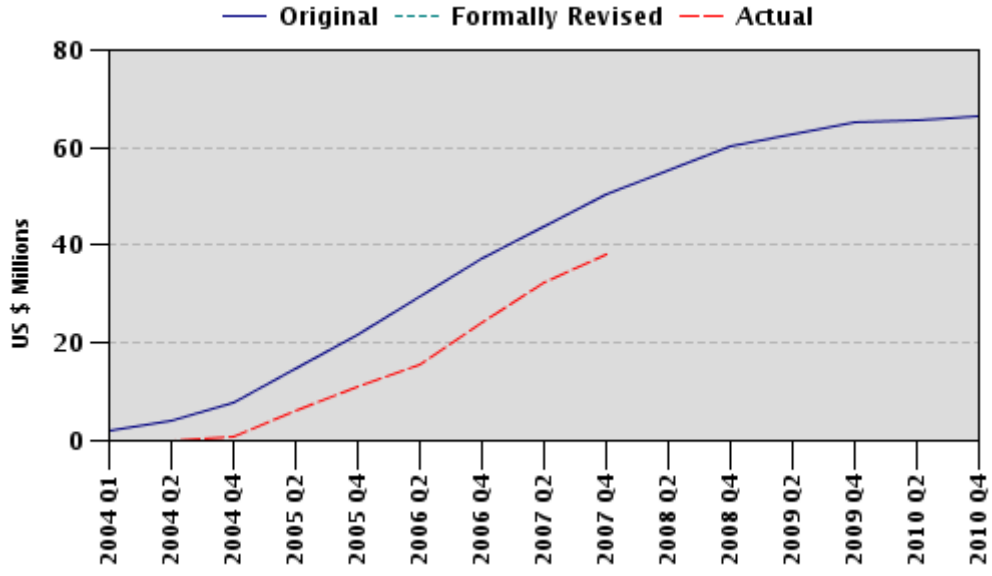

Project Name (ID): Jiangxi Integrated Agric. Modern. (P065463)

Country: China

Board Approval Date : 11/20/2003

Closing Date : 06/30/2010

Loan/Credit/Grant Number : JPN-26208, IBRD-47200

Sector(s): Irrigation and drainage(50%), Agricultural extension and research(15%),
Agricultural marketing and trade(15%), Animal production(10%), Crops(10%)

Theme(s): Rural services and infrastructure(P), Rural markets(P), Other rural
development(P)

Project Development Objectives:

The objective of the project is to improve the livelihoods of rural households in project counties in Jiangxi Province by establishing integrated, economically and environmentally sustainable market-driven agricultural production systems focusing on productivity and agricultural output of high quality and value.

Progress toward achieving development objective(s):


Project implementation progress has improved significantly, with about 40% of the project completed at mid-year. However, progress is still behind schedule. Emphasis is being put on completing the farm-level irrigation and drainage works that will allow improved agricultural production. Once these works are completed, the impact can be demonstrated in agricultural activities. A Mid-term Review will take place in August 2007 to address bottle-necks for the successful completion of the project.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26208	Closed	0.50	0.50	0.00	0.00
IBRD-47200	Effective	100.00	35.92	64.08	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

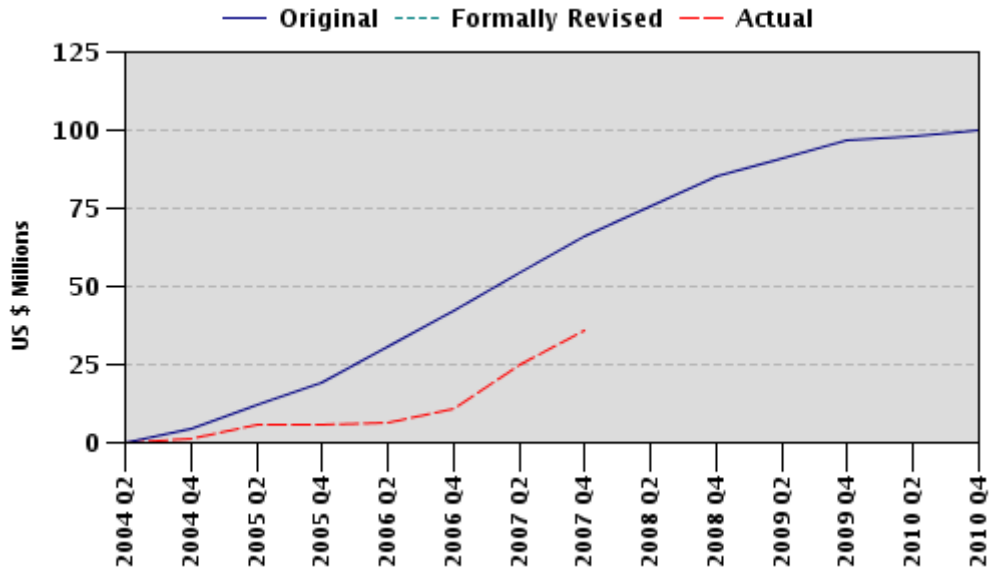

Project Name (ID): ZHEJIANG URBAN ENVMT (P066955)

Country: China

Board Approval Date : 01/29/2004

Closing Date : 06/30/2010

Loan/Credit/Grant Number : JPN-26241, IBRD-47240, JPN-26849

Sector(s): Sewerage(35%), Roads and highways(25%), Other social services(25%), Solid waste management(10%), Water supply(5%)

Theme(s): Municipal governance and institution building(P), Pollution management and environmental health(P), Access to urban services and housing(P), Infrastructure services for private sector development(S), Other urban development(S)

Project Development Objectives:

To enhance the efficiency and equity of waste management in Ningbo (wastewater)and Hangzhou (solid waste) municipalities and the redevelopment of the historic inner city of Shaoxing and Cicheng.

Progress toward achieving development objective(s):


Good progress was made in fiscal year 2007 towards the project's development objective of improved sustainability, efficiency and equity of urban development. Physical implementation in all three project cities is progressing well. The redevelopment of the historic inner city of Shaoxing is advanced while corresponding developments under the project in Cicheng are slower. Physical implementation at the Hangzhou landfill is at an advanced stage, but institutional and financial reforms are slow. The wastewater tariff was recently increased in Ningbo. The project has significant loan savings because some implementation was own-financed and because of procurement savings. Plans to use the savings to deepen the achievement of the project's objectives have been drawn up and are currently under review.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26241	Closed	0.50	0.50	0.00	0.00
IBRD-47240	Effective	133.00	42.66	90.34	0.00
JPN-26849	Closed	0.79	0.79	0.00	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

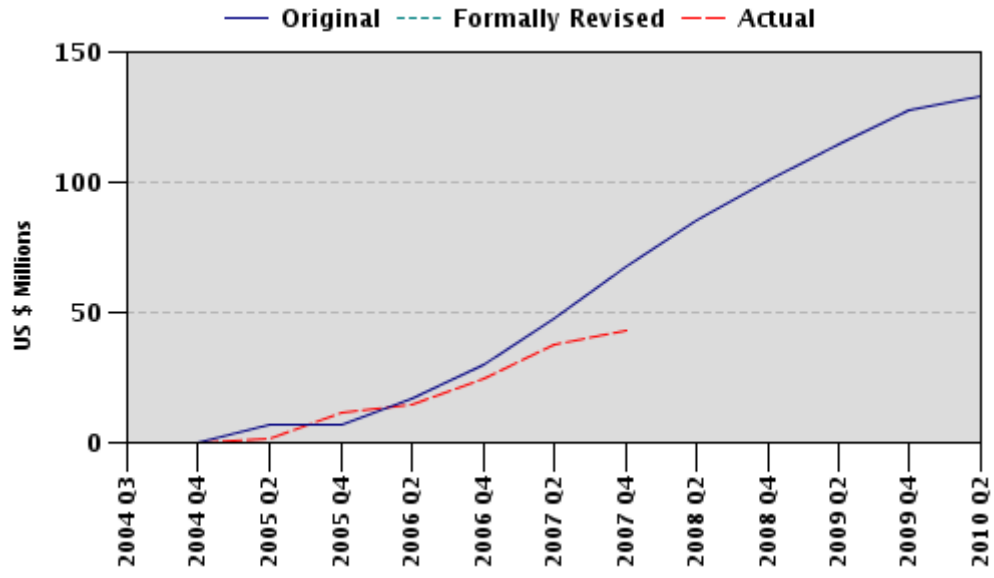

Project Name (ID): 2nd GEF Energy Conservation (P067337)

Country: China

Board Approval Date : 10/24/2002

Midterm Review Date : 05/22/2006

Closing Date : 06/30/2010

Loan/Credit/Grant Number : MULT-51678

Sector(s): District heating and energy efficiency services(91%), Non-compulsory pensions, insurance and contractual savings(7%), Central government administration(2%)

Theme(s): Climate change(P), Pollution management and environmental health(P), Other financial and private sector development(S)

Project Development Objectives:

To expand domestic investment in energy efficiency projects through the aggressive development of China's nascent Energy Management Company (EMC) industry, thereby achieving large-scale energy efficiency improvements and associated reductions in the growth of carbon dioxide emissions and other pollutants.

Progress toward achieving development objective(s):


The project continues to make very good progress in achieving its development objectives of major energy savings from the development and expansion of the energy performance contracting industry in China. The energy performance contracting investment by Chinese companies amounted to US\$246 million in 2005, now ranking among the highest in the world. These investment will provide energy savings of about 18.0 million tons standard coal over the lifetime of the assets created, and a reduction of about 10.8 million tons of carbon emissions. These achievements far exceed original targets for this phase of the project.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-51678	Effective	26.00	18.43	7.57	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

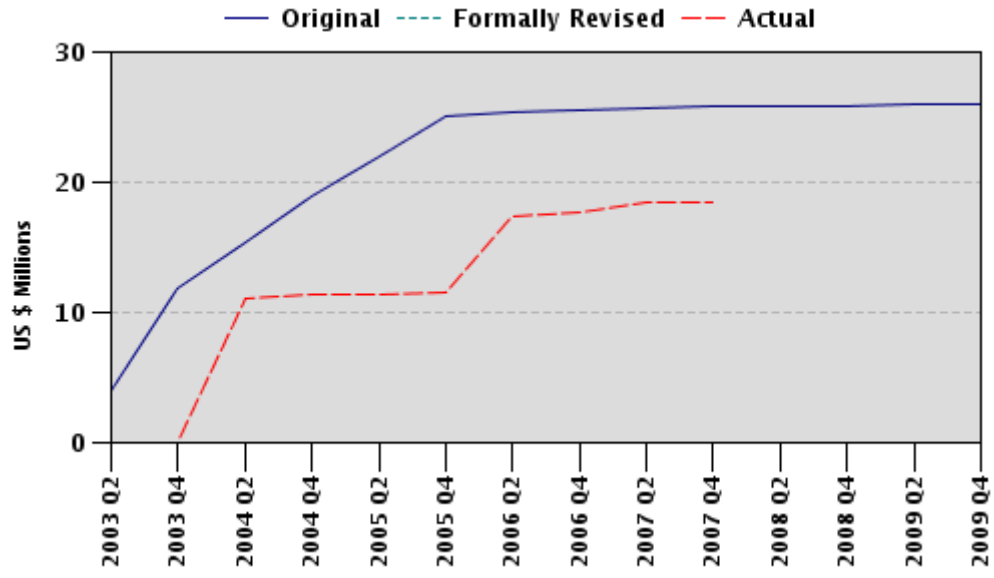

Project Name (ID): Renewable Energy Scale-up Program (P067828)

Country: China

Board Approval Date : 06/16/2005

Closing Date : 09/30/2010

Loan/Credit/Grant Number : JPN-26384, IBRD-47920

Sector(s): Renewable energy(100%)

Theme(s): Environmental policies and institutions(P), Climate change(P), Infrastructure services for private sector development(P), Rural services and infrastructure(S)

Project Development Objectives:

The program objective is to enable commercial renewable electricity suppliers to provide energy to the electricity market efficiently, cost-effectively, and on a large scale. The first phase of the program is to: create a legal, regulatory, and institutional environment conducive to large-scale, renewable based electricity generation; and demonstrate early success in large-scale renewable energy development with participating local developers in two provinces.

Progress toward achieving development objective(s):


Good progress on the investment projects, which are set to meet their DO satisfactorily, and possibly earlier than expected. Although there are delays in the implementation of the Institutional Development and Capacity Building Component, there are several actions being taken which underline government commitment to achieving the development objective on the legal and regulatory side.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26384	Closed	0.46	0.46	0.00	0.00
IBRD-47920	Effective	87.00	67.62	19.38	10.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

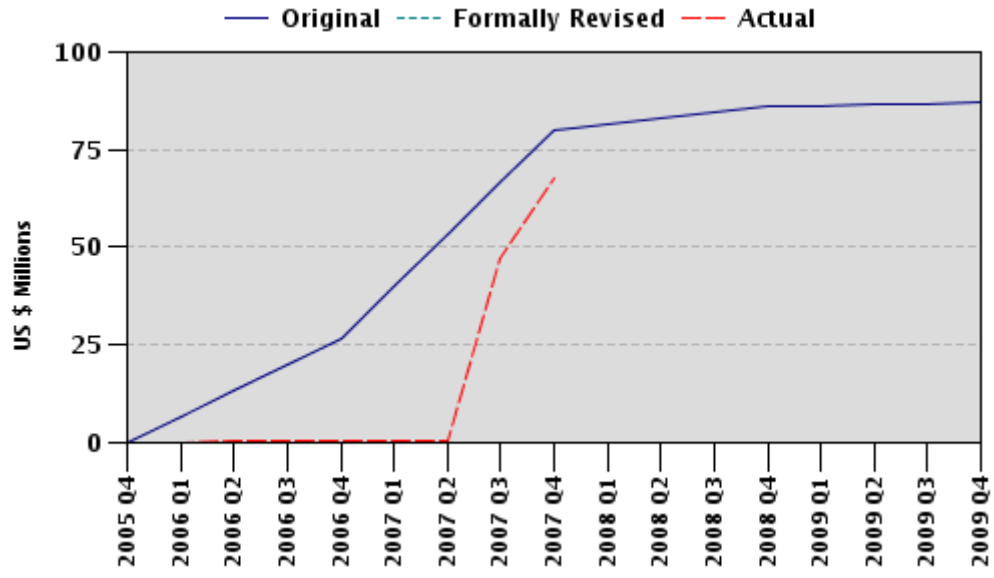

Project Name (ID): Hubei Hydropower Development in Poor Areas (P068049)

Country: China

Board Approval Date : 06/25/2002

Closing Date : 12/31/2008

Loan/Credit/Grant Number : IBRD-46660, JPN-26234, MULT-56753

Sector(s): Power(97%), Other social services(3%)

Theme(s): Infrastructure services for private sector development(P), Pollution management and environmental health(P), Rural services and infrastructure(P), Poverty strategy, analysis and monitoring(P), Other social development(S)

Project Development Objectives:

The project has three objectives: (a) facilitate economic growth in Hubei by expanding electric power generation capacity in an economically and environmentally sustainable manner; (b) enhance the efficiency of the electricity sector in Hubei by commercializing county generation companies; and (c) contribute to poverty alleviation efforts in poor communities in Hubei.

Progress toward achieving development objective(s):


Project implementation is progressing smoothly. Dongping and Songshuling have successfully commissioned the targeted renewable energy generation capacity. Although the other two sub-projects will have delayed commissioning of units, it is likely that the projects will deliver more than targeted renewable energy generation capacity. Project companies were established under the Chinese Company Law and are functioning properly in project financing, implementation. All relevant legal arrangements have been completed. Capacity building program for future plant operation are in progress. County Governments have committed 20% of future fiscal revenues from the Project be earmarked for contribution of poverty alleviation funds; and Bank financed TA on poverty alleviation planning was completed satisfactorily.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46660	Effective	105.00	89.06	15.94	0.00
JPN-26234	Closed	0.66	0.66	0.00	0.00
MULT-56753	Effective	4.61	0.40	4.21	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

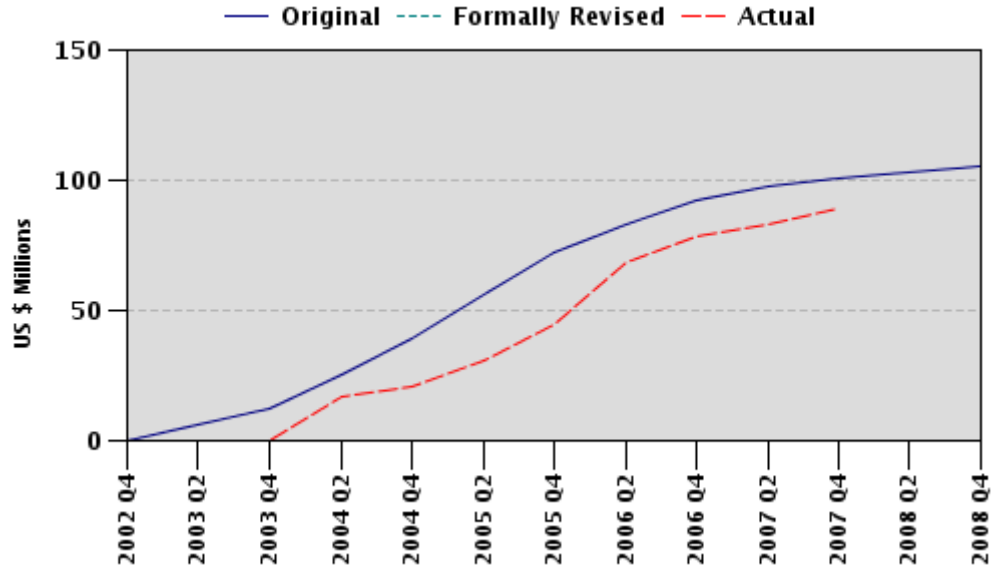

Project Name (ID): Yixing Pumped Storage Project (P068058)

Country: China

Board Approval Date : 03/20/2003

Closing Date : 12/31/2009

Loan/Credit/Grant Number : IBRD-46860, JPN-26238

Sector(s): Power(97%), Sub-national government administration(3%)

Theme(s): Infrastructure services for private sector development(P), Regulation and competition policy(P)

Project Development Objectives:


The proposed project is to increase the overall efficiency of the power sector in Jiangsu Province in two ways: (a) through the design and implementation of a far-reaching restructuring of the sector to further competition at the generation level and to provide large consumers access to generators; (b) through the construction of a pumped storage plant and associated transmission in Yixing to ease acute peaking problems and improve generation mix that would create the conditions for more flexible dispatch and improved supply reliability, an essential requirement for well-functioning competitive markets.

Progress toward achieving development objective(s):

The project construction progress and the overall project management (including environmental and social management) continue to be satisfactory. It's expected that the project development objectives will be achieved.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46860	Effective	145.00	85.39	59.61	0.00
JPN-26238	Closed	0.48	0.48	0.00	0.01

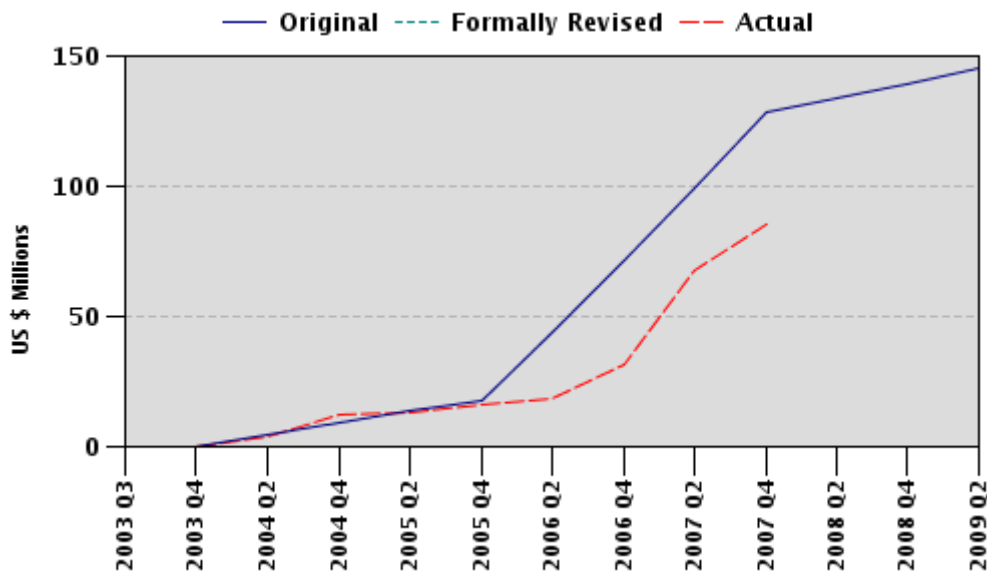

Project Name (ID): Inner Mongolia Highway and Trade Corridor (P068752)

Country: China

Board Approval Date : 02/15/2005

Closing Date : 06/30/2010

Loan/Credit/Grant Number : IBRD-47650

Sector(s): Roads and highways(99%), Sub-national government administration(1%)

Theme(s): Trade facilitation and market access(P), Administrative and civil service reform(S)

Project Development Objectives:


The main objective of the project is to sustain and promote the development of cross-border trade between China on one hand and Russia and Mongolia on the other by improving transport infrastructure and logistics. These improvements, in turn, will lower transport costs, increase income from external trade, and raise incomes in Inner Mongolia, the country's third-largest province and one of the poorest provinces of the western region.

Progress toward achieving development objective(s):

The project is still at an early stage of implementation. There is significant progress in most components and no major problems that would have significant impact on the likelihood of achieving the project development objective.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47650	Effective	100.00	23.07	76.93	0.00

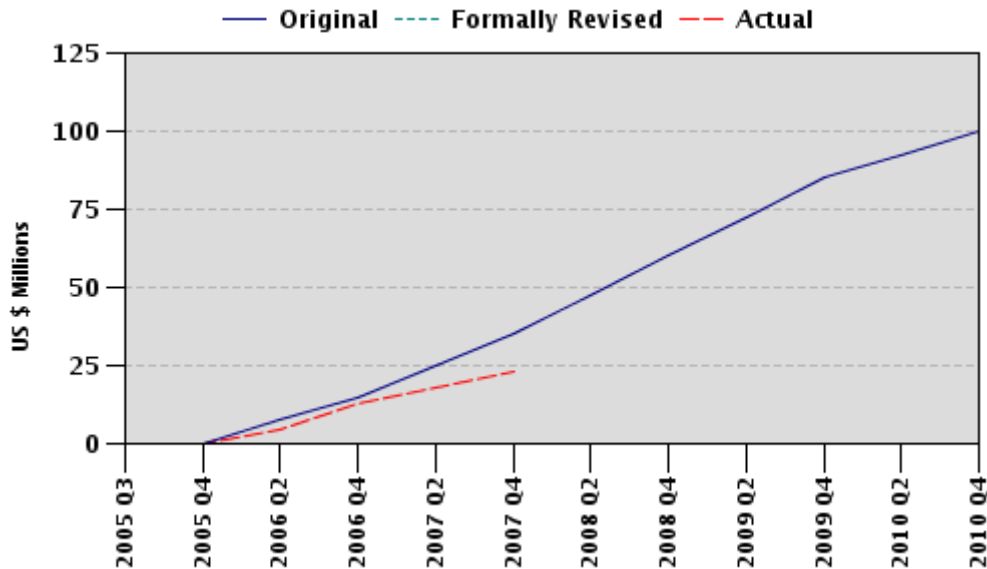

Project Name (ID): Wuhan Urban Transport (P069852)

Country: China

Board Approval Date : 03/09/2004

Closing Date : 06/30/2009

Loan/Credit/Grant Number : JPN-26239, IBRD-47270

Sector(s): General transportation sector(96%), Sub-national government administration(4%)

Theme(s): Access to urban services and housing(P), Other urban development(P), Municipal governance and institution building(S), Pollution management and environmental health(S), Injuries and non-communicable diseases(S)

Project Development Objectives:


To promote development of an integrated, efficient, and sustainable transport system for the rapid, safe and convenient movement of people and goods in Wuhan.

Progress toward achieving development objective(s):

Wuhan is making good progress with implementation of investments. Several of the TA which contributes to the PDO is under way including the urban transport strategy and the public transport reform. To address the current system efficiency as stated in the PDO, Wuhan is implementing exclusive bus lanes on a pilot basis under this project. At this point, the likelihood of achieving the PDOs is high.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26239	Closed	0.76	0.73	0.00	0.02
IBRD-47270	Effective	200.00	104.94	94.06	1.00

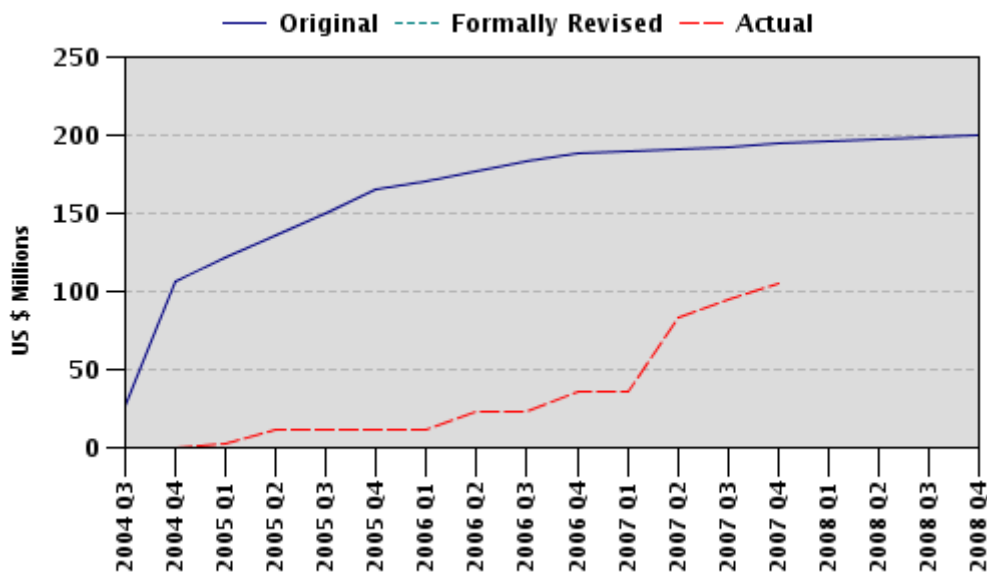

Project Name (ID): Agricultural Technology Transfer (P069862)

Country: China

Board Approval Date : 04/28/2005

Closing Date : 12/31/2010

Loan/Credit/Grant Number : JPN-26377, IBRD-47730

Sector(s): Agricultural extension and research(45%), Agricultural marketing and trade(25%), Agro-industry(20%), Information technology(5%), Other social services(5%)

Theme(s): Rural policies and institutions(P), Rural services and infrastructure(P), Other rural development(S), Export development and competitiveness(S)

Project Development Objectives:

The objective of the project is to develop and test innovative models for agricultural technology transfer and application aimed to generate additional farm income in high-value markets with a potential for scaling up. The project aims to give poor farmers the opportunity to participate in high-value agricultural markets both domestically and internationally.

Progress toward achieving development objective(s):


The project has launched 49 sub-projects that cover many different areas of agriculture and agribusiness and are making good progress. The types of innovations being tested include the introduction of both technical and institutional innovations. For example, the project has several sub-projects that allow small dairy, pork and poultry farmers to adopt higher production standards and to aggregate product, through technical and organizational changes, that allow them to share large-scale facilities. The project has also introduced commercial farmers' associations to many areas. New technologies have been introduced including mushroom farming, goat and dairy cattle breeding programs, pesticide residue testing for fresh products, hybrid seed production, and organic meat production.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26377	Closed	0.26	0.00	0.00	0.26
IBRD-47730	Effective	100.00	16.14	83.86	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

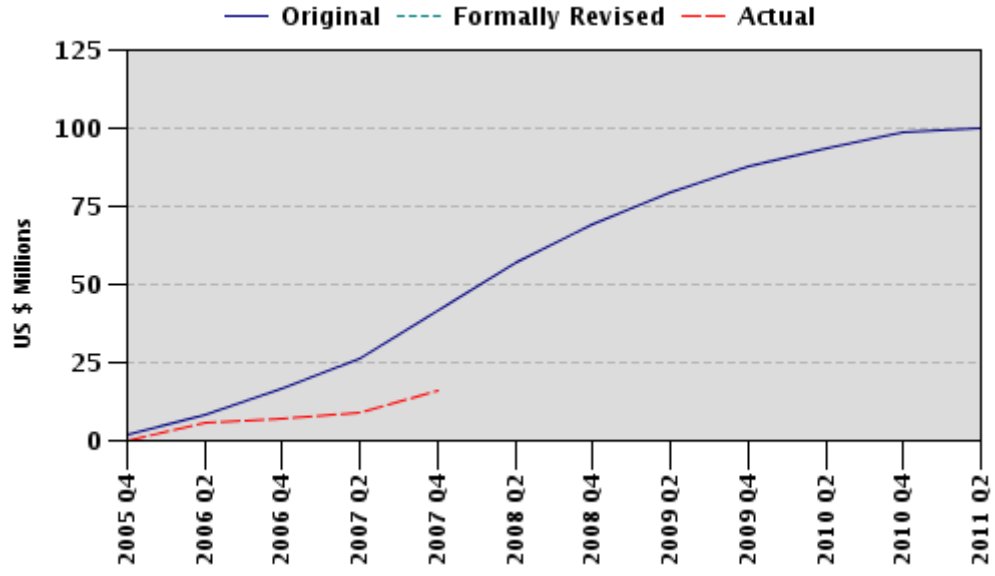

Project Name (ID): SHANGHAI URB ENVMT APL1 (P070191)

Country: China

Board Approval Date : 06/17/2003

Closing Date : 03/31/2009

Loan/Credit/Grant Number : JPN-26236, IBRD-47050

Sector(s): Sewerage(73%), Solid waste management(20%), Sub-national government administration(7%)

Theme(s): Other urban development(P), Pollution management and environmental health(P), Access to urban services and housing(P), Environmental policies and institutions(P)

Project Development Objectives:

(a) To put in place some of the underpinnings and enabling conditions to pursue an integrated, metropolitan-wide approach for managing the urban environment; (b) to install, in both the city center and districts, facilities already known to be high priority to achieve metropolitan-wide environmental objectives.

Progress toward achieving development objective(s):


Progress has been steady toward meeting the objectives. Work on the infrastructure necessary to upgrade the urban environment is well underway. The Zhu Yuan wastewater treatment plant was scheduled for commissioning in June 2007 and the twin tunnel outfall construction is nearing completion. The Phase IV Laogang landfill is receiving 8000 tons of solid waste daily and additional cells are almost complete. A few issues with construction quality at the leachate treatment plant are being addressed. Work on the urban planning and upgrading component is also advancing and will benefit some 200,000 people in dense, low-income areas. The institutional strengthening component remains somewhat behind schedule, and needs to be accelerated, particularly to fully meet objective (a).

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26236	Closed	0.99	0.99	0.00	0.00
IBRD-47050	Effective	200.00	102.11	97.89	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

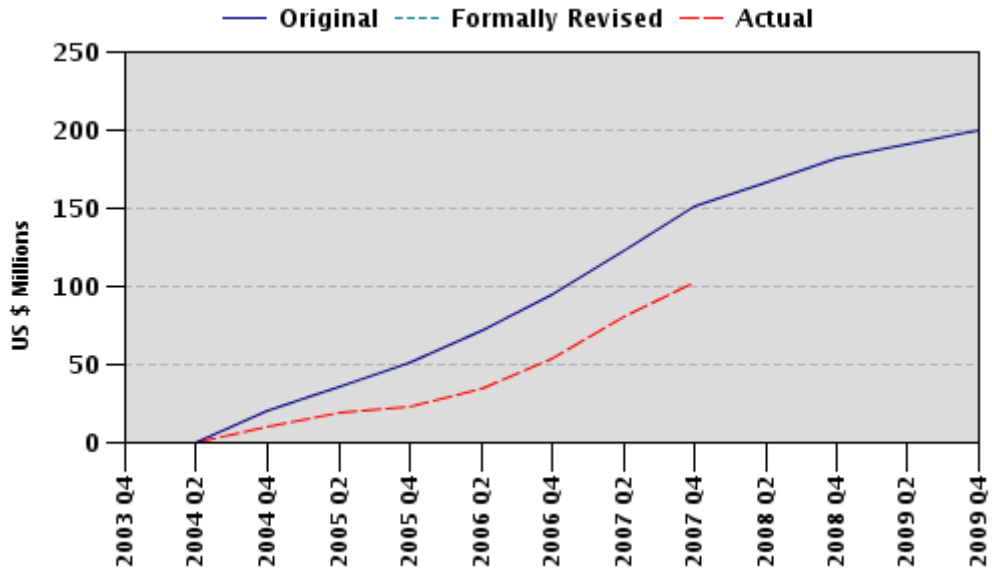

Project Name (ID): Hubei Xiaogan Xiangfan Hwy (P070441)

Country: China

Board Approval Date : 09/17/2002

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IBRD-46770

Sector(s): Roads and highways(90%), Sub-national government administration(10%)

Theme(s): Infrastructure services for private sector development(P), Municipal governance and institution building(S), Rural services and infrastructure(S)

Project Development Objectives:


To provide a more effective, safe and efficiently managed transport infrastructure to sustain and support socio-economic development, trade, and regional integration in Hubei province and to improve transport links to lagging western regions.

Progress toward achieving development objective(s):

The project is on track to meet its development objectives. The expressway opened in September 2005 and the quality is good. The safety problems on the interconnecting roads have been resolved to the Bank's satisfaction. The institutional development and road sector management activities are largely completed and have had useful results.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46770	Effective	250.00	214.45	35.55	0.00

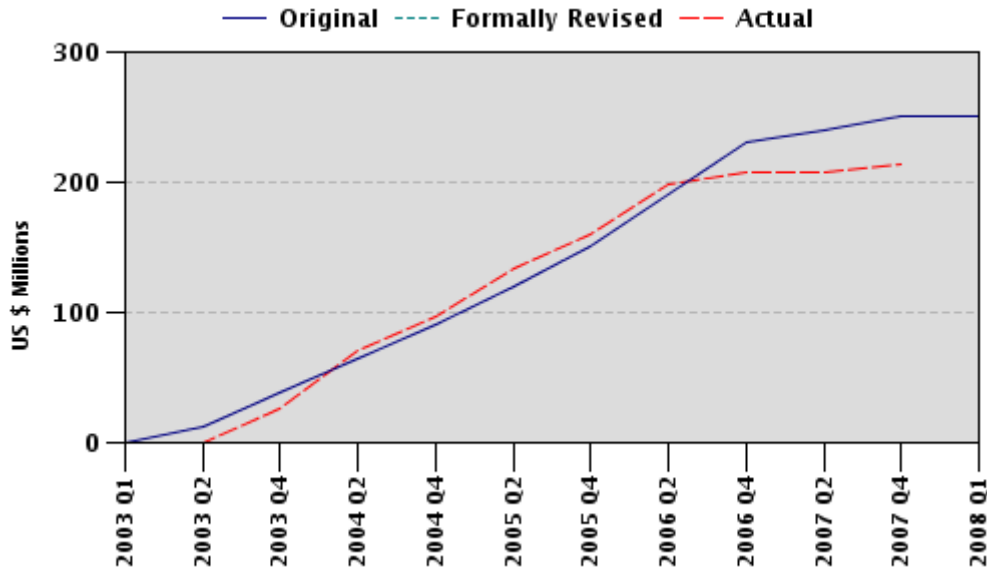

Project Name (ID): Inner Mongolia Hwy Project (P070459)

Country: China

Board Approval Date : 06/06/2002

Closing Date : 03/31/2008

Loan/Credit/Grant Number : IBRD-46630

Sector(s): Roads and highways(99%), Sub-national government administration(1%)

Theme(s): Infrastructure services for private sector development(P), Rural services and infrastructure(P), Regional integration(P), Trade facilitation and market access(S)

Project Development Objectives:


The project aims to improve the efficiency, safety, and cost-effectiveness of the transport infrastructure to support the social and economic development of the Inner Mongolia Autonomous Region, and to improve accessibility to its poorer areas thus reducing social and economic disparity within the region.

Progress toward achieving development objective(s):

Project is highly likely to achieve the development objective with most of the targeted results already reached or even exceeded.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-46630	Effective	100.00	79.67	20.33	0.00

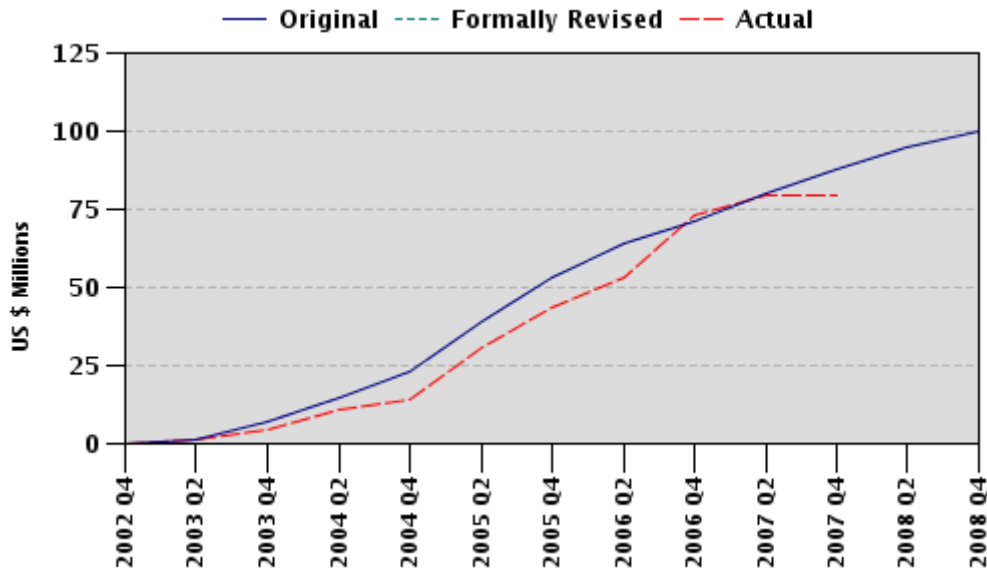

Project Name (ID): Fuzhou Nantai Island Peri-Urban Development (P070519)

Country: China

Board Approval Date : 12/15/2005

Closing Date : 06/30/2011

Loan/Credit/Grant Number : IBRD-48120

Sector(s): Roads and highways(87%), General transportation sector(10%), Sub-national government administration(3%)

Theme(s): Other urban development(P), Environmental policies and institutions(S), Pollution management and environmental health(S), Injuries and non-communicable diseases(S)

Project Development Objectives:


The objective of the project is to support sustainable peri-urban development in Fuzhou (as it expands to include Nantai Island) by providing strategic transport infrastructure and by strengthening the city’s decision support system on land development and management.

Progress toward achieving development objective(s):

The Loan was declared effective on February 16, 2007. Project disbursements are behind schedule due to the delay in the signing of the Loan documents. Discussions on both physical and institutional strengthening components are proceeding as expected.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48120	Effective	100.00	0.25	99.75	0.00

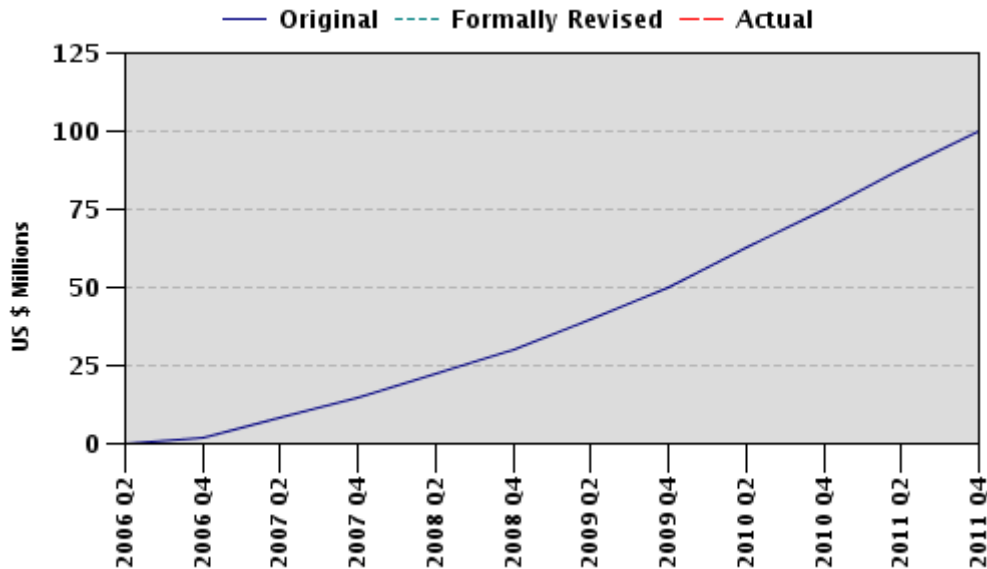

Project Name (ID): Poor Rural Communities Development (P071094)

Country: China

Board Approval Date : 06/21/2005

Closing Date : 12/31/2010

Loan/Credit/Grant Number : DF55699, IBRD-73100, JPN-26424, JPN-54747

Sector(s): General agriculture, fishing and forestry sector(65%), Roads and highways(13%), Sub-national government administration(10%), General water, sanitation and flood protection sector(6%), General education sector(6%)

Theme(s): Participation and civic engagement(P), Rural services and infrastructure(P), Other rural development(P), Indigenous peoples(P), Education for all(S)

Project Development Objectives:

The objective is to improve the security of livelihoods and to achieve the sustained participation of the poorest rural people in project design, implementation, and monitoring and evaluation, in eighteen counties of the three provinces.

Progress toward achieving development objective(s):


Implementation during the project's first eighteen months is on the right track and is accelerating. The positive impact of the successful rollout of the participatory approach is evident in each of the three project provinces, and project plans have been kept flexible enough to accommodate beneficiaries' changing demands. The most significant challenge at present is that counterpart funding and other constraints have undermined the project's ability to provide the forms of assistance (primarily roads, drinking water supply, and other basic rural infrastructure) that are most strongly favored by the poor. This challenge is greatest in those project counties with the highest concentrations of the most severely-disadvantaged ethnic minority people.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
DF55699	Effective	2.21	0.35	1.84	0.00
IBRD-73100	Effective	100.00	15.07	84.93	0.00
JPN-26424	Closed	0.54	0.54	0.00	0.00
JPN-54747	Effective	1.93	0.37	1.55	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

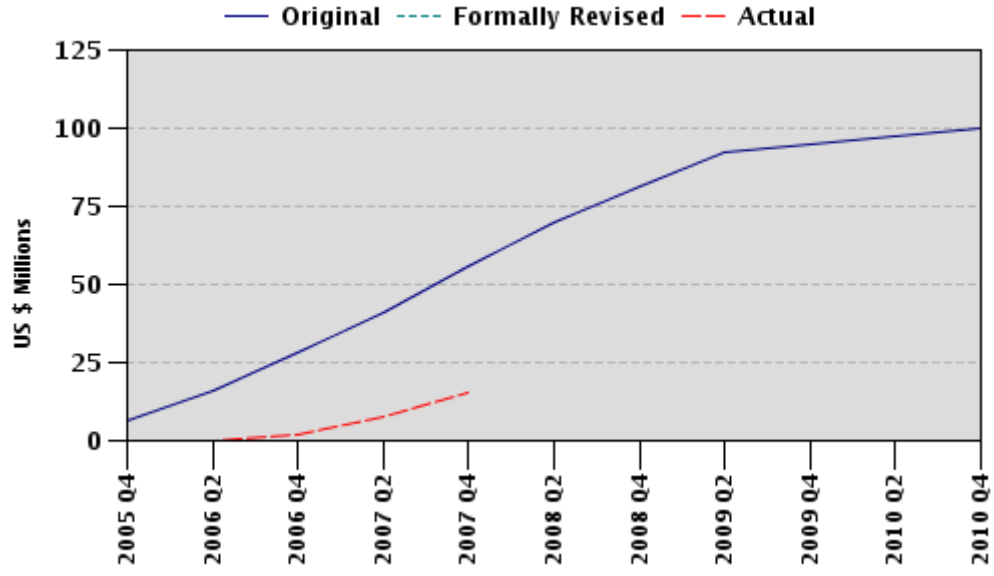

Project Name (ID): Tuberculosis Control Project (P071147)

Country: China

Board Approval Date : 03/21/2002

Midterm Review Date : 08/21/2006

Closing Date : 03/15/2010

Loan/Credit/Grant Number : JPN-26428, IBRD-71070

Sector(s): Health(93%), Sub-national government administration(7%)

Theme(s): Other communicable diseases(P), Child health(S), Rural services and infrastructure(S)

Project Development Objectives:


The project's main development objectives are to achieve 70% case detection rate for smear positive TB cases and 85% cure rate.

Progress toward achieving development objective(s):

The MTR found that not only had the development objectives been met at that point but even exceeded. The current focus of the project is to address new challenges such as the threat of Multiple Drug Resistance and more effectively reaching poor and remote populations.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26428	Closed	0.42	0.42	0.00	0.00
IBRD-71070	Effective	104.00	59.07	44.93	0.00

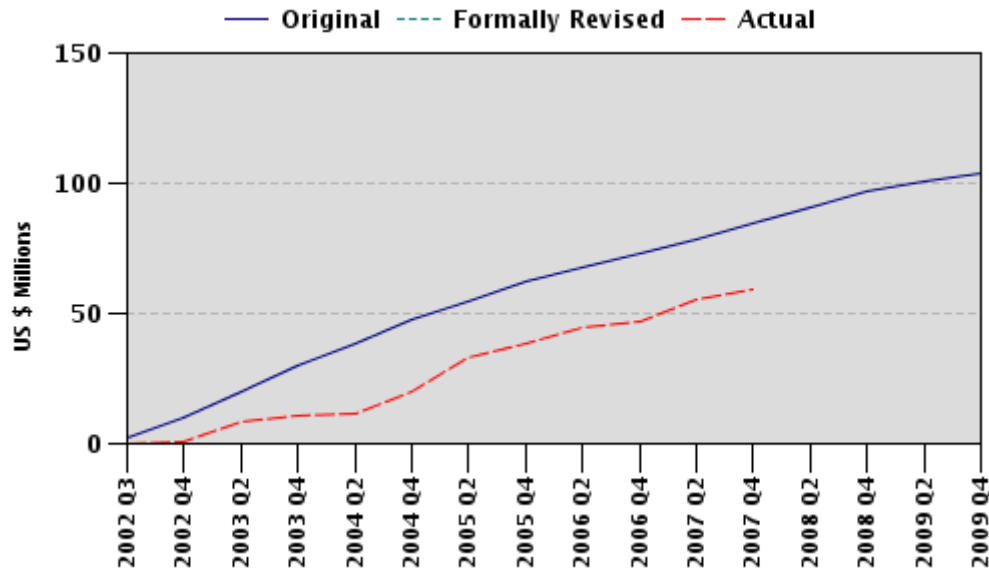

Project Name (ID): GEF-Heat Reform and Bldg Egy Eff. (P072721)

Country: China

Board Approval Date : 03/17/2005

Closing Date : 12/31/2011

Loan/Credit/Grant Number : MULT-51792, MULT-54687

Sector(s): Housing construction(40%), District heating and energy efficiency services(32%), Sub-national government administration(17%), Central government administration(11%)

Theme(s): Climate change(P), Municipal governance and institution building(S)

Project Development Objectives:

To achieve substantial, sustained and growing increases in energy efficiency in urban residential buildings and the heating systems in China's cold climate regions.

Progress toward achieving development objective(s):


Two demonstration projects in Tianjin, totaling about 300,000 m², have been completed. Consumption based-billing has been introduced at relatively large scale in Tianjin, first in China. Tianjin also began to implement a significantly more stringent building energy efficiency standards than the current national standards. A series of TAs have been launched, directly assisting the formulation of national heat reform policies as well as Tianjin's experiments. New project cities, including Dalian, Tangshan and Chengde have been launched. New demonstration projects and TAs in Tianjin, Dalian, Tangshan and Chengde are under preparation.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-51792	Closed	0.35	0.35	0.00	0.00
MULT-54687	Effective	18.00	3.05	14.95	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

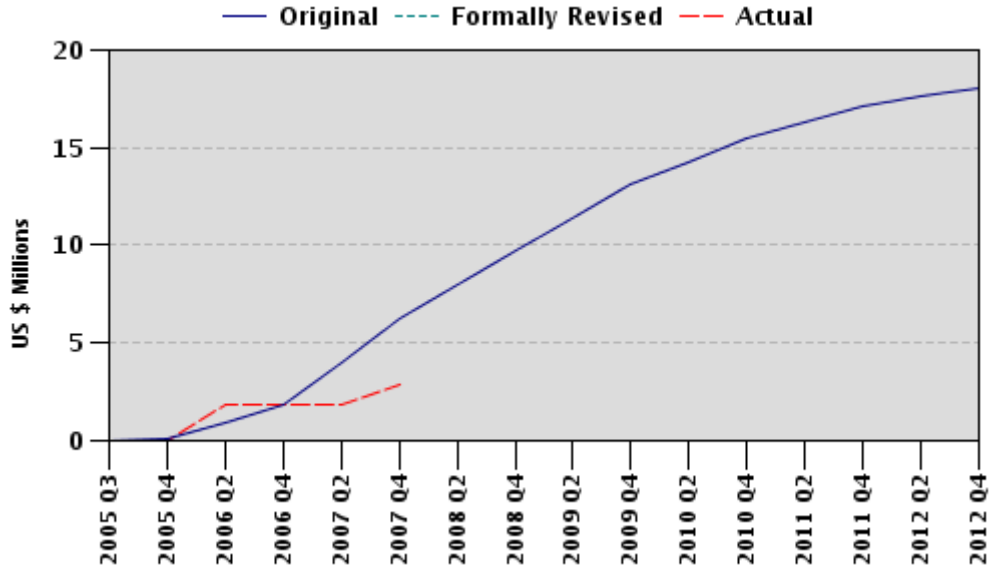

Project Name (ID): Basic Education in Western Areas (P073002)

Country: China

Board Approval Date : 09/09/2003

Midterm Review Date : 06/15/2007

Closing Date : 06/30/2009

Loan/Credit/Grant Number : JPN-26772, IBRD-71940

Sector(s): Primary education(95%), Sub-national government administration(3%),
Central government administration(2%)

Theme(s): Education for all(P), Participation and civic engagement(P), Gender(S),
Indigenous peoples(S), Rural services and infrastructure(S)

Project Development Objectives:

Project aims toward the improved access to and completion of affordable and quality basic education for poor boys and girls in over a hundred counties in Sichuan, Gansu, Yunnan Provinces, Ningxia Hui and Guangxi Zhuang Autonomous Regions. The project promotes greater community participation in the management of school and provides training to support the implementation of the new national curriculum.

Progress toward achieving development objective(s):


The project is on track to achieve its development objectives. The findings from the recent mid-term review indicate significant progress made in the reporting year and measured by the steady pace of implementation and marked improvement in key performance indicators. These input helped create a more conducive environment for teaching and learning in project supported schools. The key performance indicators have shown significant increase in primary and junior secondary enrolment rates, reduction in drop-out rates and considerable increase in primary and junior secondary completion rates across general cohorts and of the targeted student population in 5 project provinces. The feedback from stakeholders points to the progress in piloting school development planning, catalytic in fostering stakeholder participation and school-community partnership in school management and planning. The project has contributed to the shift toward student centered active learning and improved teacher performance in classroom.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-26772	Closed	0.51	0.51	0.00	0.00
IBRD-71940	Effective	100.00	59.35	40.65	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

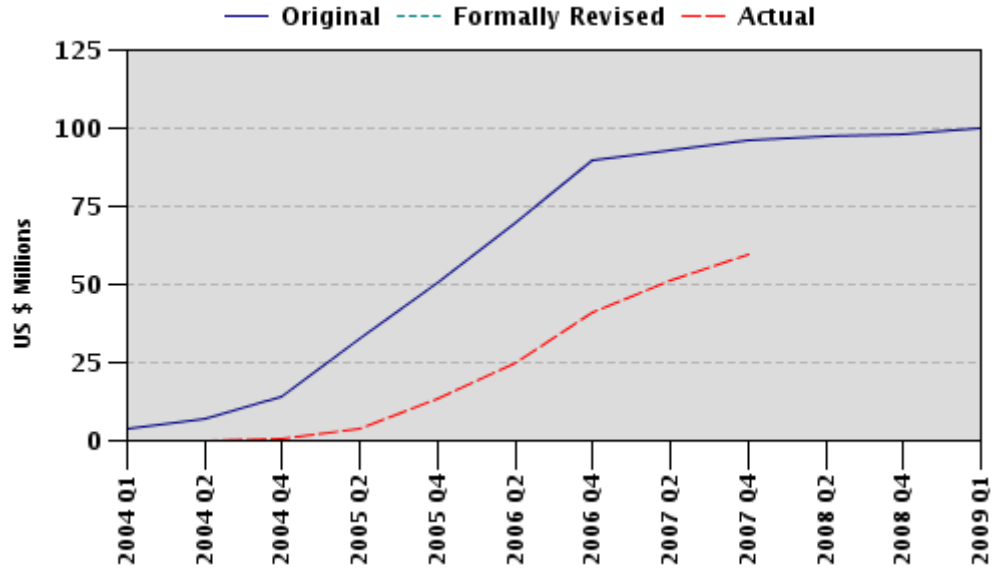

Project Name (ID): GEF-Hai Basin Integrated Water Environment Mgmt. (P075035)

Country: China

Board Approval Date : 04/15/2004

Closing Date : 06/30/2010

Loan/Credit/Grant Number : MULT-51398, MULT-53183

Sector(s): Sewerage(35%), Central government administration(35%), Sub-national government administration(15%), Irrigation and drainage(15%)

Theme(s): Water resource management(P), Pollution management and environmental health(P), Environmental policies and institutions(S)

Project Development Objectives:

The objective is to catalyze an integrated approach to water resource management and pollution control in the Hai Basin in order to improve the Bohai Sea environment by: (a) improving integrated water and environment planning and management in the Hai Basin; (b) supporting institutional aspects related to effective local, municipal/provincial and basin-wide water and environment planning and management; (c) enhancing capacity-building in water and environment knowledge management and implementation; and (d) reducing waste-water discharges from small cities.

Progress toward achieving development objective(s):


The project is being well implemented. The planned "top-down" and "bottom-up" approaches and vertical and horizontal integration have been followed in project implementation. The key start-up issues have been resolved, including the availability of counterpart funds, the understanding of the project concept and design, and cooperation between water and environment departments at various levels. Project outputs are expected to be completed as planned, and outcomes are to be produced throughout project implementation and beyond.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-51398	Closed	0.23	0.23	0.00	0.00
MULT-53183	Effective	17.00	5.48	11.52	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

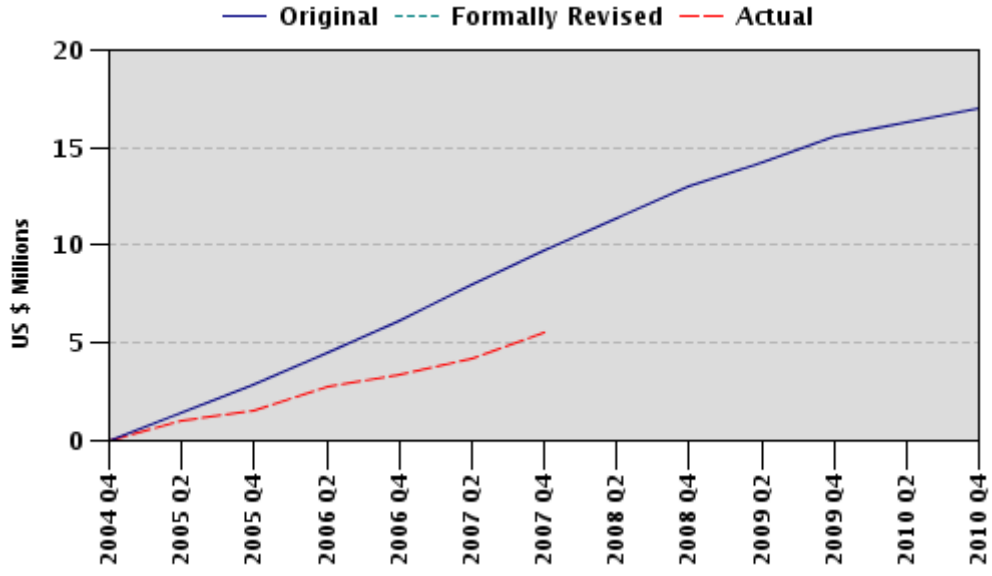

Project Name (ID): 2nd National Railways (Zhe-Gan Line) (P075602)

Country: China

Board Approval Date : 06/24/2004

Closing Date : 01/31/2008

Loan/Credit/Grant Number : IBRD-47460

Sector(s): Railways(99%), Central government administration(1%)

Theme(s): Infrastructure services for private sector development(P), Climate change(S)

Project Development Objectives:


To (a) improve services provided to customers of the Zhe-Gan railway line; and (b) upgrade the quality of track maintenance on heavily used portions of China Railways' network.

Progress toward achieving development objective(s):

The procurement of goods is nearly complete. It is highly likely that the service-related project development objective will be achieved after the electrification of the line has been fully commissioned and track machines are placed in service, though this cannot be confirmed until the operational indicators are available.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47460	Effective	200.00	193.90	5.10	1.00

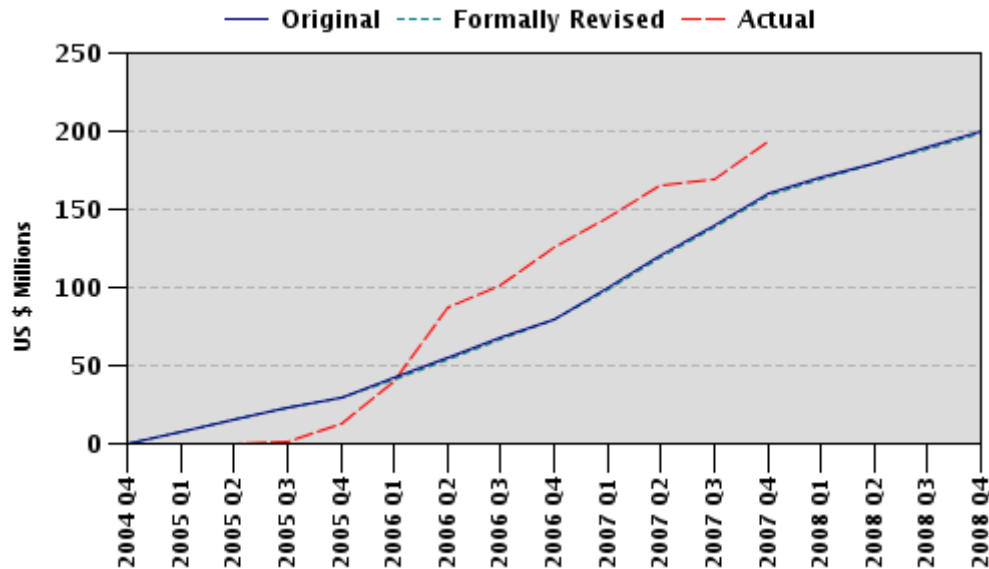

Project Name (ID): Shaanxi Ankang Road Development (P075613)

Country: China

Board Approval Date : 03/13/2007

Closing Date : 06/30/2012

Loan/Credit/Grant Number : IBRD-48530

Sector(s): Roads and highways(99%), Sub-national government administration(1%)

Theme(s): Infrastructure services for private sector development(P), Rural services and infrastructure(P), Injuries and non-communicable diseases(S), Administrative and civil service reform(S)

Project Development Objectives:

The objective of the Project is to assist the Borrower in improving passenger and freight traffic flows in an efficient and safe manner along the corridor from Ankang to Maoba in Shaanxi Province by: (i) enhancing road infrastructure capacity and network integration along the corridor Ankang-Maoba; (ii) increasing accessibility to markets and social services for the lower-income families in rural areas of Ankang; and (iii) strengthening Shaanxi Provincial Communications Department's capacity in managing the increasing number of kilometers of roads under its responsibility in the Shaanxi province and, in particular, within the Ankang region.

Progress toward achieving development objective(s):

The project was signed May 28, 2007. (The loan became effective on August 10, 2007.) Procurement processes were advanced during FY07 to move into full implementation during FY08.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48530	Not Effective	300.00	0.00	300.00	0.00



Project Name (ID): Guangdong/Pearl River Delta Urban Environment (P075728)

Country: China

Board Approval Date : 06/08/2004

Closing Date : 12/31/2009

Loan/Credit/Grant Number : IBRD-47420

Sector(s): Sewerage(88%), Solid waste management(7%), Sub-national government administration(5%)

Theme(s): Pollution management and environmental health(P), Other urban development(P), Other human development(S), Other financial and private sector development(S)

Project Development Objectives:

To improve the quality of the environment in key cities in the Pearl River Delta using an integrated regional planning approach to facilitate continued economic and social development.

Progress toward achieving development objective(s):


Progress toward building the infrastructure necessary to improve the quality of the environment is reasonably good. One wastewater treatment plant (WWTP) has been completed and put into operation, while a second is nearing completion. Networks to the WWTPs are not yet complete due to construction delays stemming from land acquisition and resettlement difficulties. Work on the hazardous waste component is much behind schedule due to inadequate counterpart funds, land acquisition delays and inattentive management. Detailed designs are now complete. Guangzhou Sewerage Treatment Company is considering a private operator for the Dashadi WWTP and has begun consultations on development of the management contract and process to follow. Under the Global Environment Facility Grant, two of the three subprojects to pilot inter-municipal cooperation in infrastructure provision have started, but a third remains pending.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47420	Effective	128.00	52.45	74.91	0.64



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

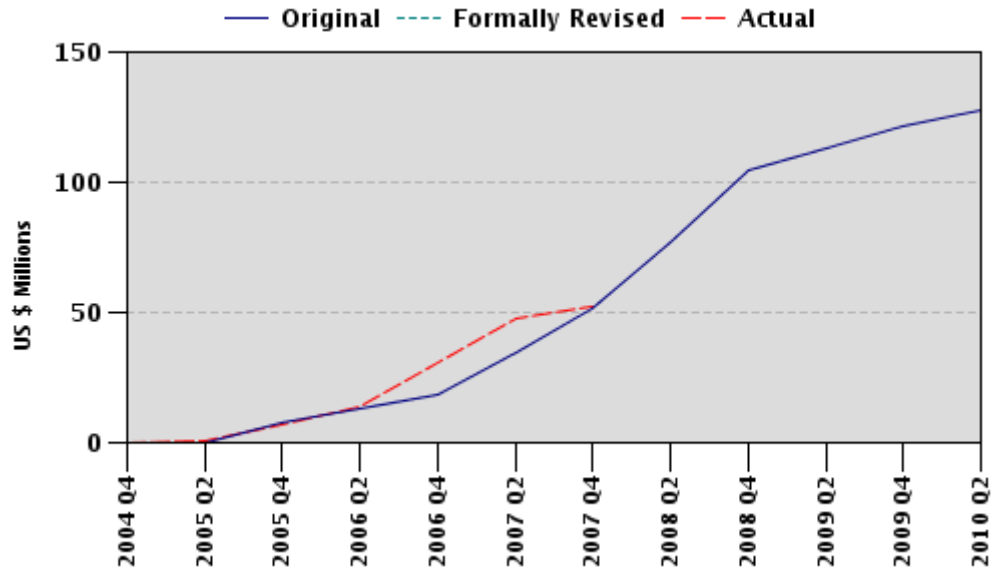

Project Name (ID): Hunan Urban Development (P075730)

Country: China

Board Approval Date : 09/16/2004

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-47510, JPN-50626

Sector(s): Flood protection(45%), Sewerage(27%), General transportation sector(20%), Mining and other extractive(5%), Other social services(3%)

Theme(s): Other urban development(P), Pollution management and environmental health(P), Climate change(S)

Project Development Objectives:


To foster greater integration in the Changsha-Zhuzhou-Xiangtan (CZT) Region of Hunan Province through priority investments addressing specific regional needs in a sustainable manner.

Progress toward achieving development objective(s):

Project implementation is in a difficult phase presently and progress toward meeting the objectives has been very slow. Complicated resettlement issues have arisen but progress in resolving them has been made. There have also been issues with compliance with the project legal documents related to a concession contract bid out in a non-competitive manner. Weak project management is also an issue. Nevertheless, Hunan and the city in question intend to continue with Bank financing of the project.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47510	Effective	172.00	11.94	160.06	0.00
JPN-50626	Closed	1.27	1.27	0.00	0.00

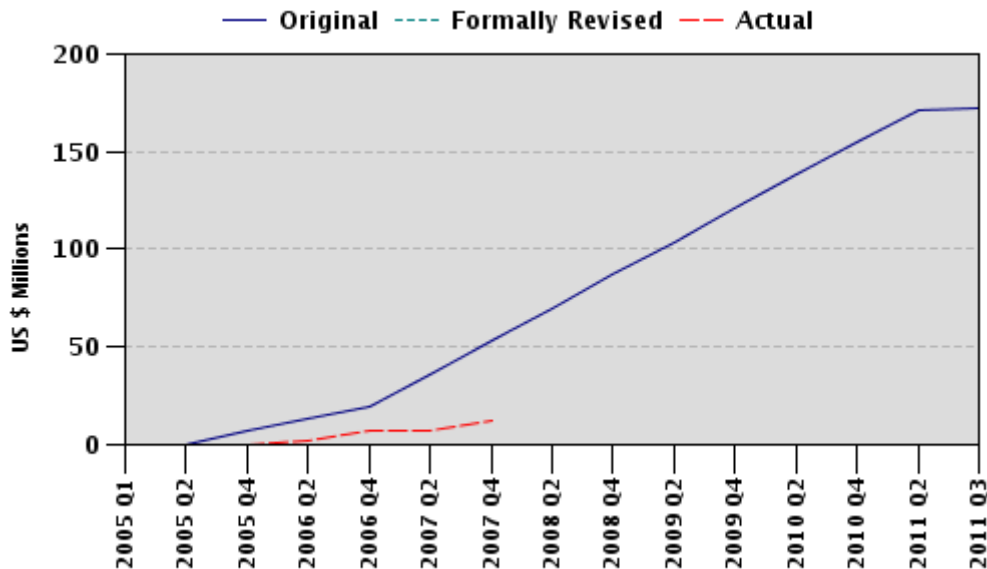

Project Name (ID): Shanghai Urban APL2 (P075732)

Country: China

Board Approval Date : 07/05/2005

Closing Date : 03/31/2011

Loan/Credit/Grant Number : IBRD-48010

Sector(s): Sewerage(50%), Water supply(20%), Sub-national government administration(20%), Solid waste management(10%)

Theme(s): Pollution management and environmental health(P), Access to urban services and housing(P), Other human development(P), Environmental policies and institutions(S), Municipal finance(S)

Project Development Objectives:

To expand Shanghai's environmental management agenda in the metropolitan area

Progress toward achieving development objective(s):


The project is making good progress toward meeting its objectives by improving environmental conditions with progressive development and implementation of integrated, metropolitan-wide measures, supported by large scale investments. Shanghai has completed the water supply investments, thereby strengthening the foundation of the Adaptable Program Loan (APL) concept, and has moved ahead rapidly with the APL's financial innovations. In the coming year, Shanghai should accelerate implementation of the wastewater collection and sludge management works. More attention to the institutional component is needed as well as a water tariff increase to ensure sustainability.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48010	Effective	180.00	30.21	149.79	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

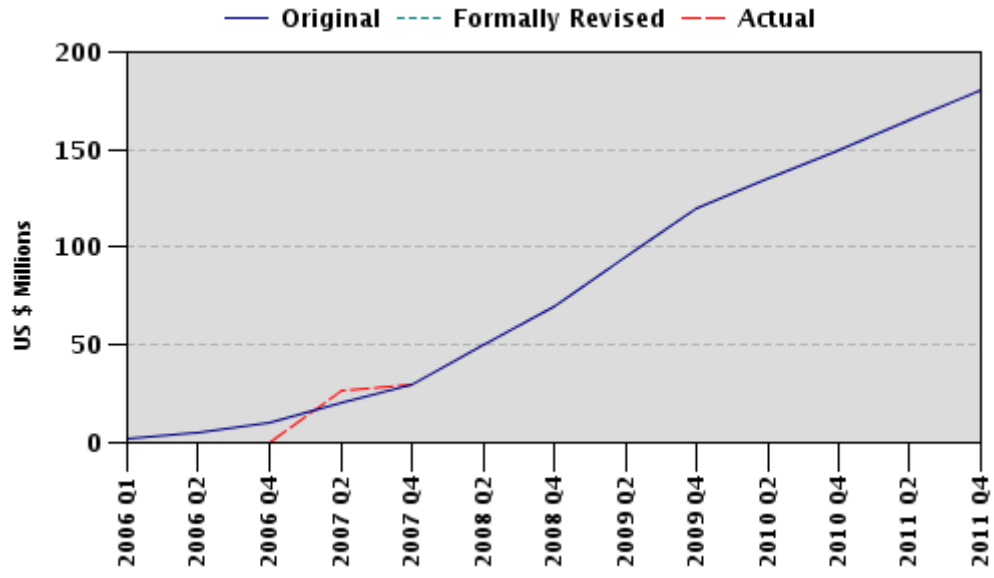

Project Name (ID): 2nd Anhui Highway (P076714)

Country: China

Board Approval Date : 06/24/2003

Closing Date : 06/30/2009

Loan/Credit/Grant Number : IBRD-71830

Sector(s): Roads and highways(80%), Sub-national government administration(20%)

Theme(s): Regional integration(P), Rural services and infrastructure(P), Other public sector governance(S), Export development and competitiveness(S)

Project Development Objectives:


The project aims to support the social and economic development of Anhui Province by providing an efficient, safe, and cost-effective highway infrastructure and to improve transport links.

Progress toward achieving development objective(s):

Project overall implementation continues to advance adequately. The delays experienced at the beginning of the project have been largely eliminated. The application of environmental and social safeguards has continued to be carried out according to initial plans and adequately. The implementing entity has increasingly adopted policies and actions on overloading as well as on road safety issues. New road management initiatives are being designed.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-71830	Effective	250.00	177.30	72.70	0.00

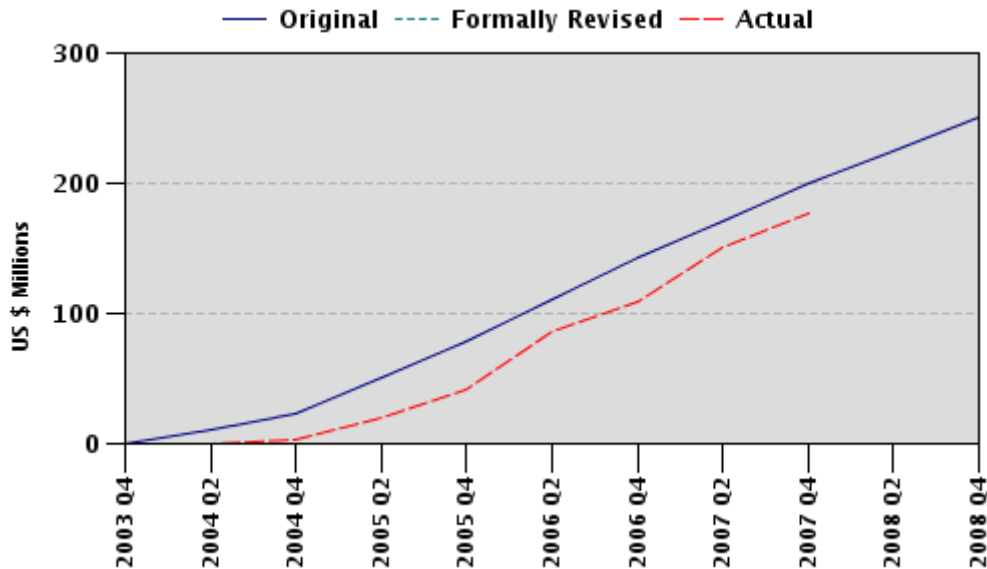

Project Name (ID): 4th Inland Waterways (P077137)

Country: China

Board Approval Date : 03/25/2004

Closing Date : 01/31/2010

Loan/Credit/Grant Number : IBRD-47280

Sector(s): Ports, waterways and shipping(65%), Renewable energy(15%), Power(10%), Sub-national government administration(10%)

Theme(s): Infrastructure services for private sector development(P), Water resource management(P), Rural services and infrastructure(S), Climate change(S)

Project Development Objectives:


To assist the Borrower in (1) improve access for poor regions of southern China by upgrading navigation conditions on the region's major east-west river and other waterways feeding traffic into the Pearl River Delta region; and (2)harness water flow in two of these rivers to generate environmentally clean electricity to help meet the growing energy demand in Guangdong and Guangxi.

Progress toward achieving development objective(s):

Project implementation is delayed for one year due to typhoon in July 2006, unforeseen geological conditions, and slow progress with some contracts. The first calendar year's project performance indicators, which was 2006, was evaluated and found to be satisfactory. Satisfactory progress has been made in TA and training. It remains likely, based upon the progress to date, that the development objective is achievable.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47280	Effective	91.00	32.99	57.55	0.46

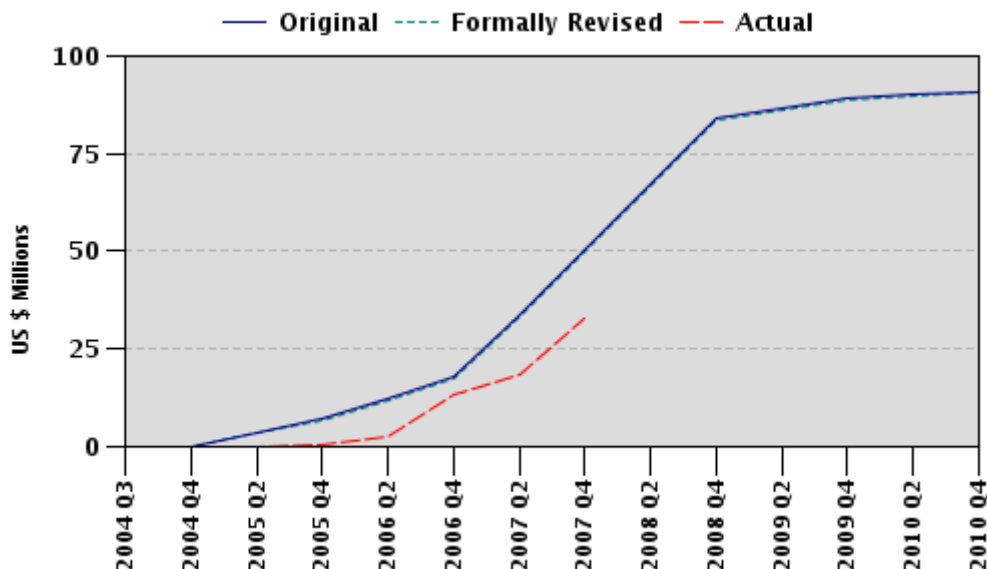

Project Name (ID): Shandong Environment 2 (P077752)

Country: China

Board Approval Date : 02/27/2007

Closing Date : 12/31/2013

Loan/Credit/Grant Number : IBRD-48520

Sector(s): Sanitation(77%), Water supply(13%), Solid waste management(9%), Sub-national government administration(1%)

Theme(s): Pollution management and environmental health(P), Water resource management(S)

Project Development Objectives:


To improve the environmental conditions in participating municipalities and counties

Progress toward achieving development objective(s):

The Loan has only recently become effective.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48520	Effective	147.00	0.00	147.00	0.00

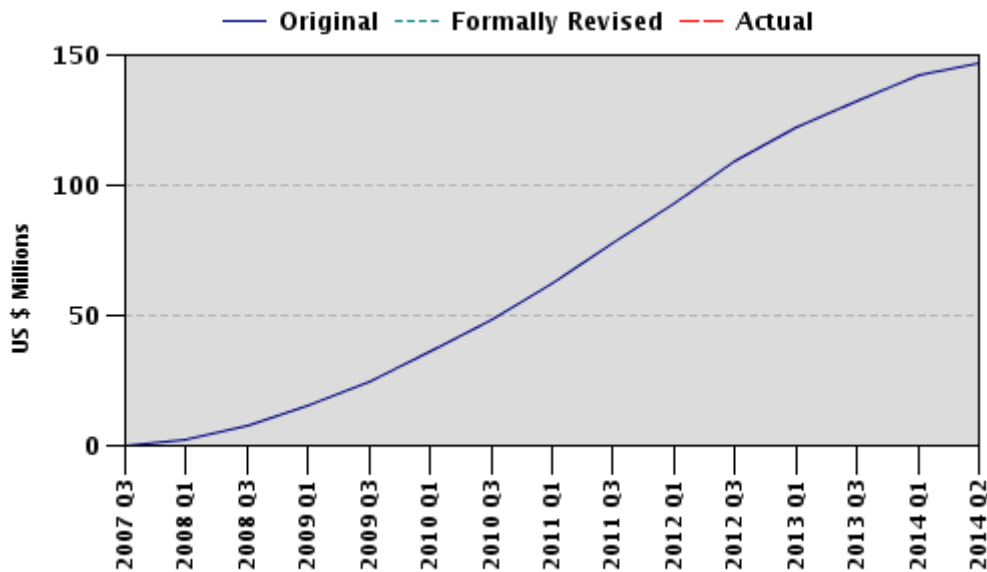

Project Name (ID): Chongqing Small Cities (P081161)

Country: China

Board Approval Date : 06/21/2005

Closing Date : 06/30/2012

Loan/Credit/Grant Number : IBRD-47940

Sector(s): Water supply(35%), Roads and highways(33%), Flood protection(21%), Sanitation(8%), Sub-national government administration(3%)

Theme(s): Access to urban services and housing(P), Other urban development(P), Other human development(S), Pollution management and environmental health(S), Natural disaster management(S)

Project Development Objectives:

To support emerging small cities to improve the efficiency and effectiveness of infrastructure service delivery, to accommodate the rapid urban growth

Progress toward achieving development objective(s):


The project is off to a good start toward meeting its objectives. All subsidiary loan agreements with the participating cities have been signed and a key consultancy for design, review and certification has been working well, with preliminary designs for 12 subprojects and nine bidding documents reviewed. Construction has commenced on 29 out of 46 contracts. These works will improve the efficiency and effectiveness of the cities' infrastructure. In addition, the institutional strengthening consultancy contract is under way, and the Western Chongqing water resource assessment and tariff study got under way in fiscal year 07, so all major studies are at least started and some completed. These should foster sustainable operations and growth.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47940	Effective	180.00	14.48	165.52	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

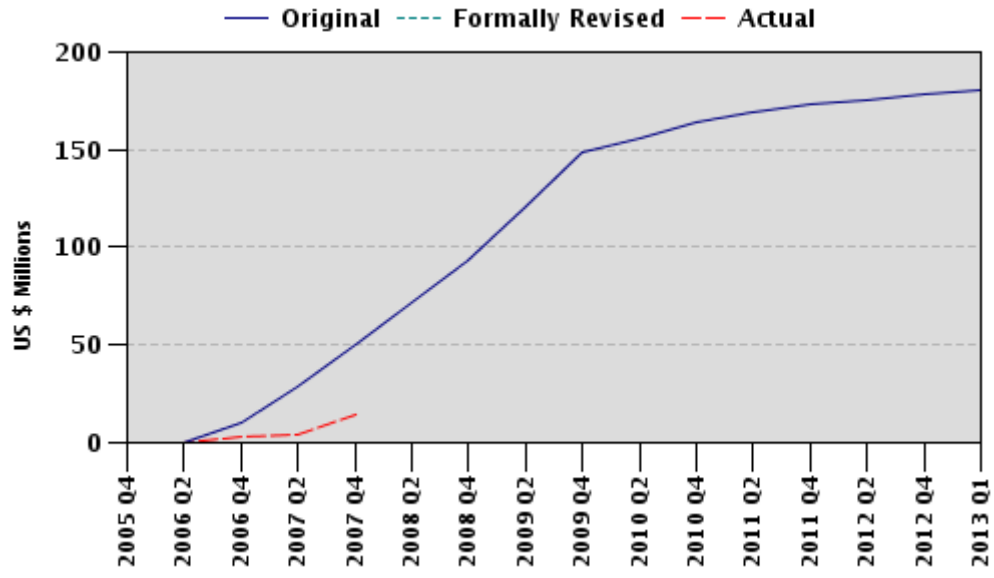

Project Name (ID): Changjiang/Pearl River Watershed Rehab (P081255)

Country: China

Board Approval Date : 06/27/2006

Closing Date : 06/30/2012

Loan/Credit/Grant Number : JPN-52802, IBRD-48320, EECT-57329

Sector(s): Forestry(23%), Crops(22%), Irrigation and drainage(20%), Animal production(20%), Flood protection(15%)

Theme(s): Other environment and natural resources management(P), Water resource management(S), Rural services and infrastructure(S), Land administration and management(S), Other rural development(S)

Project Development Objectives:


The objective is to improve the livelihood of farmers and to protect the environment in poor and highly-degraded watersheds of the Changjiang and Pearl River Basins.

Progress toward achieving development objective(s):

In each of the participating counties, implementation has started in one sub-watershed and participatory design is in progress in at least one other sub-watershed. The project has started broadly as planned, but it is too early to measure the actual impact of these mostly medium- to long-term investments.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-52802	Closed	0.50	0.50	0.00	0.00
IBRD-48320	Effective	100.00	2.25	97.75	0.00
EECT-57329	Effective	13.23	0.60	12.62	0.00

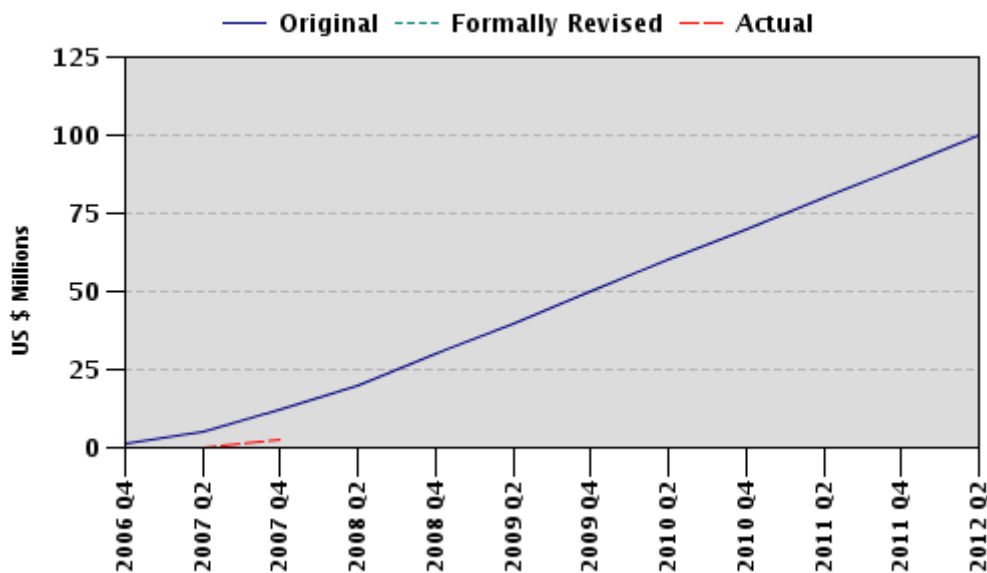

Project Name (ID): Liuzhou Environment Management (P081346)

Country: China

Board Approval Date : 05/24/2005

Closing Date : 06/30/2011

Loan/Credit/Grant Number : IBRD-47810

Sector(s): Sewerage(88%), Sanitation(5%), Solid waste management(5%), Sub-national government administration(2%)

Theme(s): Pollution management and environmental health(P), Access to urban services and housing(P), Municipal governance and institution building(S)

Project Development Objectives:

To sustainably improve the environmental conditions in Liuzhou through improved wastewater treatment, sanitation control and solid waste management

Progress toward achieving development objective(s):


Progress toward improving the environmental conditions in Liuzhou has been good. Construction contracts for two wastewater treatment plants have been awarded. Site selection for a number of public toilets and solid waste collection points was completed. Consultants to support project management and institutional development have mobilized. A financial forecast model is being used to review and revise forecasts for the Liuzhou Municipal Wastewater Treatment Company to improve financial management. These forecasts show a need to increase wastewater tariffs in 2007 to ensure sustainability. Key to keeping the project moving in the coming period are timely land acquisition and resettlement which are now causing delays in several components.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47810	Effective	100.00	20.26	79.74	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

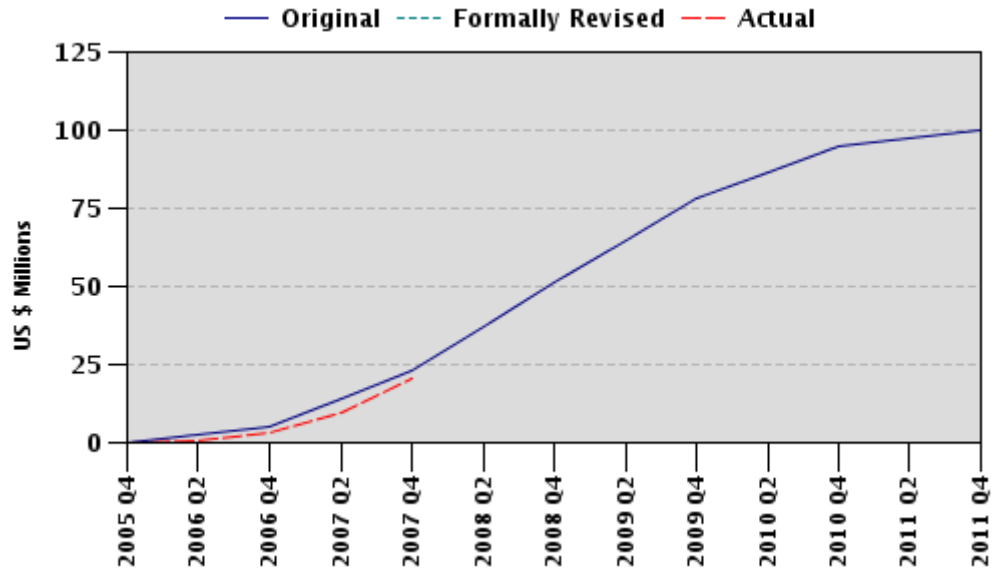

Project Name (ID): Henan Towns Water (P081348)

Country: China

Board Approval Date : 06/27/2006

Closing Date : 06/30/2013

Loan/Credit/Grant Number : IBRD-48290

Sector(s): Water supply(77%), Sanitation(9%), Sewerage(9%), Sub-national government administration(5%)

Theme(s): Access to urban services and housing(P), Pollution management and environmental health(P), Municipal governance and institution building(S), Regulation and competition policy(S), Water resource management(S)

Project Development Objectives:

To help create or expand water supply and wastewater management services and improve the planning, regulatory, and operational capacity of sector institutions.

Progress toward achieving development objective(s):


Effectiveness was declared in December 2006, so the project is in the early stages of implementation. Some works have begun, but procurement problems have made them ineligible for retroactive finance. The Provincial Project Management Office will require strengthening to provide sound engineering advice, improve construction supervision and ensure proper procurement monitoring. The provincial expert advisory group established during project preparation, is now having a positive impact on the quality of design work, and a few bid documents have been approved for issuance. Also technical assistance for institutional strengthening should mobilize in a timely manner for the various implementing agencies to benefit from their advice.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48290	Effective	150.00	0.38	149.63	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

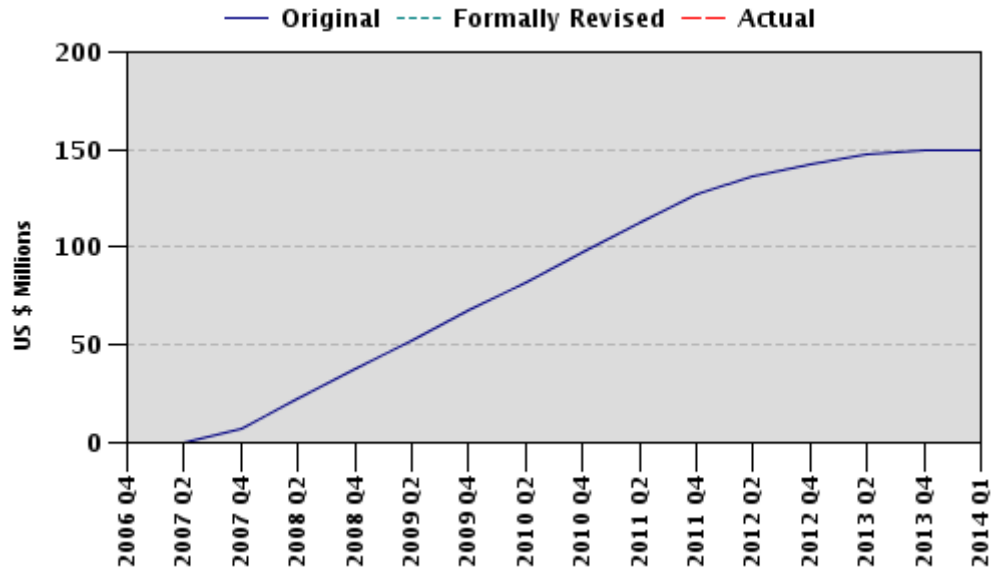

Project Name (ID): Hubei Shiman Highway (P081749)

Country: China

Board Approval Date : 06/24/2004

Closing Date : 06/30/2009

Loan/Credit/Grant Number : IBRD-47450

Sector(s): Roads and highways(97%), Sub-national government administration(3%)

Theme(s): Infrastructure services for private sector development(P), Rural services and infrastructure(P), Administrative and civil service reform(P), Trade facilitation and market access(S), Injuries and non-communicable diseases(S)

Project Development Objectives:


The main objective of the project is to support socioeconomic development of Hubei province by enhancing its access to other provinces, particularly the western region of China, improving local mobility within poor, remote western parts of the province, and strengthening governance of the provincial road sector.

Progress toward achieving development objective(s):

The project is progressing well. The main expressway component should be completed within 6-9 months. Most of the local road improvements are completed. The institutional strengthening has lagged, but this now appears to be on track. It is anticipated that the project will meet its PDOs.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47450	Effective	200.00	170.59	28.41	1.00

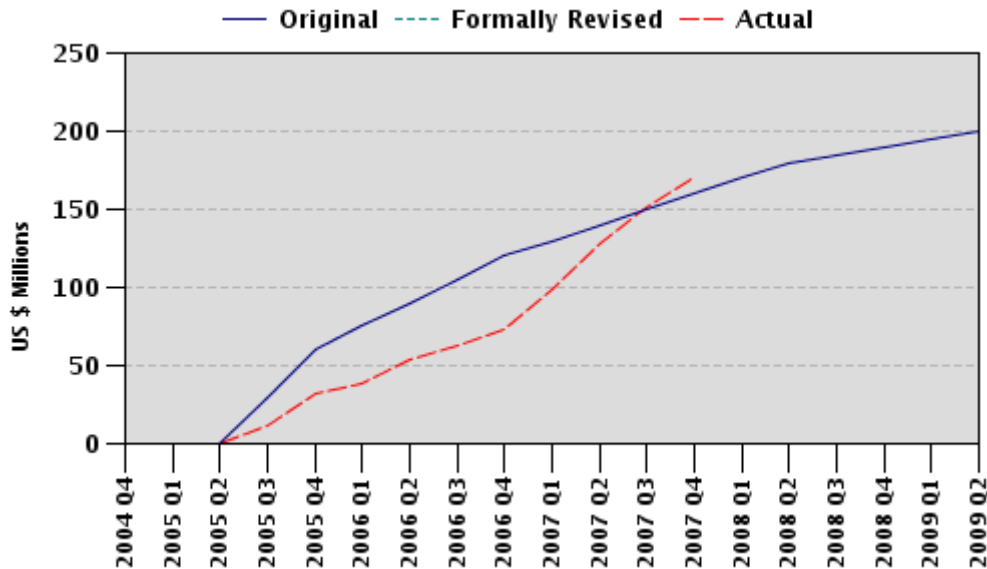

Project Name (ID): Guangdong/Pearl River Delta 2 (P081776)

Country: China

Board Approval Date : 03/21/2007

Closing Date : 12/31/2012

Loan/Credit/Grant Number : IBRD-48560

Sector(s): Sewerage(39%), Flood protection(31%), Sub-national government administration(20%), Sanitation(10%)

Theme(s): Access to urban services and housing(P), Pollution management and environmental health(P), Water resource management(S), Environmental policies and institutions(S)

Project Development Objectives:

To reduce water pollution in the Pearl River system originating from Foshan and Jiangmen municipalities

Progress toward achieving development objective(s):

The Loan is not yet effective.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48560	Not Effective	96.00	0.00	96.00	0.00



Project Name (ID): GEF-Termite Control Demonstration (P082992)

Country: China

Board Approval Date : 06/29/2006

Closing Date : 12/31/2010

Loan/Credit/Grant Number : MULT-53075, MULT-56588

Sector(s): Housing construction(64%), Central government administration(16%), Sub-national government administration(16%), Petrochemicals and fertilizers(4%)

Theme(s): Pollution management and environmental health(P), Environmental policies and institutions(S), Other environment and natural resources management(S), Other human development(S)

Project Development Objectives:

The objective is to mitigate environmental and health risks associated with chlordane and mirex in termite control by: (a) demonstrating the elimination of their use through the introduction of integrated pest management in selected areas; and (b) preparing a national replication program for the complete phase-out of chlordane and mirex in China by 2014.

Progress toward achieving development objective(s):


Two new provinces, Anhui and Hunan, were approved by GEF SEC on January 10, 2007 for participation in the project to replace the Zhejiang Province (which abruptly pulled out before appraisal). The project is now being implemented in three provinces (Anhui, Hunan and Jiangsu) and the Grant Agreement was amended on March 15, 2007 to reflect this. Project progress is on schedule.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-53075	Closed	0.28	0.27	0.00	0.01
MULT-56588	Effective	14.36	0.00	14.36	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

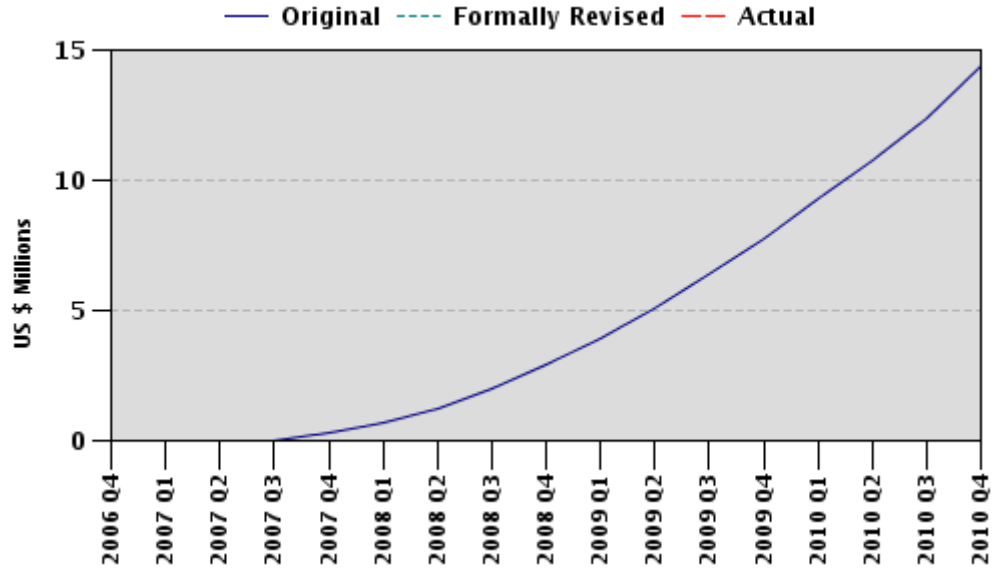

Project Name (ID): GEF-PCB Management and Disposal (P082993)

Country: China

Board Approval Date : 12/15/2005

Closing Date : 06/30/2010

Loan/Credit/Grant Number : MULT-53076, MULT-56008

Sector(s): Other industry(57%), Solid waste management(33%), Sub-national government administration(6%), Central government administration(4%)

Theme(s): Pollution management and environmental health(P), Environmental policies and institutions(S), Other environment and natural resources management(S)

Project Development Objectives:


The objective of the project is to identify and demonstrate environmentally-sound and cost-effective policies, procedures and techniques for safely managing and disposing of China's unique temporarily-stored PCBs and associated PCB-contaminated wastes.

Progress toward achieving development objective(s):

Many project activities have been initiated but overall progress has been slow, principally because the construction of the Zhejiang storage facilities and procurement of the thermal desorption system have been delayed. PCB site cleanup in Zhejiang is expected to start in August 2008.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-53076	Closed	0.29	0.29	0.00	0.00
MULT-56008	Effective	18.34	0.77	17.57	0.00

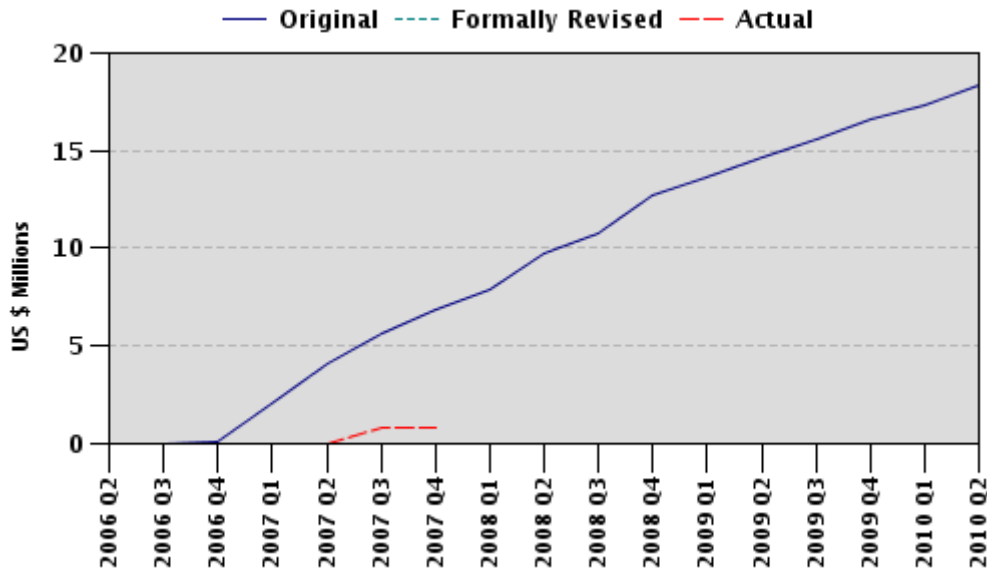

Project Name (ID): Sichuan Urban Development (P083322)

Country: China

Board Approval Date : 09/07/2006

Closing Date : 12/31/2013

Loan/Credit/Grant Number : IBRD-48380

Sector(s): Roads and highways(67%), Flood protection(14%), Sewerage(13%), General agriculture, fishing and forestry sector(4%), Other social services(2%)

Theme(s): Other urban development(P), Access to urban services and housing(S), Municipal governance and institution building(S), Other social development(S), Water resource management(S)

Project Development Objectives:


To improve core urban functions in an equitable and resource-efficient manner by removing identified infrastructure bottlenecks

Progress toward achieving development objective(s):

The Loan just became effective in January 2007. The project management office is now in the process of recruiting the project management consultant to move implementation forward.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48380	Effective	180.00	5.00	175.00	0.00

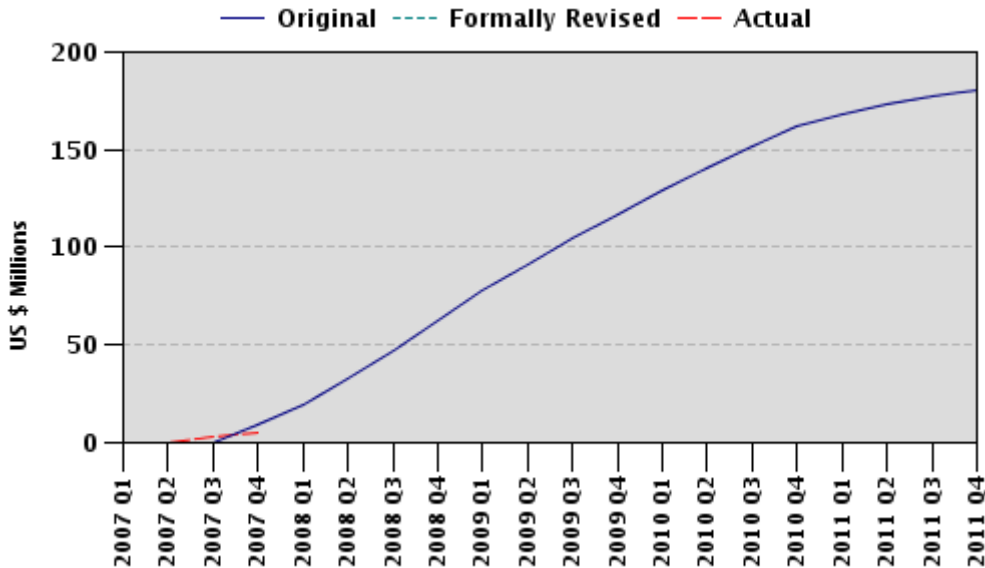

Project Name (ID): IAIL III (P084742)

Country: China

Board Approval Date : 10/11/2005

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-48030

Sector(s): Irrigation and drainage(68%), Agricultural extension and research(12%), General public administration sector(11%), Forestry(5%), General agriculture, fishing and forestry sector(4%)

Theme(s): Other rural development(P), Rural services and infrastructure(P), Rural policies and institutions(S), Environmental policies and institutions(S)

Project Development Objectives:

The objectives are: (a) to increase water and agricultural productivity in low- and medium-yield farm land areas; (b) to raise farmers' incomes and strengthen their competitive capacity under post-access conditions of the World Trade Organization; and (c) to demonstrate and promote sustainable participatory rural water resources management and agro-ecological environmental management in the Huang-Huai-Hai River Basin area.

Progress toward achieving development objective(s):

The project is making good progress on all components, especially the main ones -- development of water-saving irrigation and drainage, agricultural modernization and organization, and agro-ecological environment and management -- and is expected to achieve its development objectives. The project covers five original Project Provinces -- Anhui, Henan, Hebei, Shandong and Jiangsu -- located in the Huang-Huai-Hai Basin (the breadbasket of China), plus five additional Participating Provinces of Ningxia, Jilin, Inner Mongolia, Chongqing and Yunnan which were recently added for Water User Association (WUA) Development. The implementation of water-saving irrigation system improvements and WUA development has started well in the five original provinces, and initial training and investigations for WUA development in the five new provinces has started. Under the agricultural modernization component, the establishment of Farmer Associations (FAs) and pilot Farmer Cooperatives (FCs), and development of non-polluted and organic crop production has started in all project provinces and counties. Significant value-added from improved technical assistance and production capabilities and helping farmers coordinate marketing activities has been demonstrated. Under the agro-ecological component, development of farmland forest belts, on-farm protective forests, environment monitoring and management and training is on schedule. The provincial Mobile Expert Teams, key innovations under the project, are providing specialized expert technical assistance. Project Management Offices at all levels are giving strong attention to integrated water-saving measures, demonstration and extension activities, and integrated and coordinated development of WUAs, FAs/FCs and green/organic crop development in all subproject area.


Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/	Status	Amount	Disbursed	Undisbursed	Cancellation
--------------	--------	--------	-----------	-------------	--------------



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

Grant						
IBRD-48030	Effective	200.00	57.12	142.88	0.00	

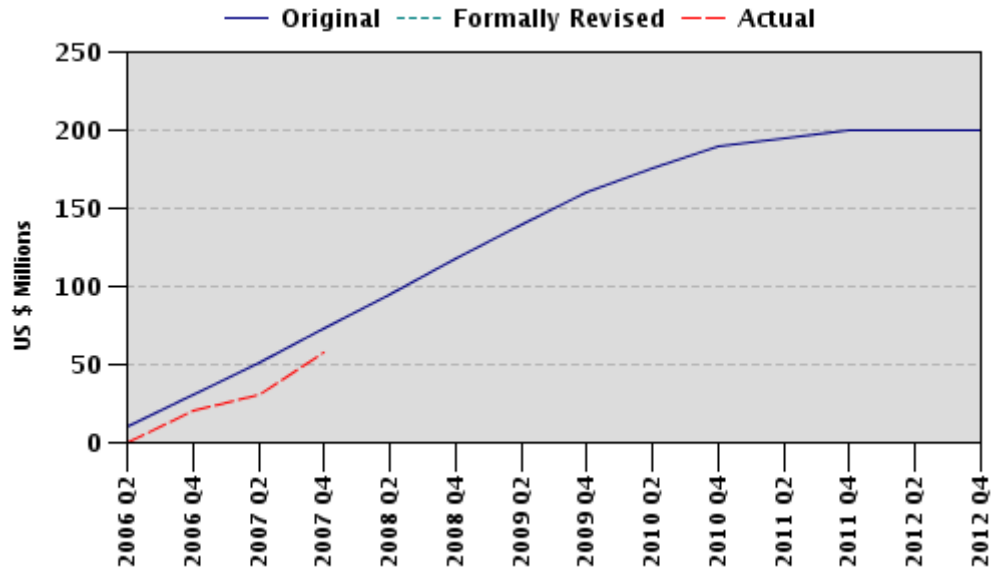

Project Name (ID): Economic Reform Implementation (P085124)

Country: China

Board Approval Date : 04/11/2006

Closing Date : 12/31/2011

Loan/Credit/Grant Number : IBRD-48200, DF57202

Sector(s): Central government administration(65%), Sub-national government administration(30%), Banking(5%)

Theme(s): Analysis of economic growth(P), Public expenditure, financial management and procurement(S), Improving labor markets(S), Biodiversity(S), Indigenous peoples(S)

Project Development Objectives:

The project development objective is to assist the GOC in implementing its reform and development agenda by significantly increasing the adoption and use of sound reform and development strategies, policies and implementation plans through a series of technical assistance subprojects tailored to address specific challenges through institutional capacity building at the national and sub-national levels.

Progress toward achieving development objective(s):


Most subprojects have started implementation only recently and it is too early to measure results. However, the implementation process has been of satisfactory quality. The likelihood of achieving project development objectives is reasonable, despite the adherent difficult caused by low observability and measurability of results indicators. The next supervision will take place in October 2007, which will provide a updated progress report.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48200	Effective	20.00	1.56	18.44	0.00
DF57202	Effective	11.22	1.14	10.02	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

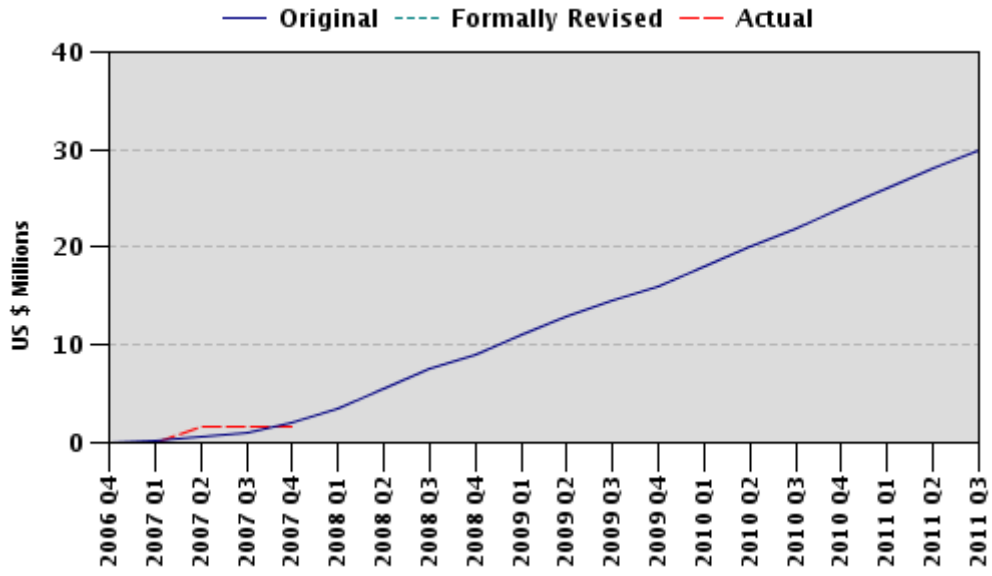

Project Name (ID): 5th Inland Waterways (P085333)

Country: China

Board Approval Date : 10/11/2005

Closing Date : 06/30/2011

Loan/Credit/Grant Number : IBRD-48040

Sector(s): Ports, waterways and shipping(50%), Renewable energy(35%), Sub-national government administration(15%)

Theme(s): Infrastructure services for private sector development(P), Other rural development(P), Water resource management(S), Administrative and civil service reform(S)

Project Development Objectives:

The project's development objective is to enhance the standard of living in the Han River region by developing its potential water resources, including: a) increasing the waterway transport capacity along the Han River and its cost-effectiveness; and

(b) ensuring the availability of sustainable hydropower and water resources for use in the Xiangfan area and the Tangdong farmland region.

Progress toward achieving development objective(s):


The project is progressing satisfactorily. Given the status of implementation, the likelihood of achieving the project objective is at least satisfactory. Key engineering complexities of the project are being addressed. The key outcomes indicators will be measured once the key investment component (Cuijiaying complex) is completed.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48040	Effective	100.00	25.01	74.99	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

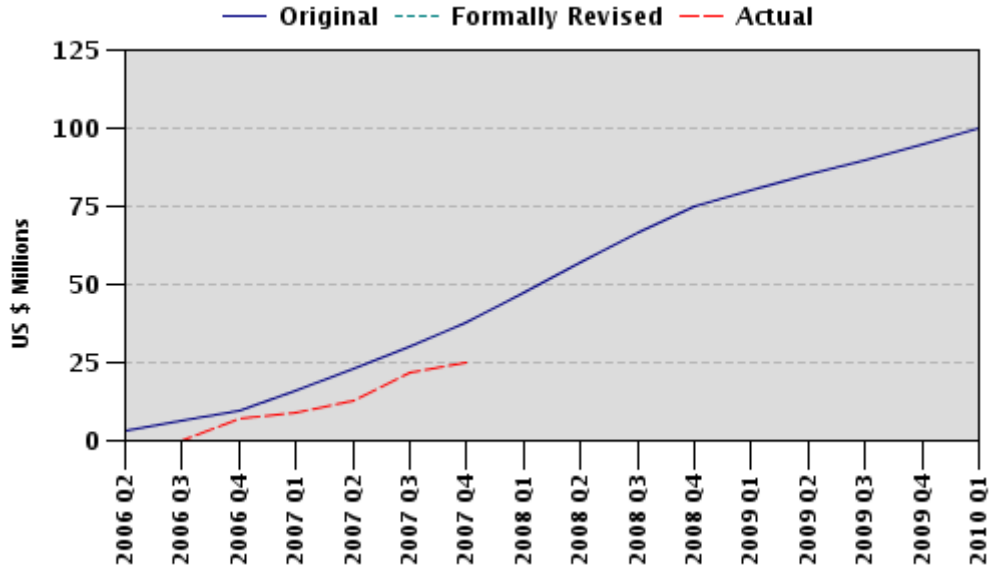

Project Name (ID): Ningbo Water and Environment (P086505)

Country: China

Board Approval Date : 03/17/2005

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-47700

Sector(s): Water supply(55%), Sewerage(45%)

Theme(s): Pollution management and environmental health(P), Water resource management(P), Municipal governance and institution building(S)

Project Development Objectives:


To facilitate the expansion and quality of water and wastewater services in Ningbo City and Cixi City in an economically efficient and environmentally sustainable manner.

Progress toward achieving development objective(s):

Progress toward meeting the project objectives has been solid. The expansion and improvement of the quality of water and wastewater services are well underway with construction of several wastewater treatment plants, a transmission and ring main, and a raw water tunnel. Institutional development is somewhat behind schedule, but two key consultant assignments are starting shortly: (a) one to prepare a water supply plan for Ningbo City, develop a strategic business plan for Ningbo Water Supply Company, and develop a plan to improve the utility regulatory system in Ningbo; and (b) another to build the technical and business capacity of the Cixi Municipal Sewerage Company. Progress on financial viability is going well with adequate tariffs in place.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-47700	Effective	130.00	22.24	107.76	0.00

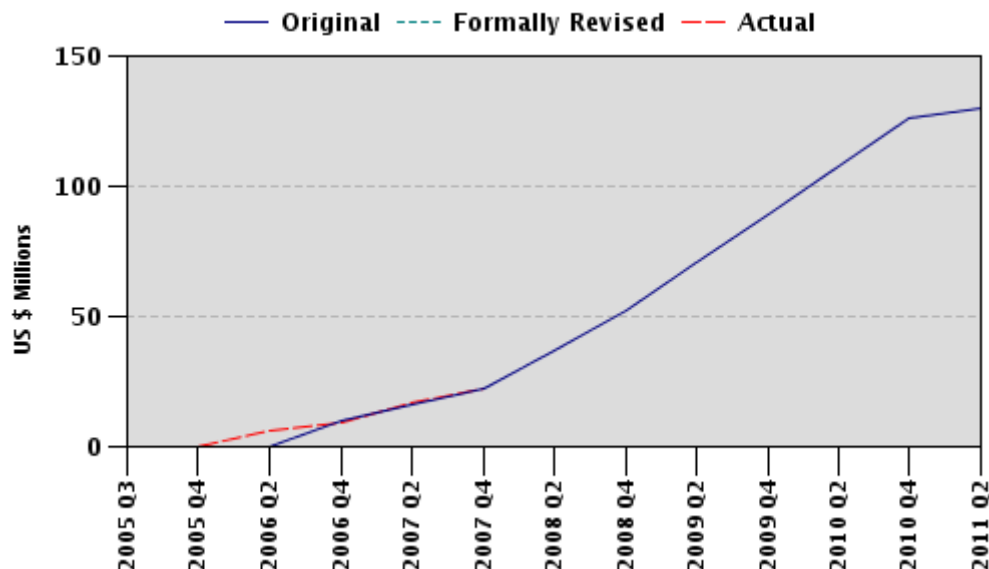

Project Name (ID): 3rd National Railway (P086515)

Country: China

Board Approval Date : 01/23/2007

Closing Date : 06/30/2012

Loan/Credit/Grant Number : IBRD-48470

Sector(s): Railways(99%), Central government administration(1%)

Theme(s): Trade facilitation and market access(P), Other public sector governance(S)

Project Development Objectives:


The Project aims to assist China in expanding the capacity of its railway system to meet the growing demand for transport of people and goods between Guizhou and Yunnan Provinces.

Progress toward achieving development objective(s):

The civil works to be financed under the Bank loan is six months behind schedule, but the project stated that it can be overcome and therefore still complete the construction as scheduled by the end of 2011. Otherwise indications are that the Project will be implemented more or less to schedule. In addition, general demand for railways remains high.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48470	Effective	200.00	0.00	200.00	0.00

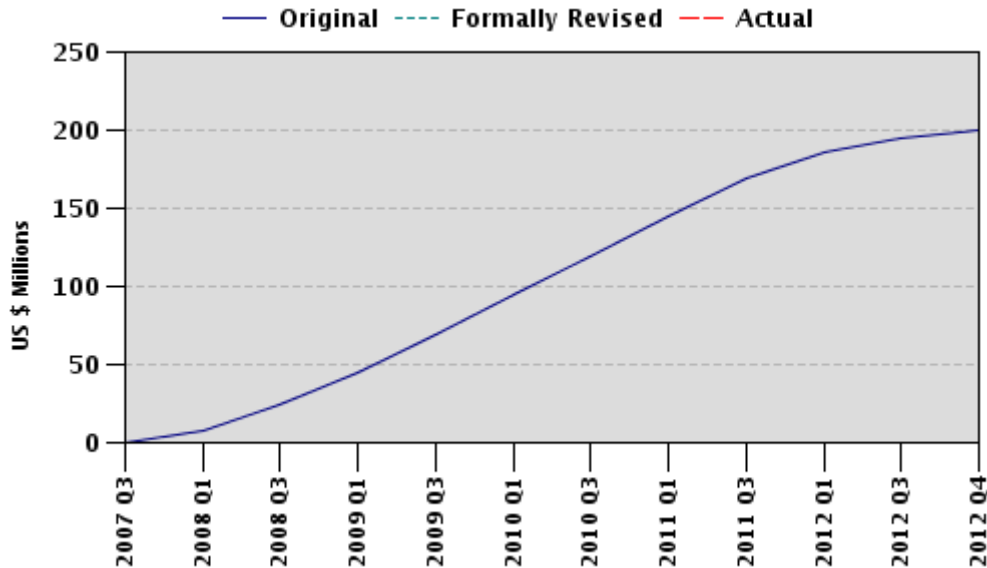

Project Name (ID): Heilongjiang Dairy (P086629)

Country: China

Board Approval Date : 01/24/2006

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-48150

Sector(s): Animal production(69%), Agricultural extension and research(27%), Crops(3%), Sub-national government administration(1%)

Theme(s): Other rural development(P), Rural services and infrastructure(P), Technology diffusion(S), Rural policies and institutions(S), Climate change(S)

Project Development Objectives:


The objectives are: (a) to improve the financial viability of existing and new dairy operations in selected areas of Heilongjiang province; and (b) to demonstrate innovative technologies to reduce green-house gas emissions and increase carbon sequestration.

Progress toward achieving development objective(s):

Because of the increased costs of milk production and low farm-gate prices, the implementation of the Dairy Production Development component of the project has been slow to start. It is anticipated that the project may need to be restructured to broaden its development objectives.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48150	Effective	100.00	3.25	96.75	0.00

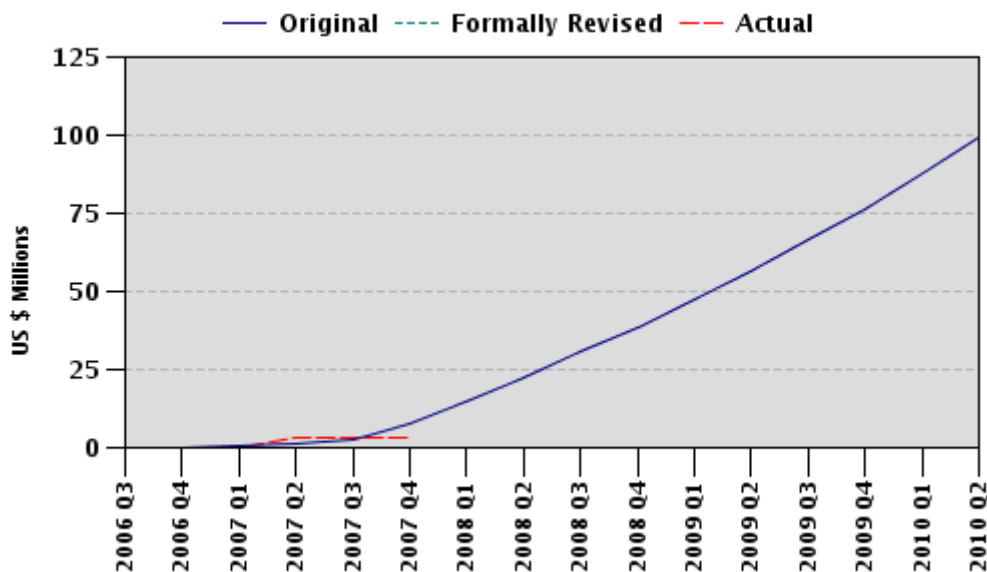

Project Name (ID): Guangxi Integrated Forestry Development (P088964)

Country: China

Board Approval Date : 12/14/2006

Closing Date : 12/31/2012

Loan/Credit/Grant Number : IBRD-48440

Sector(s): Forestry(94%), Sub-national government administration(6%)

Theme(s): Other environment and natural resources management(P), Rural markets(S), Rural services and infrastructure(S), Environmental policies and institutions(S), Land administration and management(S)

Project Development Objectives:


The objective is to improve the effectiveness of forest management and institutional arrangements in timber production, watershed protection and nature reserve management in selected areas of the Guangxi Zhuang Autonomous Region.

Progress toward achieving development objective(s):

Since Loan and Grant effectiveness in April 2007, project activities have been carried out on the ground as scheduled, despite some delay in signing of on-lending and on-granting agreements between government agencies. Some project counties have been able to achieve more than 50% of the plantation and watershed management targets for CY2007. It is expected that the project objective will be achieved.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48440	Effective	100.00	0.00	100.00	0.00

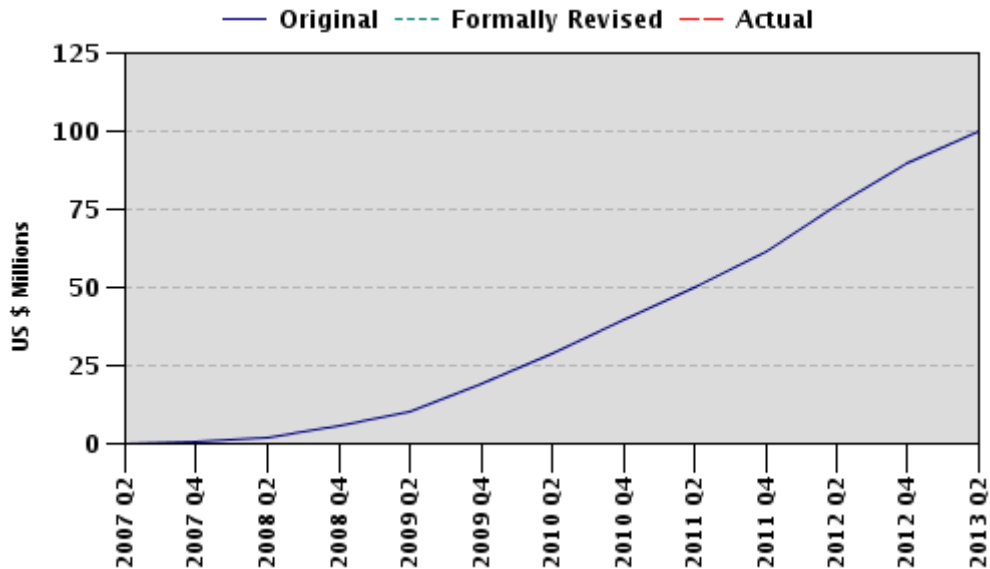

Project Name (ID): GEF-Ningbo Water and Environment (P090336)

Country: China

Board Approval Date : 06/29/2006

Closing Date : 12/31/2010

Loan/Credit/Grant Number : MULT-55469, MULT-56692

Sector(s): General water, sanitation and flood protection sector(100%)

Theme(s): Pollution management and environmental health(P), Biodiversity(S), Water resource management(S)

Project Development Objectives:


To reduce land-based pollution along the Cixi coast and the East China Sea, promote the replication of innovative low cost wastewater treatment techniques, and encourage coastal zone conservation

Progress toward achieving development objective(s):

Progress toward meeting the grant's objective is off to a reasonable start since effectiveness was declared in December 2006. Procurement of two key consultant contracts is underway: one for engineering designs for the constructed wetland, and the second for management of the wetland center. Mobilization of both teams of consultants is expected in October 2007.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-55469	Closed	0.25	0.25	0.00	0.00
MULT-56692	Effective	5.00	0.50	4.50	0.00

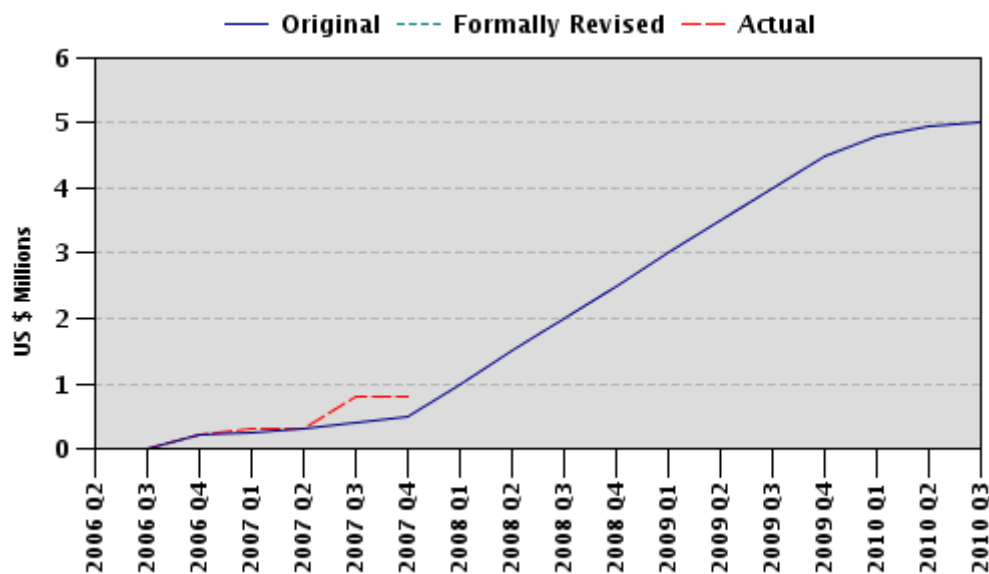

Project Name (ID): Fujian Highway Sector Investment (P091020)

Country: China

Board Approval Date : 10/12/2006

Closing Date : 06/30/2012

Loan/Credit/Grant Number : IBRD-48400

Sector(s): Roads and highways(99%), Sub-national government administration(1%)

Theme(s): Rural services and infrastructure(P), Infrastructure services for private sector development(P)

Project Development Objectives:

The project aims to increase the effective use of the road infrastructure in Fujian Province to support its social and economic development. This objective seeks to contribute to: (i) improving living conditions in rural areas-particularly those in the areas of the Province where poverty rates are higher-by enhancing the transport accessibility of the rural communities to economic opportunities and social services; (ii) stimulating higher economic growth in Fujian Province by reducing transport costs; and (iii) facilitating the interconnection across the coastal provinces. In this respect, the project will meet both the provincial government objective to improve the transport network to support the social and economic development of the province (especially in the economically lagging counties), and the central government objective to facilitate transport interconnections across Coastal Provinces.

Progress toward achieving development objective(s):

This project was approved by the Board on October 12, 2006. (The loan and project agreements were signed on August 31, 2007.) Procurement activities are well underway and investments under the Rural Roads Improvement Component have advanced adequately. The project is expected to be in full implementation within the first half of FY08.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48400	Not Effective	320.00	0.00	320.00	0.00



Project Name (ID): Liaoning Medium Cities Infrastructure 2 (P092618)

Country: China

Board Approval Date : 06/26/2007

Closing Date : 12/31/2013

Loan/Credit/Grant Number : IBRD-48640

Sector(s): Water supply(42%), Sewerage(34%), Solid waste management(17%), Flood protection(6%), Sub-national government administration(1%)

Theme(s): Pollution management and environmental health(P), Other urban development(P), Water resource management(S)

Project Development Objectives:

To improve the performance and sustainability of water supply, wastewater, and solid waste services in the project cities

Progress toward achieving development objective(s):

The Loan and Grant were just approved on June 26, 2007.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48640	Not Effective	173.00	0.00	173.00	0.00



Project Name (ID): 3rd Jiangxi Hwy (P093906)

Country: China

Board Approval Date : 06/27/2006

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IBRD-48300

Sector(s): Roads and highways(97%), Sub-national government administration(3%)

Theme(s): Infrastructure services for private sector development(P), Trade facilitation and market access(P), Injuries and non-communicable diseases(S), Rural services and infrastructure(S)

Project Development Objectives:


The project development objective is to improve east-west passenger and freight flows in Jiangxi province by investing in the construction of an expressway, enhancing local roads, and strengthening highway management.

Progress toward achieving development objective(s):

Expressway construction started early 2007 so this component has not made very much progress. The local roads component is behind schedule. The institutional strengthening activities have not commenced as of yet.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48300	Effective	200.00	6.50	193.50	0.00

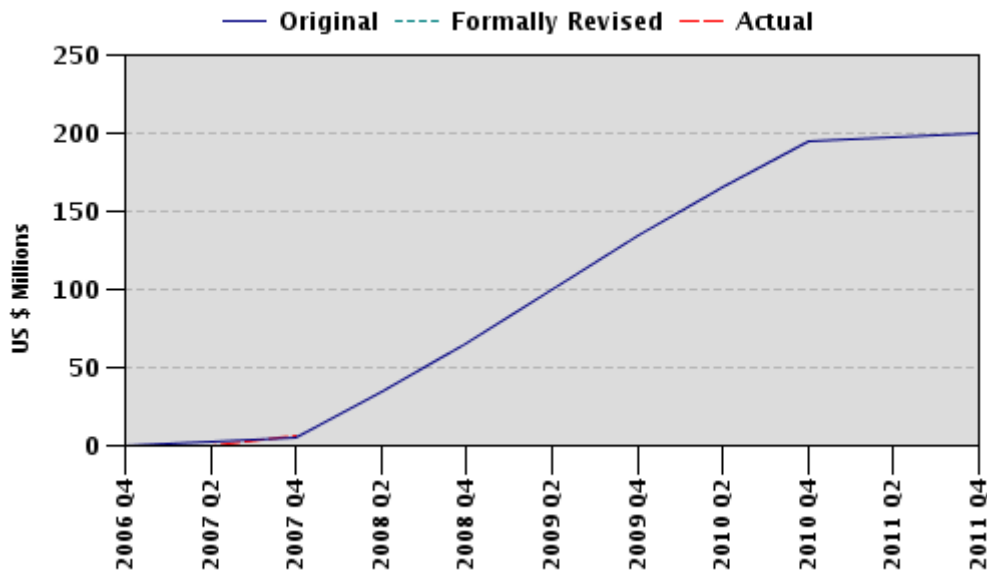

Project Name (ID): Western Region Rural Water and Sanitation (P095315)

Country: China

Board Approval Date : 06/26/2007

Closing Date : 09/30/2012

Loan/Credit/Grant Number : IBRD-48630

Sector(s): Water supply(63%), Sanitation(27%), Sub-national government administration(5%), Other social services(5%)

Theme(s): Rural services and infrastructure(P), Other human development(P), Participation and civic engagement(S), Pollution management and environmental health(S)

Project Development Objectives:

To increase access of poor participating communities to sustainable and equitable water supply, sanitation and hygiene promotion services

Progress toward achieving development objective(s):

The Loan was just approved on June 26, 2007.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48630	Not Effective	25.00	0.00	25.00	0.00



Project Name (ID): Renewable Energy II (CRESP II) (P096158)

Country: China

Board Approval Date : 02/07/2006

Closing Date : 09/30/2010

Loan/Credit/Grant Number : IBRD-48160

Sector(s): Renewable energy(100%)

Theme(s): Climate change(P), Infrastructure services for private sector development(P), Environmental policies and institutions(P), Rural services and infrastructure(S)

Project Development Objectives:

The project development objective is to demonstrate early success in large-scale renewable energy investments with participating local developers in one pilot autonomous region and one pilot province.

Progress toward achieving development objective(s):


For Zhejiang small hydro component, the project is generally progressing well, with batch one projects now completed or under construction, batch two now under procurement. Inner Mongolia North Long Yuan Wind Power Company has initiated appointment of a procurement agent and has draft bidding documents for the supply and supervision of installation of wind turbines, which is to be financed by the Bank loan. The Inner Mongolia component is facing delays with bidding documents still not completed. Concerns with application of the agreed RAP have also been identified. Actions are being taken to resolve them. Outcome information will be developed as part of the CRESP M&E program.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48160	Effective	86.33	11.69	74.64	0.00



Status of Projects in Execution - FY07
EAST ASIA AND PACIFIC REGION

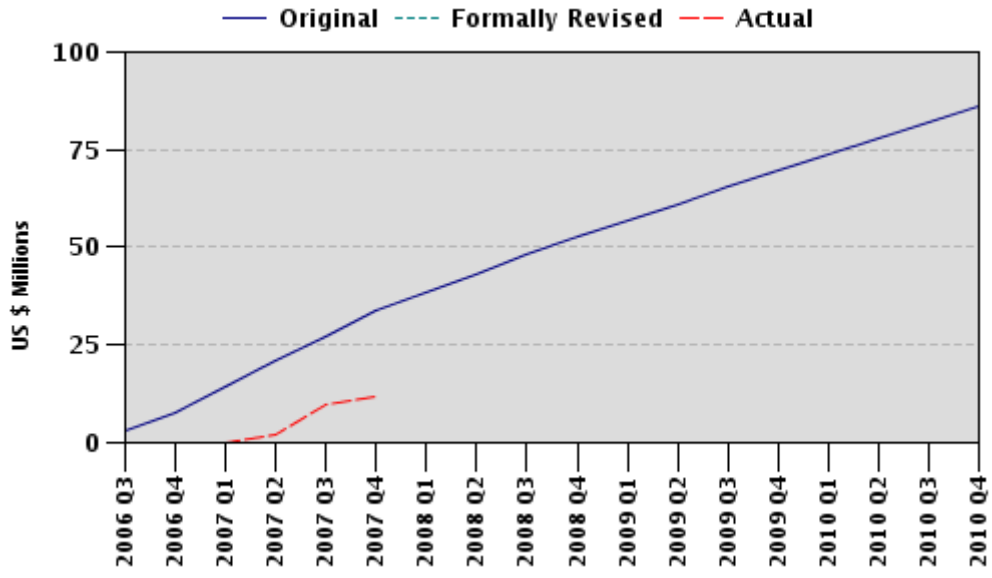

Project Name (ID): MSE Finance (P096285)

Country: China

Board Approval Date : 06/19/2007

Closing Date : 06/30/2011

Loan/Credit/Grant Number : IBRD-74610

Sector(s): Micro- and SME finance(95%), Banking(5%)

Theme(s): Small and medium enterprise support(P), Other financial and private sector development(S)

Project Development Objectives:

The project development objective is to expand credit flows to MSEs on a mass-market and commercially sustainable basis.

Progress toward achieving development objective(s):

The project was approved in June 2007 and is not yet effective.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-74610	Not Effective	100.00	0.00	100.00	0.00



Project Name (ID): Liaoning Medium Cities Infrastructure (P099992)

Country: China

Board Approval Date : 06/27/2006

Closing Date : 12/31/2011

Loan/Credit/Grant Number : IBRD-48310

Sector(s): Roads and highways(70%), General transportation sector(16%), Sanitation(14%)

Theme(s): Other urban development(P), Access to urban services and housing(S), Municipal governance and institution building(S)

Project Development Objectives:

The objective of the Project is to assist the Borrower's Project Cities in enhancing: (i) the performance and quality of their existing urban transport infrastructure in terms of mobility, access, and safety; (ii) the efficiency and effectiveness of their urban public transport and road maintenance services; and (iii) the responsiveness of their urban transport systems to the needs of population without access to private motorized vehicles.

Progress toward achieving development objective(s):

The US\$218 million Loan was approved by the World Bank on June 27, 2006. The legal agreements were signed on October 18, 2006 and the Loan was declared effective on January 5, 2007. Implementation is proceeding. First year construction activities are underway as planned and will be financed using the retroactive financing facility.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IBRD-48310	Effective	218.00	22.36	195.64	0.00

