

STATUS OF PROJECTS IN EXECUTION – FY07
SOPE
MOLDOVA

Operations Policy and Country Services
OCTOBER 10, 2007



Introduction

The Status of Projects in Execution (SOPE) Report for FY07 provides information on all IBRD/IDA projects that were active as of June 30, 2007. The World Bank has issued a SOPE Report every year as an internal communication to the Board of Executive Directors. In accordance with the Bank's revised disclosure policy, since FY02, the SOPE Report is available to the public.

The report is intended to bridge the gap in information available to the public between the Project Appraisal Document or Program Document, disclosed after the Bank approves a project, and the Implementation Completion Report, disclosed after the project closes.

In addition to the project progress description, the FY07 SOPE report¹ contains project level comparisons of disbursement estimates and actual disbursements, and a table showing the loan/credit/grant amount and disbursements to date.

¹ Notes:

- Amounts and Graphs for loans/credits/grants in currencies other than U.S. dollars may not match exactly due to exchange rate fluctuations over the life of the project.
- Disbursement graphs are not included for Development Policy Operations, which provide quick-disbursing financing to support policy and institutional reforms. For these operations, funds are disbursed in one or more stages (tranches), released when the borrower complies with agreed prior actions.
- Projects which are not yet effective may not have a planned disbursement schedule and thus will not include a graph.



Country: Moldova

Project Name (ID): Energy 2 (P040558)

Country: Moldova

Board Approval Date : 11/25/2003

Midterm Review Date : 04/21/2006

Closing Date : 04/30/2008

Loan/Credit/Grant Number : IDA-Q1910, IDA-38330, JPN-25294

Sector(s): Power(70%), District heating and energy efficiency services(10%), Central government administration(10%), Health(5%), General education sector(5%)

Theme(s): Infrastructure services for private sector development(P), Access to urban services and housing(P), Regulation and competition policy(P), Pollution management and environmental health(S), Climate change(S)

Project Development Objectives:

The project development objectives are two-fold: (a) facilitate unimpeded commercial operation of the power system by improving the security and reliability of the electricity transmission system and wholesale electricity supply; and (b) improve access to high quality and efficient heating in priority public and residential buildings catering to disabled and other vulnerable groups.

Progress toward achieving development objective(s):

The reliability of the electricity supply is improving. Both technical and non-technical losses have been significantly reduced. An action plan has been agreed with the government, the regulator, and the transmission company to address deficiencies in the current power market design and align it with provisions of the Energy Community of Southeast Europe Treaty.


The second development objective has largely been met, with improved availability, quality, and efficiency of heating provided to 26 educational and 9 medical institutions, benefiting 8,399 students, approximately 1.1 million patients/visitors, and about 2,132 families whose apartment buildings were connected to the new boilers, which provide comfortable temperatures at a lower cost.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-Q1910	Closed	1.50	0.00	0.00	1.50
IDA-38330	Effective	38.95	16.57	22.01	0.00
JPN-25294	Closed	0.70	0.66	0.00	0.04



Status of Projects in Execution - FY07
EUROPE AND CENTRAL ASIA REGION

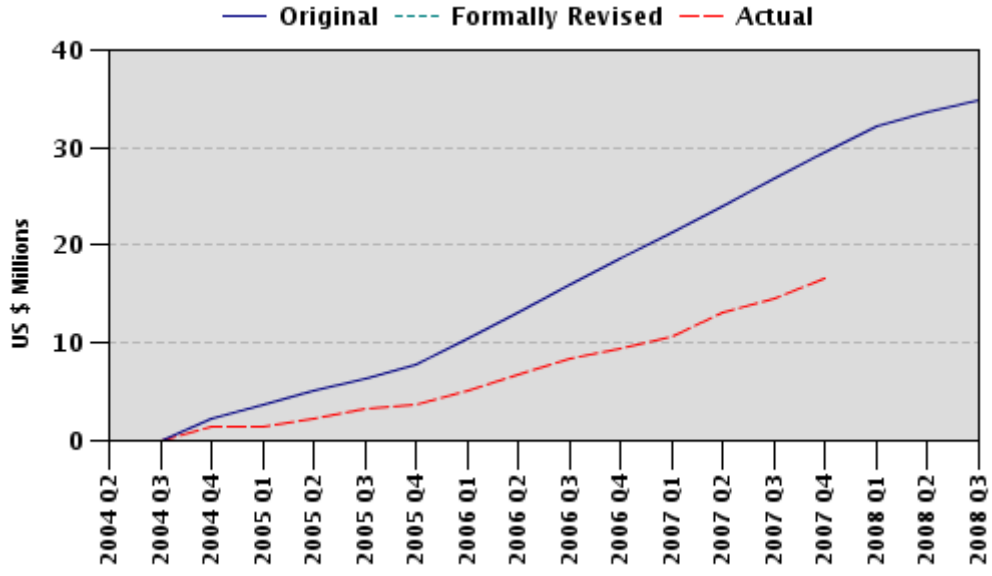

Project Name (ID): Trade and Transport Facilitation in Southeast Europe (P073626)
Country: Moldova
Board Approval Date : 06/10/2003
Closing Date : 09/30/2007
Loan/Credit/Grant Number : IDA-37830, IDA-Q3100
Sector(s): Central government administration(100%)
Theme(s): Trade facilitation and market access(P), Tax policy and administration(P),
Regional integration(S)

Project Development Objectives:

The project development objectives are to reduce non-tariff costs to trade and transport and to increase revenue and compliance, and reduce smuggling and corruption at border crossings by: (a) strengthening customs institutional capacity; (b) modernizing and integrating customs information systems for border processing and clearance of shipments; (c) developing a transit control system; (d) upgrading the capacity and effectiveness of existing border points; (e) improving mechanisms of interaction and cooperation between border control agencies and the trading community; (f) disseminating information and providing training to the trading community (private sector); and (g) implementing, at pilot sites, an integrated set of new customs procedures, information technology, human resource management techniques, and cooperation mechanisms for agencies at border crossings.

Progress toward achieving development objective(s):


Some of the reforms carried out by the Moldovan Customs exceeded the scope and objectives of the project and made noticeable success in terms of improving the efficiency of its services. Trade has increased approximately 20 percent between 2005 and 2006, implying an increase of the customs revenue collection. Computerization and introduction of trade facilitation measures has reduced the delays and cost for the traders due to improved and streamlined customs procedures.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-37830	Effective	8.03	7.80	0.00	0.00
IDA-Q3100	Closed	0.10	0.00	0.00	0.10



Status of Projects in Execution - FY07
EUROPE AND CENTRAL ASIA REGION

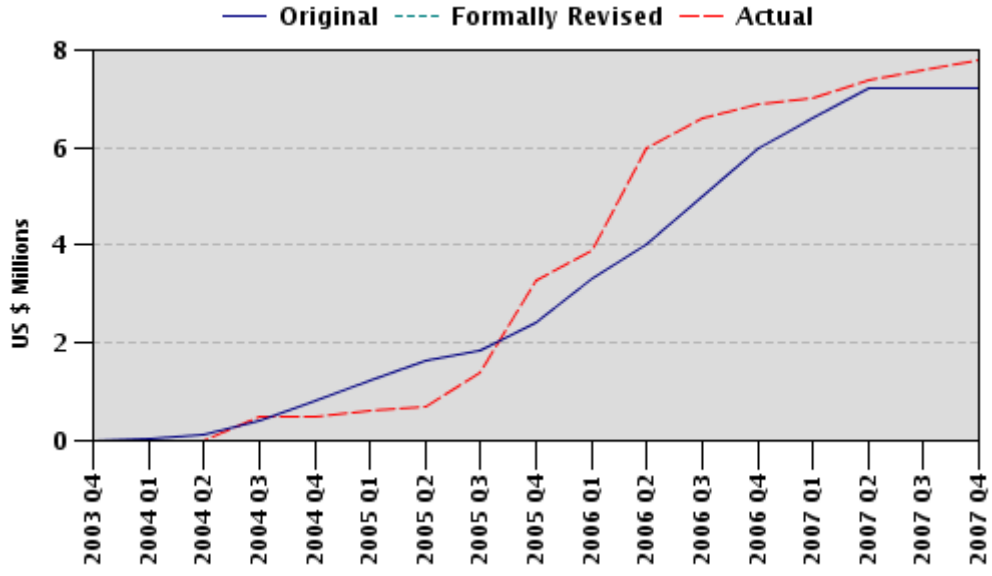

Project Name (ID): AIDS Control (P074122)
Country: Moldova
Board Approval Date : 06/10/2003
Midterm Review Date : 04/04/2006
Closing Date : 07/31/2008
Loan/Credit/Grant Number : JPN-51353, IDA-H0460
Sector(s): Health(100%)
Theme(s): HIV/AIDS(P)

Project Development Objectives:

The objective is to improve Moldova's health status and assist the country to achieve its health-related Millennium Development Goals through reducing mortality, morbidity, and the transmission of HIV/AIDS and other sexually transmitted infections.

Progress toward achieving development objective(s):


The project complements the financing from the state budget, the Global Fund, and other donor organizations. The project has increased laboratory capacities for HIV testing, started harm-reduction programs among injecting drug users and prevention programs for high risk groups, improved access to treatment for HIV and other sexually transmitted infections, and financed home care programs for AIDS patients. Testing and the provision of appropriate prevention treatment during pregnancy and childbirth has already significantly reduced mother-to-child transmission of HIV infection (from 13.3% in 2002 to 6.4% in 2005 and 0% in 2006). Provision of anti-retroviral treatment has also considerably reduced AIDS mortality. The challenge still is to curb the HIV infection rate where more efforts are needed in decreasing risky behavior. A knowledge, attitude, and behavior study conducted among youth shows improvement in knowledge, with 26% respondents answering core questions correctly in 2006, an increase from 15.8% in 2003.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-51353	Closed	0.37	0.09	0.00	0.28
IDA-H0460	Effective	6.21	4.72	1.37	0.00



Status of Projects in Execution - FY07
 EUROPE AND CENTRAL ASIA REGION

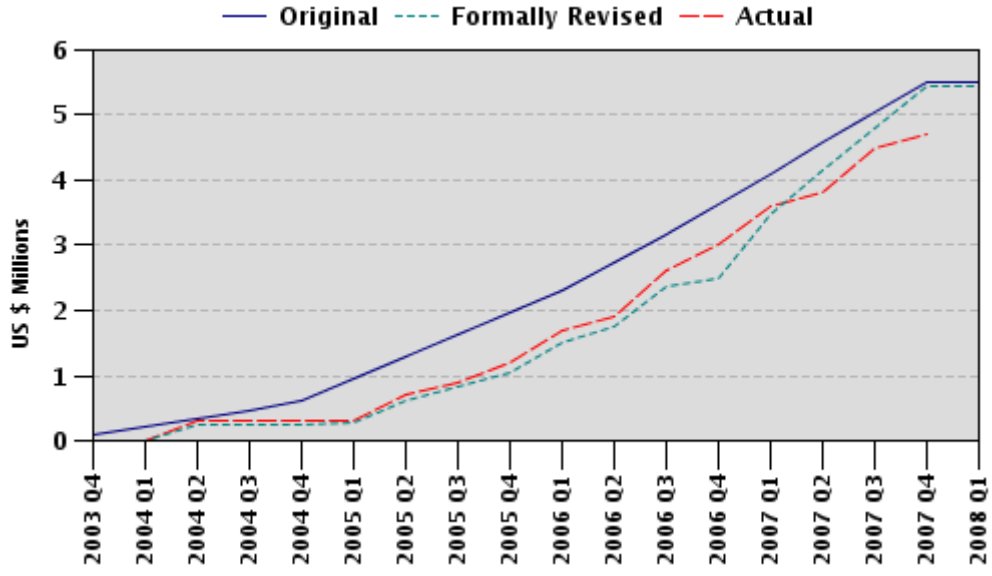

Project Name (ID): Environment Infrastructure (GEF) (P074139)

Country: Moldova

Board Approval Date : 05/29/2007

Closing Date : not yet effective

Loan/Credit/Grant Number :

Sector(s): Sewerage(96%), Central government administration(4%)

Theme(s): Pollution management and environmental health(P), Environmental policies and institutions(S), Water resource management(S)

Project Development Objectives:

The key development objectives of the project are to: (a) improve the quality of sanitation services in Soroca; (b) reduce the discharge of pollutants, including nutrients, from Soroca municipal sources that flow into the Nistru River and, subsequently, into the Black Sea; and (c) demonstrate viable nutrient reduction strategies and technologies from municipal sources for the benefit of Moldova and Black Sea region.

Progress toward achieving development objective(s):

The project loan was not yet effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)



Project Name (ID): Water Supply and Sanitation (P074469)

Country: Moldova

Board Approval Date : 05/20/2003

Midterm Review Date : 07/24/2006

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IDA-37630, JPN-26816

Sector(s): Water supply(75%), Sanitation(25%)

Theme(s): Other urban development(P), Access to urban services and housing(P), Pollution management and environmental health(S), Other financial and private sector development(S)

Project Development Objectives:

The project development objectives are to improve the quality, reliability, efficiency and sustainability of the water supply and sanitation services in the participating municipalities and rural areas. The aim is also to ensure that the water utilities move towards cost recovery.

Progress toward achieving development objective(s):


The project is making progress towards meeting its development objectives. Although some investments remain to be completed in the four participating cities, negative water quality samples have not been detected. Two cities have started to enjoy 24 hour-a-day water supply, and other two cities have also improved the water supply services hours significantly. Energy use per cubic meter of water production improved significantly. However, cost recovery has been difficult mainly due to political interventions during the tariff approval process. The fifth water company, Balti Apa Canal, started participating late in the project but is working hard to complete its sub-projects before the closing date.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-37630	Effective	13.34	7.28	5.86	0.00
JPN-26816	Closed	0.46	0.46	0.00	0.00



Status of Projects in Execution - FY07
 EUROPE AND CENTRAL ASIA REGION

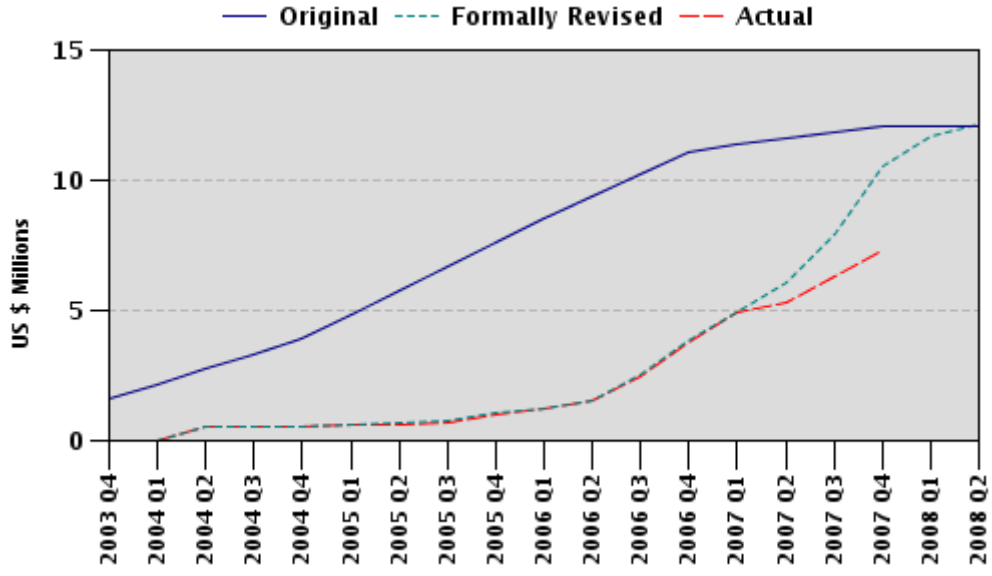

Project Name (ID): Agriculture Pollution Control (GEF) (P075995)

Country: Moldova

Board Approval Date : 02/26/2004

Midterm Review Date : 03/26/2007

Closing Date : 12/31/2009

Loan/Credit/Grant Number : MULT-50093, MULT-53023

Sector(s): Irrigation and drainage(30%), General water, sanitation and flood protection sector(30%), Central government administration(20%), Agricultural extension and research(10%), Forestry(10%)

Theme(s): Pollution management and environmental health(P), Other rural development(P), Water resource management(S), Land administration and management(S)

Project Development Objectives:

The objective is to increase the use of mitigation measures by agro-industry and farmers to reduce nutrient discharge into the surface and ground water bodies in Moldova.

The global environmental goal is to reduce, over the long-term, the discharge of nutrients and other agricultural pollutants into the Danube River and Black Sea through (a) collaboration with agro-industry and farmers benefiting from the on-going Rural Investment and Services Project and (b) interventions in a pilot watershed area.

Progress toward achieving development objective(s):


Field interviews with farmers and entrepreneurs identified the spontaneous adoption of some environmentally friendly agricultural techniques and much demand for project-supported waste management investments, some backstopped by the requirement to have land management plans to receive vineyard subsidies. Demand for soil testing has also increased. Water sampling indicates lower concentration of nitrate in waters filtering through restored area and discharging into the Prut River.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-50093	Closed	0.30	0.30	0.00	0.00
MULT-53023	Effective	4.95	3.87	1.08	0.00



Status of Projects in Execution - FY07
EUROPE AND CENTRAL ASIA REGION

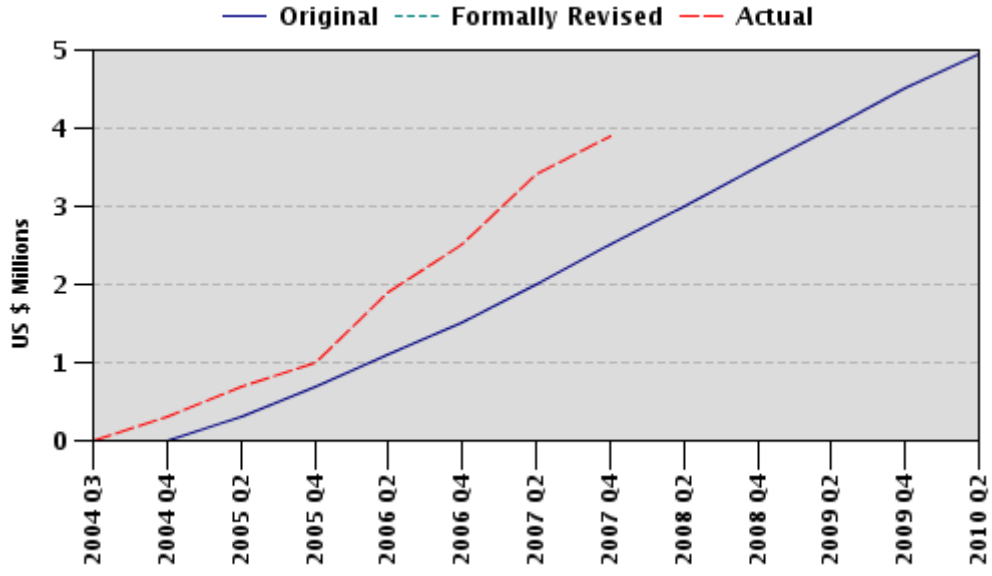

Project Name (ID): SIF 2 (P079314)

Country: Moldova

Board Approval Date : 06/17/2004

Midterm Review Date : 06/01/2007

Closing Date : 03/31/2010

Loan/Credit/Grant Number : SIDA-54460, JPN-52114, IDA-39310

Sector(s): Other social services(40%), Primary education(20%), Roads and highways(15%), District heating and energy efficiency services(15%), Water supply(10%)

Theme(s): Other social protection and risk management(P), Participation and civic engagement(S), Rural services and infrastructure(S), Rural policies and institutions(S), Other accountability/anti-corruption(S)

Project Development Objectives:

The objective is to empower poor communities and vulnerable population groups to manage their priority development needs.

Progress toward achieving development objective(s):

The project continues to be a relevant tool that empowers local communities and their institutions and efficiently provides needed social infrastructure in poor communities.

The project is strongly progressing towards achieving its development objectives.

Activities have positive impacts on the capacities of communities at different levels and are appreciated by community members.


Under the Rural Development Component 335 sub-projects worth over US\$20.2 millions have already been approved, surpassing the overall end-of-project-targets. The Social Care Services Development Component is already having an impact on policy making as the decentralization of the decision making process for the social care delivery is now being debated at the national level.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
SIDA-54460	Effective	4.29	0.79	3.47	0.00
JPN-52114	Closed	0.58	0.58	0.00	0.00
IDA-39310	Effective	20.91	11.92	8.65	0.00



Status of Projects in Execution - FY07
EUROPE AND CENTRAL ASIA REGION

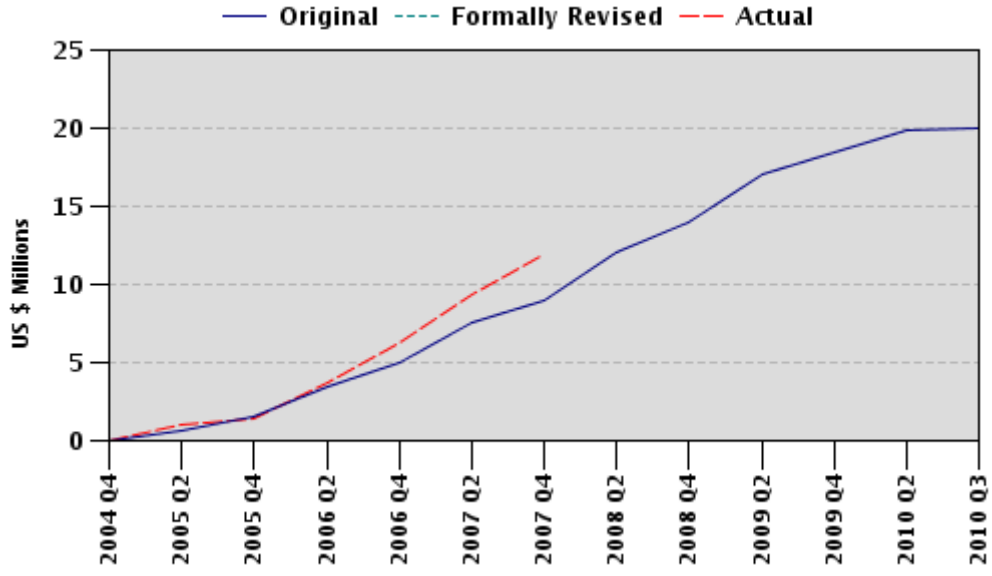

Project Name (ID): Public Financial Management TA (P082916)

Country: Moldova

Board Approval Date : 06/16/2005

Closing Date : 06/30/2010

Loan/Credit/Grant Number : SIDA-55030, SIDA-54017, NETH-55170, JPN-53751, IDA-40820

Sector(s): Central government administration(80%), Sub-national government administration(20%)

Theme(s): Public expenditure, financial management and procurement(P), Other public sector governance(S)

Project Development Objectives:

The objective is to improve the management of public finances.

Progress toward achieving development objective(s):


In the past year, some of the project's key interim results have been achieved. The 2006 budget was executed without a deficit, and budget coverage was extended with the integration of six off-budget funds. The Medium Term Expenditure Framework was expanded to include the agriculture sector and investment analysis. Necessary steps for the automation of public financial management processes were undertaken, including the introduction of a single treasury sub-account for special means of budget institutions, the design of new budget classification and chart of accounts, and the establishment of network infrastructure to support a Financial Management Information System. A concept of internal audit has been approved by the government. At present the implementation of some project components, including training, internal audit, and the introduction of a Financial Management Information System is behind schedule, but the project is still likely to achieve its development objective.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
SIDA-55030	Closed	0.49	0.29	0.00	0.18
SIDA-54017	Effective	2.04	0.18	1.85	0.00
NETH-55170	Effective	4.20	0.62	3.55	0.00
JPN-53751	Closed	0.53	0.48	0.00	0.06
IDA-40820	Effective	8.64	0.25	8.38	0.00



Status of Projects in Execution - FY07
EUROPE AND CENTRAL ASIA REGION

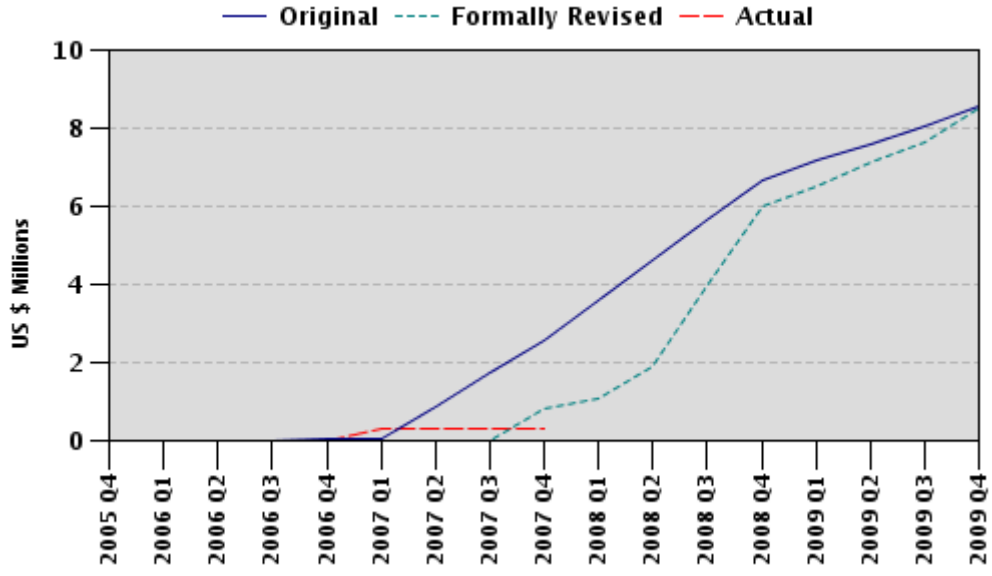

Project Name (ID): Competitiveness Enhancement (P089124)

Country: Moldova

Board Approval Date : 10/27/2005

Closing Date : 12/31/2009

Loan/Credit/Grant Number : IDA-H1870, JPN-55175, IDA-41190, JPN-54602

Sector(s): General industry and trade sector(40%), Central government administration(30%), Law and justice(20%), Micro- and SME finance(8%), Banking(2%)

Theme(s): Small and medium enterprise support(P), Regulation and competition policy(P), Export development and competitiveness(P), Other financial and private sector development(S), Standards and financial reporting(S)

Project Development Objectives:

The objective is to assist Moldova in enhancing the competitiveness of enterprises through an improvement in the business environment and making adequate standards-testing and quality-improvement services available to enterprises.

Progress toward achieving development objective(s):


While the overall assessment of results achieved since the project became effective some one and a half years ago remains positive, it is crucial that activities under all four components retain momentum as the project approached its mid-term point. Despite major progress to date (especially on the matching grant scheme), the utilization of project resources falls behind the agreed schedule. In this regards, close attention should be paid to the timely implementation of the Metrology, Standards, Testing, and Quality component, given its large size and technical complexity.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-H1870	Effective	5.08	0.42	4.64	0.00
JPN-55175	Effective	4.50	0.55	3.95	0.00
IDA-41190	Effective	5.08	0.35	4.71	0.00
JPN-54602	Closed	0.65	0.60	0.00	0.05



Status of Projects in Execution - FY07
EUROPE AND CENTRAL ASIA REGION

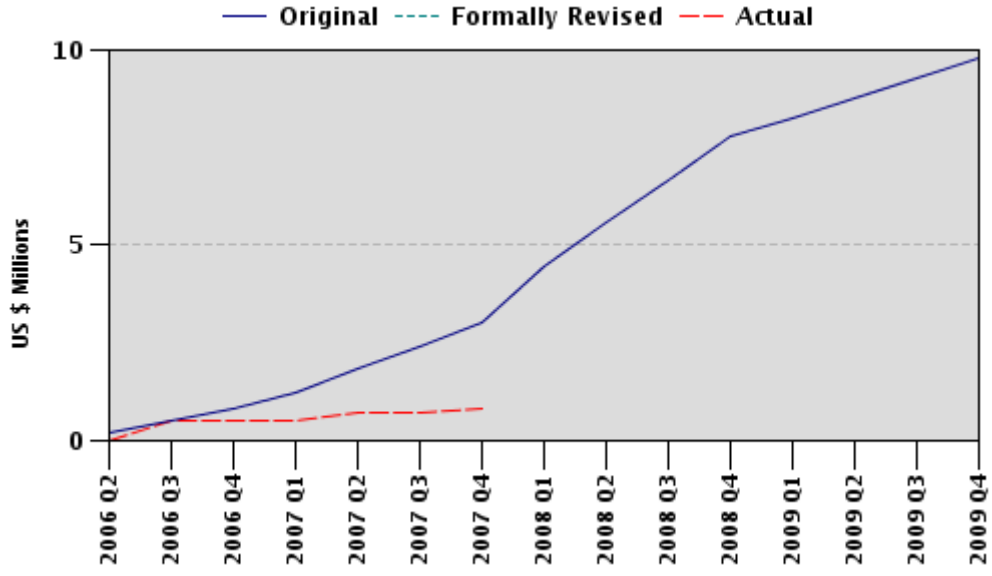

Project Name (ID): POPs Stockpiles Management and Destruction (P090037)

Country: Moldova

Board Approval Date : 12/15/2005

Closing Date : 05/31/2010

Loan/Credit/Grant Number : MULT-55875, MULT-53700

Sector(s): Central government administration(39%), Solid waste management(33%),
Petrochemicals and fertilizers(19%), Other industry(9%)

Theme(s): Pollution management and environmental health(P), Environmental policies
and institutions(S), Other environment and natural resources management(S)

Project Development Objectives:

The main development objective of the project is to protect the environment and human health by safely managing and disposing of stockpiles of persistent organic pollutants (POPs) contaminated pesticides and polychlorinated biphenyls (PCBs). The global project objective of the project is sustainable POPs stockpiles management and strengthening of the regulatory and institutional arrangements for long term control of POPs and other toxic substances in line with the requirements of the Stockholm Convention and other related conventions and protocols ratified by Moldova.

Progress toward achieving development objective(s):


The project is soundly on course to achieve its development objectives. POP and PCB clean-up activities have been advancing steadily, resulting in the reduction of the country's POP load and improved environmental conditions. At the same time, the foundation was set for establishing a modern chemical management system for long-term control of POPs and other toxic substances in the country.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-55875	Effective	6.35	1.67	4.68	0.00
MULT-53700	Closed	0.33	0.33	0.00	0.00



Status of Projects in Execution - FY07
EUROPE AND CENTRAL ASIA REGION

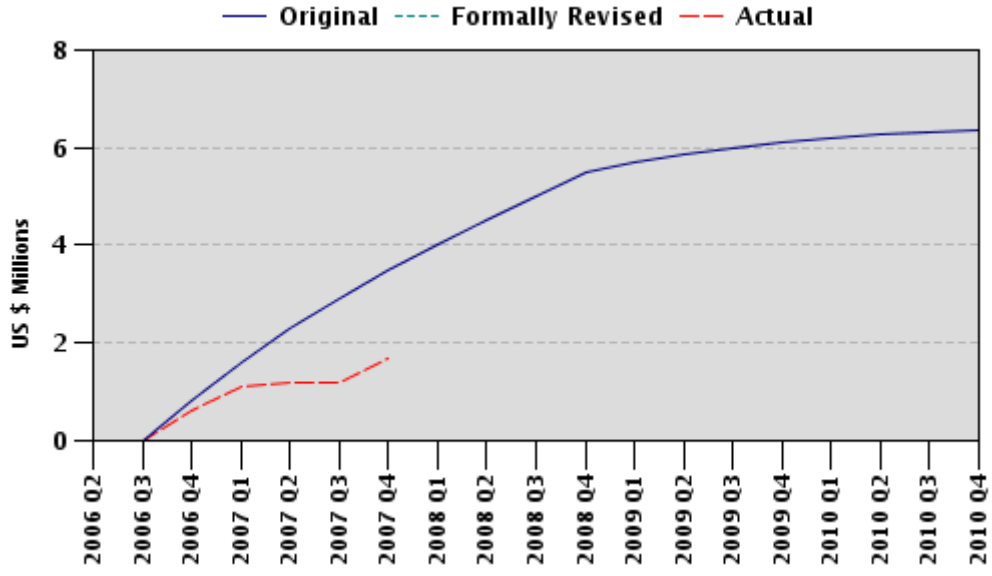

Project Name (ID): Quality Education in Rural Areas (P090340)

Country: Moldova

Board Approval Date : 03/14/2006

Closing Date : 05/31/2010

Loan/Credit/Grant Number : MULT-56717, IDA-41550, IDA-H2080, JPN-54601

Sector(s): Central government administration(35%), Secondary education(28%), Sub-national government administration(20%), Primary education(17%)

Theme(s): Education for all(P), Rural services and infrastructure(P), Education for the knowledge economy(S), Decentralization(S), Administrative and civil service reform(S)

Project Development Objectives:

The main objective of the project is to increase the quality of education in the rural areas of Moldova.

Progress toward achieving development objective(s):


The project has been under implementation for one year, and while it is still too early to report on tangible results against project objectives, progress has already been made with respect to some important project targets. For example, new curricula have been developed and teachers have been trained in the new curricula . Other project activities are proceeding on schedule, pointing to a high likelihood that the project objectives will be met.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-56717	Effective	4.40	0.62	3.78	0.00
IDA-41550	Effective	5.46	0.50	4.95	0.00
IDA-H2080	Effective	5.46	0.50	4.95	0.00
JPN-54601	Closed	0.50	0.33	0.00	0.17



Status of Projects in Execution - FY07
EUROPE AND CENTRAL ASIA REGION

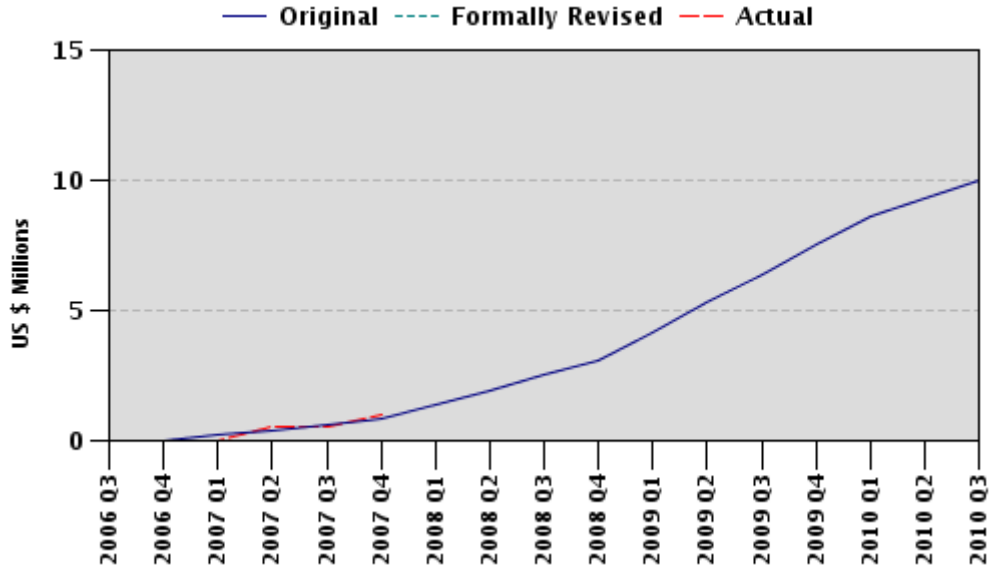

Project Name (ID): RISP (APL #2) (P090673)

Country: Moldova

Board Approval Date : 03/28/2006

Closing Date : 06/30/2010

Loan/Credit/Grant Number : IDA-Q5230, IDA-H2110, IDA-41570, JPN-54222, JPN-54603, SIDA-57273

Sector(s): General finance sector(56%), General agriculture, fishing and forestry sector(22%), General industry and trade sector(15%), General public administration sector(5%), Other social services(2%)

Theme(s): Administrative and civil service reform(P), Rural markets(P), Rural non-farm income generation(P), Rural services and infrastructure(P), Legal institutions for a market economy(S)

Project Development Objectives:

The proposed project is a second phase of the two-phased Adaptable Program Credit. The program's objective is to provide long-term support to accelerate agricultural recovery and growth so that Moldova's agricultural and rural sectors can play their full role in providing the underpinnings for future income growth and poverty reduction.

Progress toward achieving development objective(s):


The project is making substantial progress towards meeting its development objectives. The extension services are continuing their activities, with about 200,000 consulting services rendered; Development Agencies are working with 158 micro enterprises, 81 of which are already operational; the Government has introduced a new law on Savings and Associations to the Parliament; financial institutions are about to start their new training on environmental guidelines and have already made sub loans to 106 rural enterprises, representing approximately US\$8 million of investments.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-Q5230	Closed	0.66	0.00	0.66	0.00
IDA-H2110	Effective	7.88	2.79	5.06	0.00
IDA-41570	Effective	7.88	2.79	5.06	0.00
JPN-54222	Effective	1.73	1.25	0.47	0.00
JPN-54603	Closed	0.66	0.35	0.00	0.31
SIDA-57273	Effective	6.72	0.77	5.95	0.00



Status of Projects in Execution - FY07
EUROPE AND CENTRAL ASIA REGION

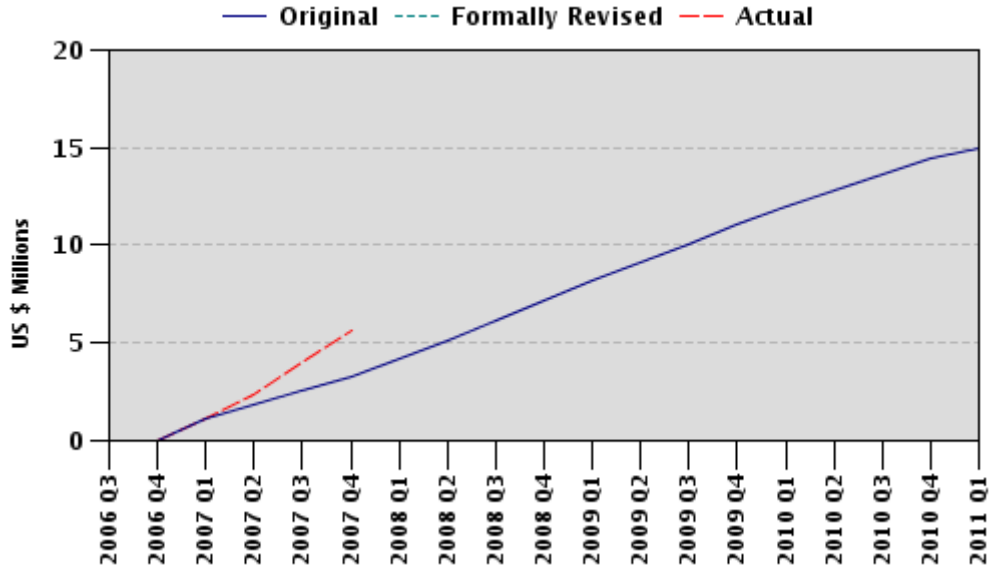

Project Name (ID): Health Services and Social Assistance (P095250)

Country: Moldova

Board Approval Date : 06/07/2007

Closing Date : 08/31/2011

Loan/Credit/Grant Number : JPN-55808, IDA-43200

Sector(s): Health(49%), Central government administration(31%), Other social services(15%), Compulsory health finance(5%)

Theme(s): Health system performance(P), Social safety nets(S), Social risk mitigation(S)

Project Development Objectives:

The overall project objective is to promote the government's program to increase access to quality and efficient health services with the aim of decreasing premature mortality and disability for the local population and improve the targeting of social transfers and services to the poor.

Progress toward achieving development objective(s):

The project loan was approved on June 7, 2007, and has not yet become effective. No tangible results to report at this time.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
JPN-55808	Effective	0.39	0.19	0.20	0.00
IDA-43200	Not Effective	17.13	0.00	17.13	0.00



Project Name (ID): Avian Flu (P099841)

Country: Moldova

Board Approval Date : 06/09/2006

Closing Date : 12/31/2009

Loan/Credit/Grant Number : IDA-41880, JPN-56630, IDA-H2330

Sector(s): General public administration sector(43%), Health(39%), Agricultural extension and research(12%), Other social services(3%), Animal production(3%)

Theme(s): Rural services and infrastructure(P), Other communicable diseases(P), Health system performance(S), Pollution management and environmental health(S), Participation and civic engagement(S)

Project Development Objectives:

The overall objective of the project is to minimize the threat posed to humans by the highly pathogenic avian influenza (HPAI). To achieve this, the project will support surveillance for outbreaks of this infection, preparation for outbreaks, and control of outbreaks among humans and animals.

Progress toward achieving development objective(s):


Early progress towards achieving the development objective of the project has been promising. Implementation results under the Animal and Human Health Components led to improvements in preparedness for diagnosis and mitigation of avian influenza outbreaks, both in birds and humans. The implementation of the Public Information and Awareness Component led to a substantial increase in awareness among the people of Moldova about the risks of and mitigation measures for avian influenza.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-41880	Effective	4.24	0.55	3.68	0.00
JPN-56630	Effective	0.50	0.15	0.35	0.00
IDA-H2330	Effective	4.24	0.55	3.68	0.00



Status of Projects in Execution - FY07
EUROPE AND CENTRAL ASIA REGION

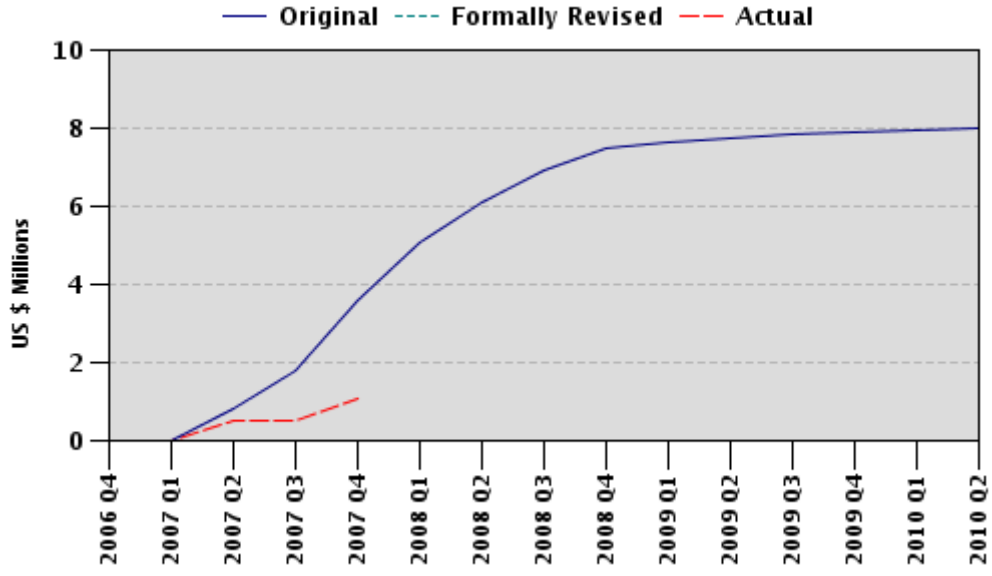

Project Name (ID): Road Sector Program Support Project (P100929)

Country: Moldova

Board Approval Date : 03/29/2007

Closing Date : 06/30/2011

Loan/Credit/Grant Number : IDA-42830, IDA-Q5520, JPN-57793

Sector(s): Roads and highways(81%), Central government administration(19%)

Theme(s): Trade facilitation and market access(P), Infrastructure services for private sector development(P), Injuries and non-communicable diseases(S), Administrative and civil service reform(S)

Project Development Objectives:

The project development objective is to reduce road transport costs for road users in Moldova by improving the condition and quality of its road network and the way it is managed.

Progress toward achieving development objective(s):

The project loan was not yet effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-42830	Not Effective	16.37	0.00	16.37	0.00
IDA-Q5520	Effective	0.80	0.00	0.80	0.00
JPN-57793	Effective	0.73	0.09	0.64	0.00

