

STATUS OF PROJECTS IN EXECUTION – FY07
SOPE
IRAQ

Operations Policy and Country Services
OCTOBER 10, 2007



Introduction

The Status of Projects in Execution (SOPE) Report for FY07 provides information on all IBRD/IDA projects that were active as of June 30, 2007. The World Bank has issued a SOPE Report every year as an internal communication to the Board of Executive Directors. In accordance with the Bank's revised disclosure policy, since FY02, the SOPE Report is available to the public.

The report is intended to bridge the gap in information available to the public between the Project Appraisal Document or Program Document, disclosed after the Bank approves a project, and the Implementation Completion Report, disclosed after the project closes.

In addition to the project progress description, the FY07 SOPE report¹ contains project level comparisons of disbursement estimates and actual disbursements, and a table showing the loan/credit/grant amount and disbursements to date.

¹ Notes:

- Amounts and Graphs for loans/credits/grants in currencies other than U.S. dollars may not match exactly due to exchange rate fluctuations over the life of the project.
- Disbursement graphs are not included for Development Policy Operations, which provide quick-disbursing financing to support policy and institutional reforms. For these operations, funds are disbursed in one or more stages (tranches), released when the borrower complies with agreed prior actions.
- Projects which are not yet effective may not have a planned disbursement schedule and thus will not include a graph.



Country: Iraq

Project Name (ID): Emergency Electricity (P087734)

Country: Iraq

Board Approval Date : 03/29/2007

Closing Date : 06/30/2011

Loan/Credit/Grant Number : IDA-42890

Sector(s): Power(86%), Central government administration(14%)

Theme(s): Conflict prevention and post-conflict reconstruction(P)

Project Development Objectives:


The objectives are to: (a) alleviate the current power supply shortfall by restoring the base load generation capacity of the Hartha Power Station Units 2 and 3 to 400 MW, and (b) lay the groundwork for improved power system planning and fuel supply by providing the tools and other support necessary to enhance in-house capability to prepare, implement and operate current and future projects.

Progress toward achieving development objective(s):

Significant progress has been achieved in preparing for the rehabilitation works, but progress could be delayed if the Credit does not become effective soon, which could in turn delay project completion and achievement of the development objectives.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-42890	Effective	125.03	0.00	125.03	0.00

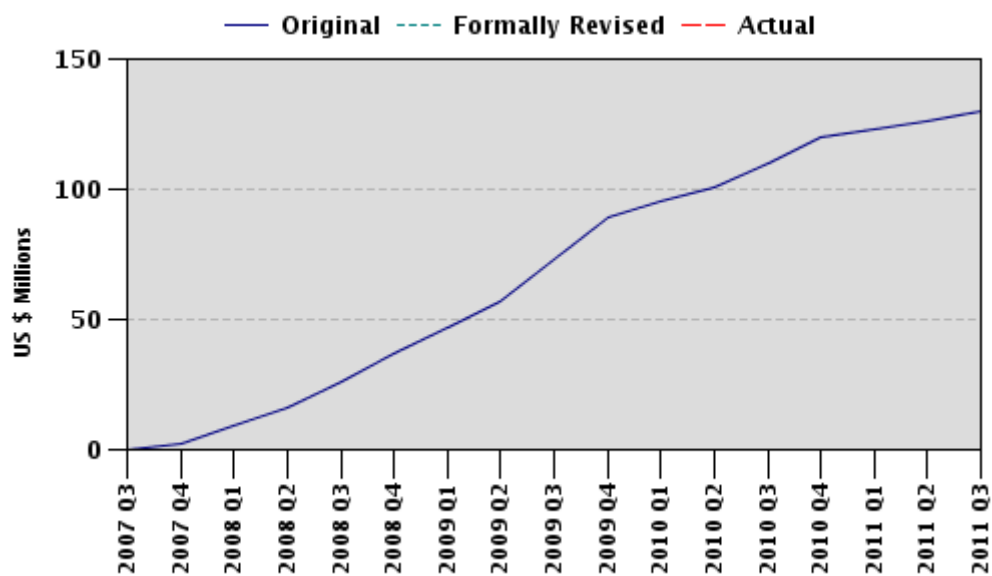

Project Name (ID): Emergency Road Rehabilitation (P087735)

Country: Iraq

Board Approval Date : 06/29/2006

Closing Date : 06/30/2010

Loan/Credit/Grant Number : IDA-42120

Sector(s): Roads and highways(98%), Central government administration(2%)

Theme(s): Rural services and infrastructure(P), Conflict prevention and post-conflict reconstruction(P), Improving labor markets(S), Injuries and non-communicable diseases(S)

Project Development Objectives:


The objective of the proposed Emergency Road Rehabilitation Project is to improve the condition of road assets by rehabilitating highly damaged segments of the country's highway and rural road networks, reestablishing critical river crossings, and restoring the capacity to manage and maintain road assets.

Progress toward achieving development objective(s):

Progress in preparing works under Part B (Northern Provinces) is moving ahead, but there has been no substantive progress for Part A (Central and Southern Provinces) activities. The Credit is not yet effective and this has delayed meaningful implementation.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-42120	Effective	141.25	0.00	141.25	0.00

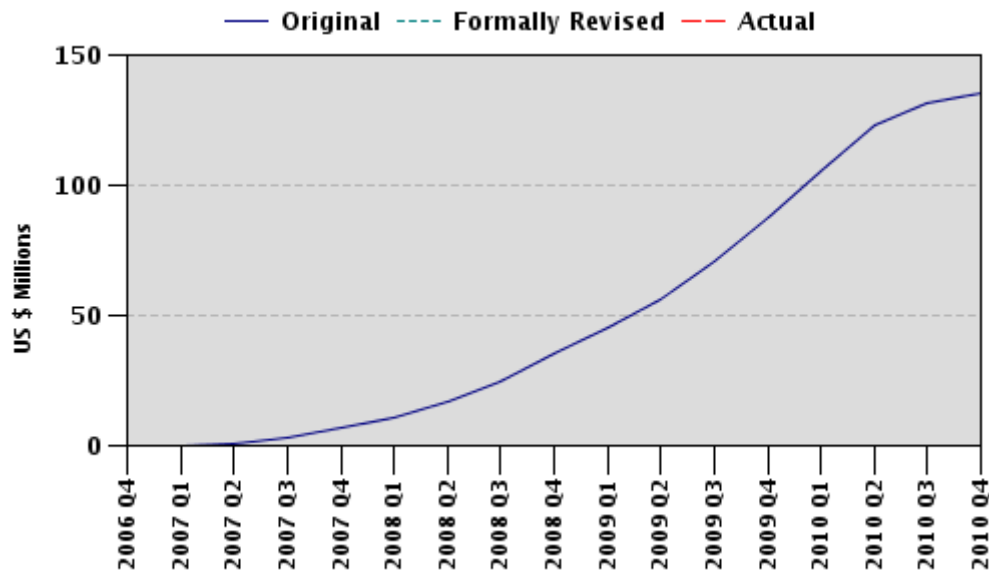

Project Name (ID): Third Emergency Education Project (P096234)

Country: Iraq

Board Approval Date : 11/29/2005

Closing Date : 01/31/2009

Loan/Credit/Grant Number : IDA-41280

Sector(s): Primary education(49%), Secondary education(49%), Central government administration(2%)

Theme(s): Education for all(P), Improving labor markets(S)

Project Development Objectives:

The principal objective of the project is to alleviate overcrowding in primary and secondary schools through school construction and provision of furniture and equipment. The project will also lay the groundwork for broader school reform and system reconstruction.

Progress toward achieving development objective(s):

The Financing Agreement was signed in April 2007; the project is not yet effective.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-41280	Not Effective	104.73	0.00	104.73	0.00



Project Name (ID): Dokan and Derbankdikhan Emergency Hydropower (P099059)

Country: Iraq

Board Approval Date : 12/12/2006

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IDA-42490

Sector(s): Renewable energy(100%)

Theme(s): Other public sector governance(P)

Project Development Objectives:

The objective is to: (a) help alleviate the current power supply shortfall in the Kurdish region through urgent repair work, (b) strengthen the capacity of local operational staff, and (c) prepare for the subsequent rehabilitation of the Dokan and Derbandikhan hydropower plants.

Progress toward achieving development objective(s):

Although the Credit is not effective yet, there has been substantial progress in preparing for the emergency repairs and the rehabilitation needs assessment. However, further delays and lack of upfront financing by the government could delay completion and, in turn, achievement of the Project Development Objectives.

Lending Information/Disbursement Summary (USD millions, as of June 30 2007)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-42490	Effective	40.92	0.00	40.92	0.00

