

STATUS OF PROJECTS IN EXECUTION – FY06
SOPE
REGION: AFRICA
REGIONAL PROJECTS

Operations Policy and Country Services
SEPTEMBER 19, 2006



Report on the Status of Projects in Execution - FY06
SOPE
Region: Africa
Regional Projects

Introduction

The Status of Projects in Execution (SOPE) Report for FY06 provides information on all IBRD/IDA projects that were active on June 30, 2006.

The World Bank has issued a SOPE Report every year as an internal communication to the Board of Executive Directors. In accordance with the Bank's revised disclosure policy, since FY02, the SOPE Report is available to the public.

The report is intended to bridge the gap in information available to the public between the Project Appraisal Document, disclosed after the Bank approves a project, and the Implementation Completion Report, disclosed after the project closes.

In addition to the project progress description, the FY06 SOPE report¹ contains project level comparisons of disbursement estimates and actual disbursements, and a table showing the loan/credit/grant amount and disbursements to date for all active projects.

¹ Notes:

- Amounts for Projects in currencies other than U.S. dollars may not match exactly due to exchange rate fluctuations over the life of the project.
- Disbursement graphs are not included for Development Policy Loans, which provide quick-disbursing external financing to support policy and institutional reforms. For these loans, funds are disbursed in one or more stages (tranches), released when the borrower complies with agreed conditions.
- Projects which are not yet effective may not have a planned disbursement schedule and thus may not include a graph.



Regional Projects: Africa

Project Name (ID): Regional Trade Facilitation Project (P063683)

Region: Africa

Board Approval Date : 04/03/2001

Midterm Review Date : 05/15/2006

Closing Date : 06/30/2011

Loan/Credit/Grant Number : IDA-34880, IDA-34881

Sector(s): Non-compulsory pensions, insurance and contractual savings (100%)

Theme(s): Regional integration (P), Trade facilitation and market access (P), Export development and competitiveness (S), International financial architecture (S)

Project Development Objectives:

The project's principal objective is to contribute to poverty alleviation through private sector led growth in participating countries by improving access to financing for productive transactions and cross-border trade. Furthermore, the project supports overall the institutional strengthening and initial operations of the African Trade Insurance Agency (ATI).


Progress toward achieving development objective(s):

A considerable amount of progress has been made towards achieving the project objective. The Board of Directors of The African Trade Insurance Agency (ATI) is supporting the restructuring of capital and the expansion of the product line to include comprehensive insurance. The increased capital, risk pooling and diversification allows ATI to leverage its capital and reinsure retained risks, thus enabling a higher volume of policies to be issued with the same amount of resources. In addition, the proposed structure would further strengthen the public-private partnership of this institution.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-34880	Closed	5.73	5.31	0.00	0.00
IDA-34881	Effective	4.85	0.00	4.85	0.00



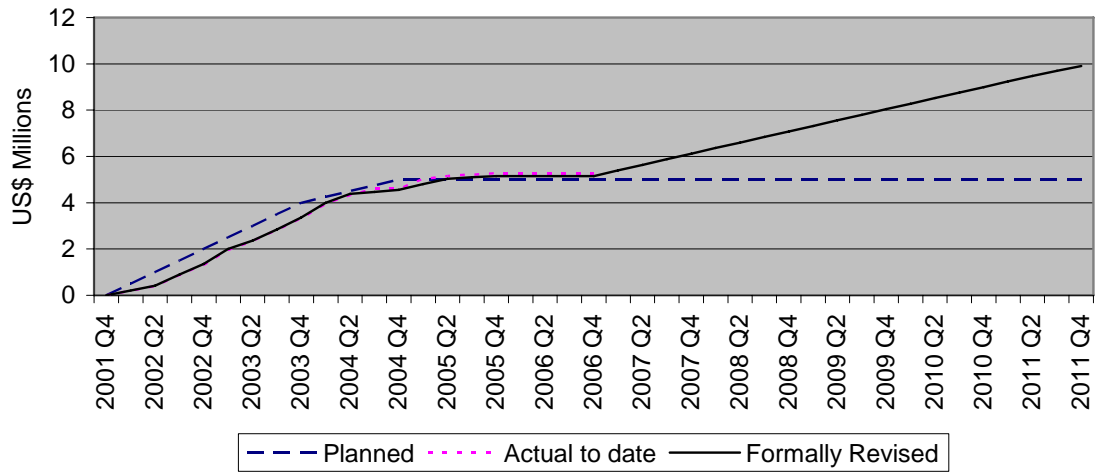

Project Name (ID): Senegal River Basin Water and Environmental Management Project (P064573)

Region: Africa

Board Approval Date : 10/28/2003

Midterm Review Date : 05/01/2006

Closing Date : 07/31/2008

Loan/Credit/Grant Number : MULT-52900, NETH-55192

Sector(s): Central government administration (75%), General agriculture, fishing and forestry (15%), General water, sanitation and flood protection (8%), Tertiary education (2%)

Theme(s): Water resources management (P), Environmental policies and institutions (P), Land administration and management (P), Regional integration (P), Participation and civic engagement (S)

Project Development Objectives:

The objective is to provide a participatory strategic environmental framework for the environmentally sustainable development of the Senegal River Basin, and to launch a basin wide cooperative program for transboundary land and water management.


Progress toward achieving development objective(s):

The project has moved steadily on meeting its objective as evidenced by Guinea recent inclusion in OMVS (Organisation pour la Mise en Valeur du Fleuve Sénégal). Moreover, OMVS and Guinea have harmonized their water legislation: Guinea's hydrology network in the Senegal Basin upstream portion has been fully assessed and upgraded to be compatible with the existing OMVS hydrology network. The framework for sustainable transboundary information exchange and knowledge sharing between the four riparian countries is underway: the basin wide hydrological reports have been prepared. The national Transboundary Diagnostic Analysis (TDA) was prepared and work for the Regional TDA is ongoing.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-52900	Effective	5.26	1.69	3.57	0.00
NETH-55192	Effective	12.29	1.27	10.96	0.00



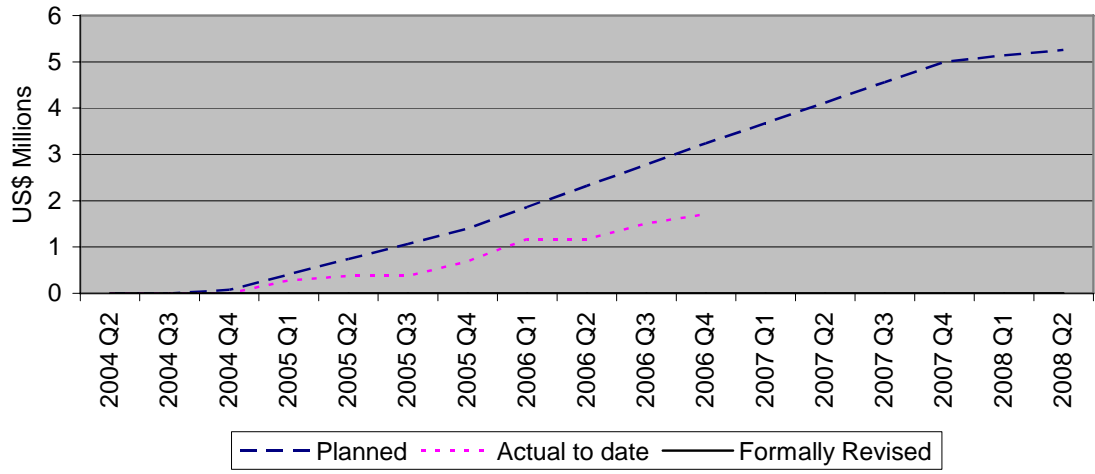

Project Name (ID): 3A-Southern Africa Power Market APL 1 (FY04) (P069258)

Region: Africa

Board Approval Date : 11/11/2003

Closing Date : 12/31/2007

Loan/Credit/Grant Number : IDA-38310, IDA-38320, IDA-Q3560, JPN-25658

Sector(s): Power (100%)

Theme(s): Regional integration (P), Infrastructure services for private sector development (P), Regulation and competition policy (P), Export development and competitiveness (S)

Project Development Objectives:

The project objective is to facilitate development of an efficient regional power market which would result in: (i) increased competition and deceleration of increases in electricity prices in SADC (Southern African Development Community) countries; (ii) increased industrial competitiveness of the region; (iii) improved conditions for investment in the power sector; and (iv) increased regional integration


Progress toward achieving development objective(s):

The financial disbursements did not occur as foreseen and the project is still in the preliminary stages. Nevertheless, in terms of technical assistance, the following achievements were registered: Feasibility and environmental studies for the potential interconnection between Zambia and Tanzania have been completed. The three countries, with the support of The African Development Bank have appointed a Transactions Adviser to prepare the necessary documentation for private sector venture in a Public-Private Partnership arrangement. The review of the draft pre-qualification documents for the Democratic Republic of Congo (DRC) - Zambia transmission line interconnection, and associated telecommunications systems, is in progress by the World Bank. The main issues relating to the adequacy of generation capacity to meet the export objective are being addressed through ongoing dialogue with the Government of the Democratic Republic of Congo.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-38310	Effective	189.92	2.53	187.40	0.00
IDA-38320	Effective	1.18	0.90	0.28	0.00
IDA-Q3560	Closed	0.90	0.00	0.00	0.90
JPN-25658	Closed	0.62	0.23	0.38	0.00



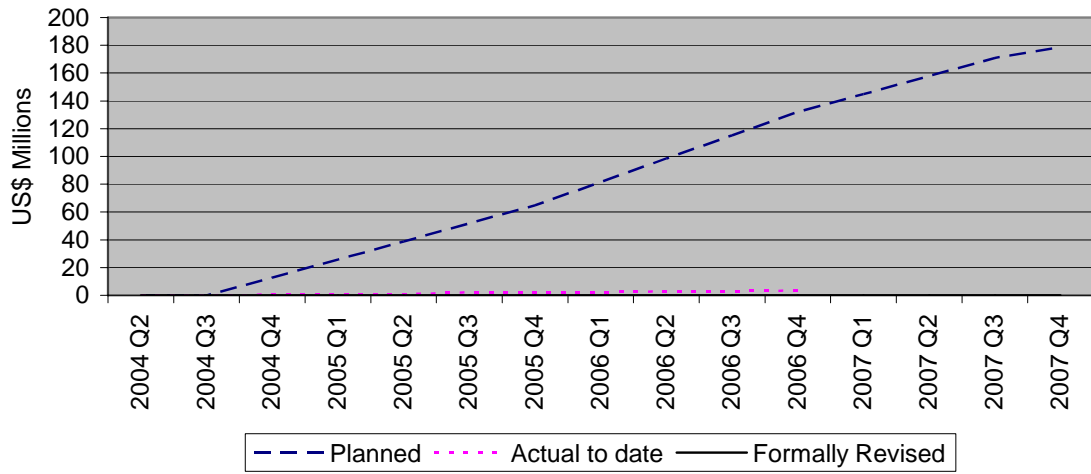

Project Name (ID): Nile Transboundary Environmental Action Project (P070073)
Region: Africa
Board Approval Date : 04/08/2003
Midterm Review Date : 12/31/2006
Closing Date : 09/30/2008
Loan/Credit/Grant Number : MULT-51539, MULT-52133
Sector(s): General water, sanitation and flood protection (100%)
Theme(s): Water resources management (P), Environmental policies and institutions (P), Pollution management and environmental health (P), Biodiversity (P)

Project Development Objectives:

The project aims at creating more effective basin-wide stakeholder cooperation on transboundary environmental issues by: (A) enhancing the analytical capacity for a basin-wide perspective to support the sustainable development, management, and protection of Nile Basin water; and (B) engaging the full spectrum of stakeholders in the management and protection of the Basin's shared resources.


Progress toward achieving development objective(s):

The project is making significant progress towards meeting its development objectives, despite the complexities and delays inherent in a nine country technical assistance program. Institutional mechanisms for project implementation are established in all Nile Basin Initiative (NBI) countries. Substantial increase in awarding first rounds of micro grants was registered. The actions taken in support of the two Nile Sub-basin programs (Eastern Nile and Nile Equatorial Lakes) include: outreach and environmental education, piloting watershed management interventions through community micro grants, and planning to provide advisory services for upstreaming environmental and social issues in the investment planning.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-51539	Effective	8.00	1.61	6.39	0.00
MULT-52133	Effective	7.18	1.81	5.37	0.00



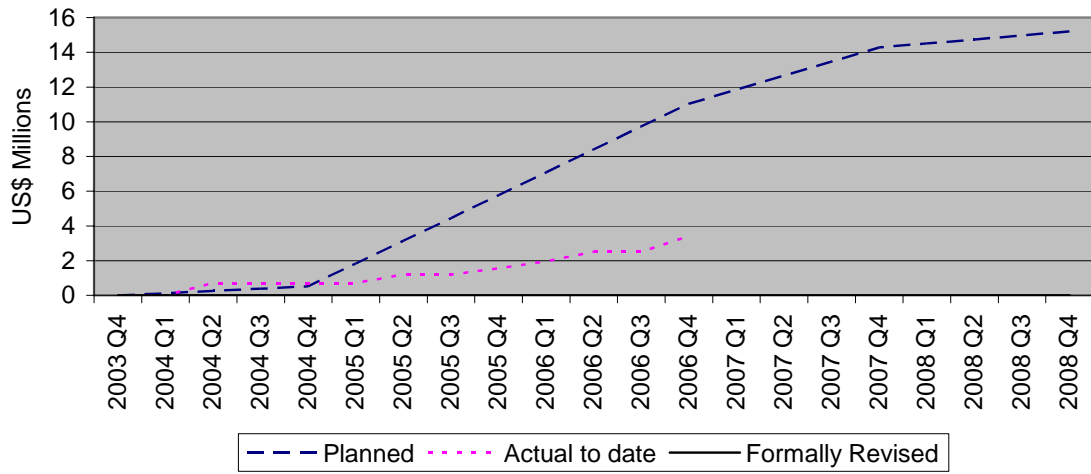

Project Name (ID): Reversal of Land and Water Degradation Trends in the Lake Chad Basin Ecosystem (P070252)

Region: Africa

Board Approval Date : 01/21/2003

Midterm Review Date : 09/18/2006

Closing Date : 01/21/2008

Loan/Credit/Grant Number : MULT-52140

Sector(s): Central government administration (50%), Irrigation and drainage (25%), General water, sanitation and flood protection (25%)

Theme(s): Water resources management (P), Land administration and management (P)

Project Development Objectives:


The project's overall development objective is to contribute to the sustainable management of land and water resources in the greater conventional basin of Lake Chad (including Cameroon, Central African Republic, Chad, Niger and Nigeria).

Progress toward achieving development objective(s):

The member countries have endorsed the Action Program for Reform of The Lake Chad Basin Commission (LCBC). The major milestones of the project are on schedule, i.e. completion of the Transboundary Diagnostic Analysis in December 2006, completion of the Strategic Action Plan in December 2007, and donor support for financing of the Strategic Action Plan mobilized by mid 2008. At this stage, there is confidence that the project will achieve its objectives.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-52140	Effective	2.90	0.53	2.37	0.00

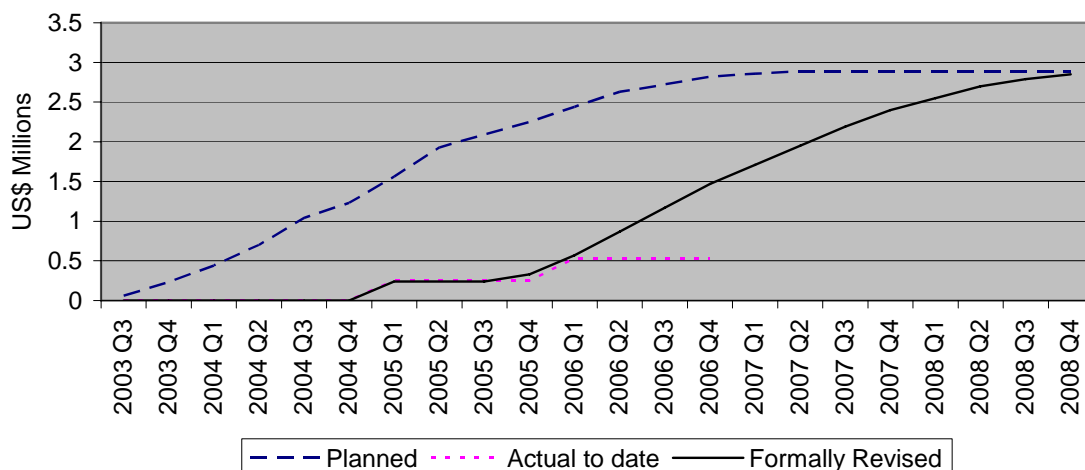

Project Name (ID): Reversing Land and Water Degradation Trends in the Niger River Basin (P070256)

Region: Africa

Board Approval Date : 05/20/2004

Midterm Review Date : 05/31/2006

Closing Date : 08/31/2009

Loan/Credit/Grant Number : MULT-53233, NETH-50530

Sector(s): Central government administration (100%)

Theme(s): Land administration and management (P), Water resources management (P), Regional integration (P), Biodiversity (S), Environmental policies and institutions (S)

Project Development Objectives:

The objective is to provide the nine riparian countries an opportunity to define a transboundary framework for the sustainable development of the Niger Basin, through strengthened capacity and better understanding of the Basins land and water resources. The project will also effectively support an inclusive decision-making process for basin level transboundary environmental planning to reverse land and water degradation in the basin.


Progress toward achieving development objective(s):

Progress towards meeting the development objectives is on track. An effective Regional Unit is in place within the Niger Basin Authority. This Unit coordinates the National Project Teams in the nine member countries, hence strengthening the transboundary framework for the sustainable development of the Niger Basin. A regional training on Transboundary Diagnostic Analysis (TDA) has been completed in May 2006 and national TDAs are under preparation in the four countries where they are not available. Capacity Building and Public Awareness plans are under preparation to raise awareness at local, national and regional levels.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-53233	Effective	6.00	1.27	4.73	0.00
NETH-50530	Closed	0.59	0.59	0.00	0.00



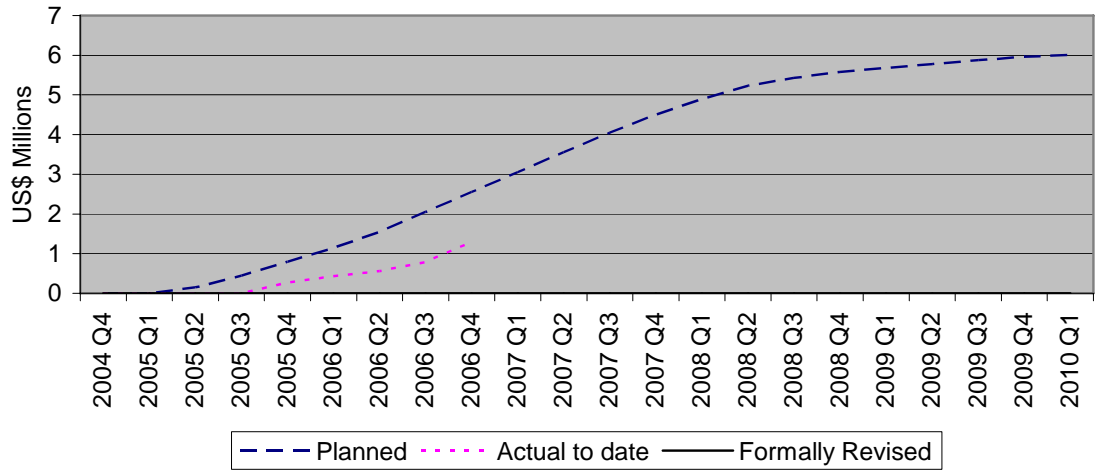

Project Name (ID): 3A-GEF Groundwater & Drought Mgmt TAL (FY05) (P070547)
Region: Africa
Board Approval Date : 06/14/2005
Midterm Review Date : 11/19/2007
Closing Date : 11/30/2009
Loan/Credit/Grant Number : MULT-27934, MULT-55090
Sector(s): Central government administration (100%)
Theme(s): Water resources management (P), Environmental policies and institutions (S)

Project Development Objectives:


The objective is to develop consensus among Member States for a regional strategic approach to support and enhance their capacities in defining drought management policies, specifically in relation to the role, availability, recharge and supply potential for ground water resources.

Progress toward achieving development objective(s):

The project became effective in the latter part of the reporting period and was still in too early a stage for meaningful progress.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
MULT-27934	Closed	0.35	0.33	0.00	0.02
MULT-55090	Effective	7.00	0.00	7.00	0.00

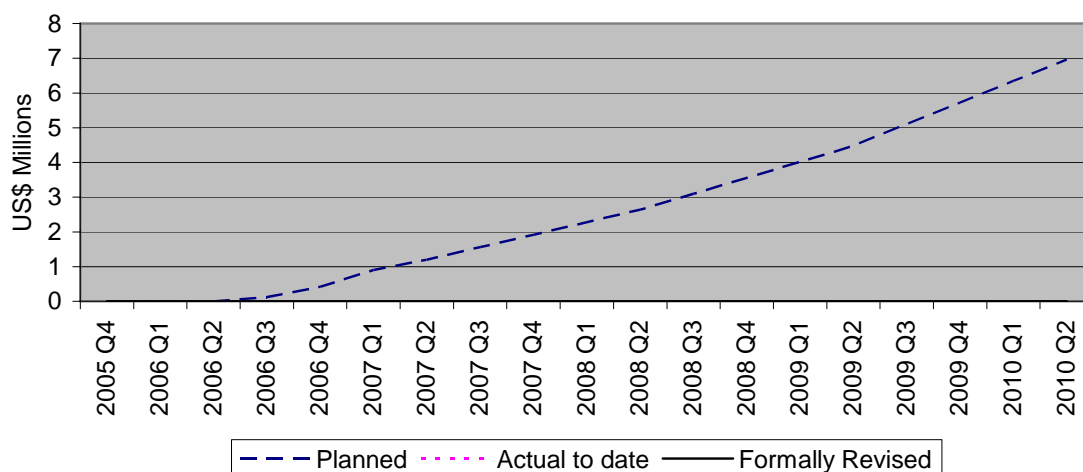

Project Name (ID): 3A-BEAC Regional Payment System (FY03) (P072881)

Region: Africa

Board Approval Date : 07/30/2002

Midterm Review Date : 09/15/2006

Closing Date : 12/31/2006

Loan/Credit/Grant Number : IDA-37040, IDA-Q2770

Sector(s): Payment systems, securities clearance and settlement (52%), Banking (40%), Telecommunications (6%), Law and justice (2%)

Theme(s): Other financial and private sector development (P), Infrastructure services for private sector development (P), Regional integration (P), Legal institutions for a market economy (S), Technology diffusion (S)

Project Development Objectives:

The project aims to improve the efficiency and security of the payment system in the Central African Economic and Monetary Union. This will be achieved by establishing and installing an appropriate set of regional payment mechanisms to satisfy the evolving needs of all market sectors.


Progress toward achieving development objective(s):

Project implementation is progressing well towards achieving the development objectives. Contracts have been awarded for the three main systems (large payment, electronic clearing and card system), and systems development is already at the installation phase for two of them, and in the design phase for the third one. The joint Central Bank-Commercial Bank-Ministries of Finance Committee in charge of harmonizing regulation and practices has been meeting regularly and good progress has been achieved. Similarly, work is advancing on developing a registry for payment incidents, with the selection of a supplier for an automated system.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-37040	Effective	17.20	9.36	7.91	0.00
IDA-Q2770	Closed	0.55	0.00	0.00	0.55



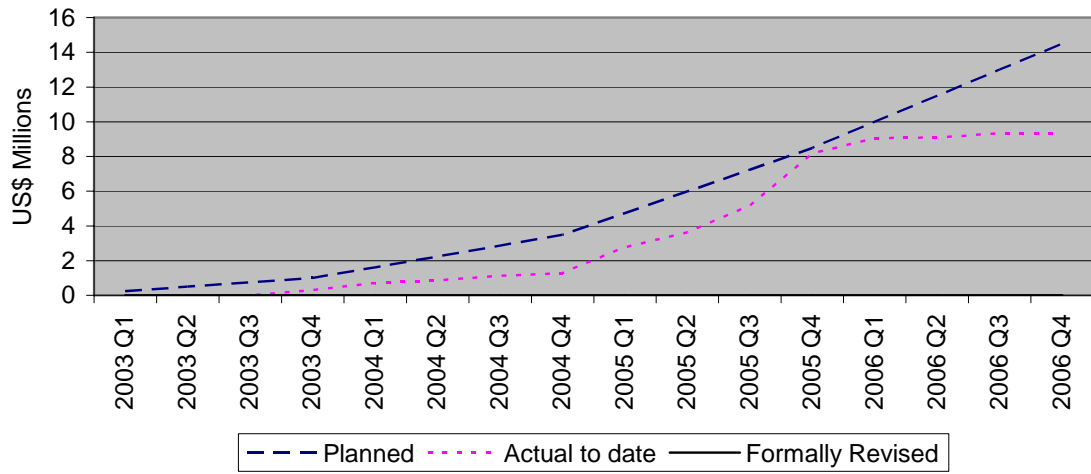

Project Name (ID): WAEMU CAPITAL MARKET DEVELOPMENT PROJECT (P074525)

Region: Africa

Board Approval Date : 02/26/2004

Midterm Review Date : 07/31/2007

Closing Date : 09/30/2009

Loan/Credit/Grant Number : IDA-38630

Sector(s): Capital markets (58%), Roads and highways (42%)

Theme(s): Regional integration (P), Other financial and private sector development (S)

Project Development Objectives:

The objective is to develop the capital markets in the West Africa Economic and Monetary Union (WAEMU), and mobilize public and private financing for the region's infrastructure development. The project is expected to contribute to WAEMU countries' efforts to achieve sustainable regional economic growth through the provision of efficient, region-wide infrastructure services and greater financial market integration.


Progress toward achieving development objective(s):

After less than one year of effectiveness, first activities have started towards achieving the project development objectives. In terms of mobilizing financing for the region, the West African Development Bank (BOAD) dedicated US\$10 million to a line of credit to the regional mortgage corporation which is expected to be created at the end of 2006. For the region's infrastructure development, road construction will start soon (on eight road project proposals received to date). Guinea Bissau and Niger have fully ratified the Guarantee Facility Agreement as a first step towards greater financial market integration. BOAD has drafted the marketing strategy for the guarantee facility. However, the identification of two guarantee projects continues to be a challenge.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-38630	Effective	98.49	0.39	98.09	0.00



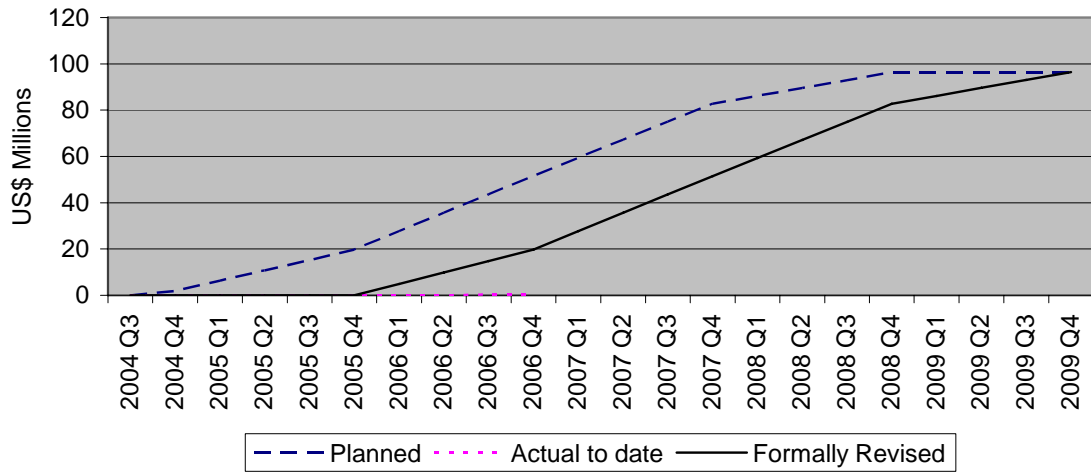

Project Name (ID): HIV/AIDS PROJECT FOR ABIDJAN - LAGOS TRANSPORT CORRIDOR (P074850)

Region: Africa

Board Approval Date : 11/13/2003

Midterm Review Date : 01/23/2006

Closing Date : 07/01/2007

Loan/Credit/Grant Number : IDA-H0660, IDA-Q3510

Sector(s): Health (41%), Other social services (32%), Central government administration (27%)

Theme(s): HIV/AIDS (P), Social risk mitigation (S), Other communicable diseases (S), Regional integration (S), Trade facilitation and market access (S)

Project Development Objectives:

The objective is to increase access to HIV/AIDS prevention, basic treatment, support and care services by underserved vulnerable groups along the Abidjan-Lagos transport corridor, with particular attention to transport workers, the migrant population, commercial sex workers and the local population.


Progress toward achieving development objective(s):

The project development objectives are likely to be achieved. Significant efforts have been made to improve access to HIV/AIDS prevention, treatment, care and support through various awareness campaigns. Additionally, 25 health centers have been rehabilitated and 11 voluntary counseling and testing centers are functioning. The number of people who use testing centers along the transport corridor has increased, and health facilities report adequate supply of antibiotics for the treatment. Construction of information booths at all borders is underway and has been completed in Togo. Leaflets have been distributed, posters published, and billboards installed to inform and assist truckers and travelers. Furthermore, all the countries concerned have adopted a common HIV/AIDS strategy for the transport corridor.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-H0660	Effective	17.93	11.24	6.67	0.00
IDA-Q3510	Closed	0.35	0.00	0.00	0.35



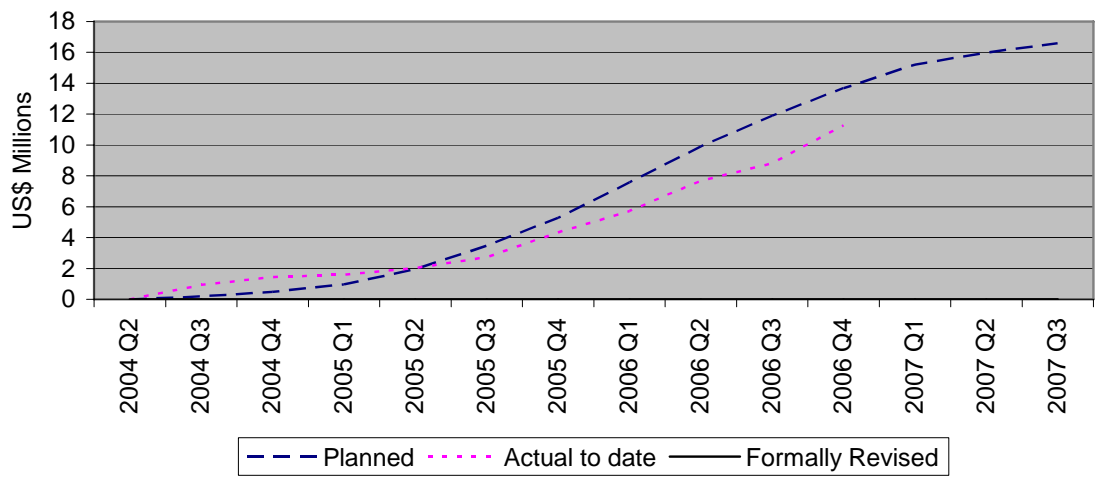

Project Name (ID): WAPP APL 1 (1st Phase - COASTAL TRANSMISSION BACKBONE) (P075994)

Region: Africa

Board Approval Date : 06/30/2005

Midterm Review Date : 06/11/2007

Closing Date : 12/31/2009

Loan/Credit/Grant Number : IDA-40920, IDA-Q3910

Sector(s): Power (100%)

Theme(s): Regional integration (P), Infrastructure services for private sector development (S)

Project Development Objectives:


The key objective of the WAPP (West Africa Power Pool) is to establish a well-functioning, cooperative, power pooling mechanism among national power utilities of ECOWAS (Economic Community of West African States) member states, based on a transparent and harmonized legal, policy, regulatory and commercial framework.

Progress toward achieving development objective(s):

The project became effective in the middle of the reporting period but was still in too early a stage for meaningful implementation progress.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-40920	Effective	38.95	0.00	38.95	0.00
IDA-Q3910	Closed	0.80	0.00	0.00	0.80

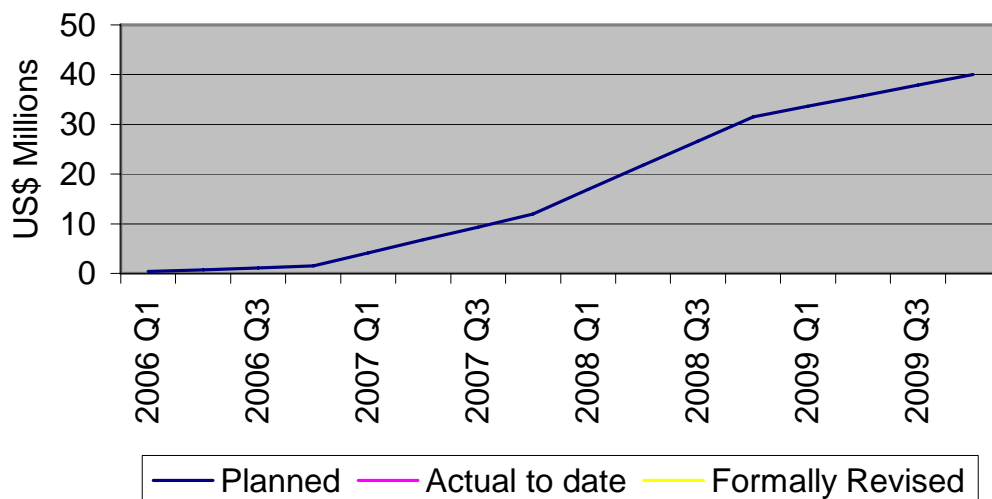

Project Name (ID): East Africa Trade and Transport Facilitation Project (P079734)

Region: Africa

Board Approval Date : 01/24/2006

Midterm Review Date : 01/24/2008

Closing Date : 09/30/2011

Loan/Credit/Grant Number : IDA-41470, IDA-41480, IDA-41490, IDA-H2020

Sector(s): General transportation (38%), Railways (37%), General public administration (13%), Ports, waterways and shipping (12%)

Theme(s): Trade facilitation and market access (P), Regional integration (P), Regulation and competition policy (S), Improving labor markets (S), Social risk mitigation (S)

Project Development Objectives:

The Project Development Objectives are: (i) improve trade environment through the effective implementation of the East Africa Community Customs Union Protocol; (b) enhance transport logistics services efficiency along key corridors by reducing non tariff barriers and uncertainty of transit time; and (c) improve railway services in Kenya and Uganda.

Progress toward achieving development objective(s):

The project had just become effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-41470	Effective	26.75	0.00	26.75	0.00
IDA-41480	Effective	122.45	0.00	122.45	0.00
IDA-41490	Effective	37.48	0.00	37.48	0.00
IDA-H2020	Effective	15.29	0.00	15.29	0.00



Project Name (ID): African Regional Capacity Building Network for HIV/AIDS Prevention, Treatment, and Care (P080406)

Region: Africa

Board Approval Date : 09/22/2004

Midterm Review Date : 02/26/2007

Closing Date : 06/30/2009

Loan/Credit/Grant Number : IDA-H1290, IDA-Q4120

Sector(s): Health (85%), Central government administration (15%)

Theme(s): HIV/AIDS (P)

Project Development Objectives:


The development objective of ARCAN is to expand access to comprehensive and evidence-based prevention, treatment, and care programs through improved training of health practitioners.

Progress toward achieving development objective(s):

After a number of difficulties experienced since project effectiveness in February 2005, steps have now been taken for implementation to finally start. The new Project Coordinating Unit staff recruited in May 2006 have produced a detailed workplan for June - December 2006 which includes implementation of a full cycle of project activities, and focuses on support to five training institutions.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-H1290	Effective	10.14	2.32	7.89	0.00
IDA-Q4120	Closed	0.32	0.00	0.00	0.32

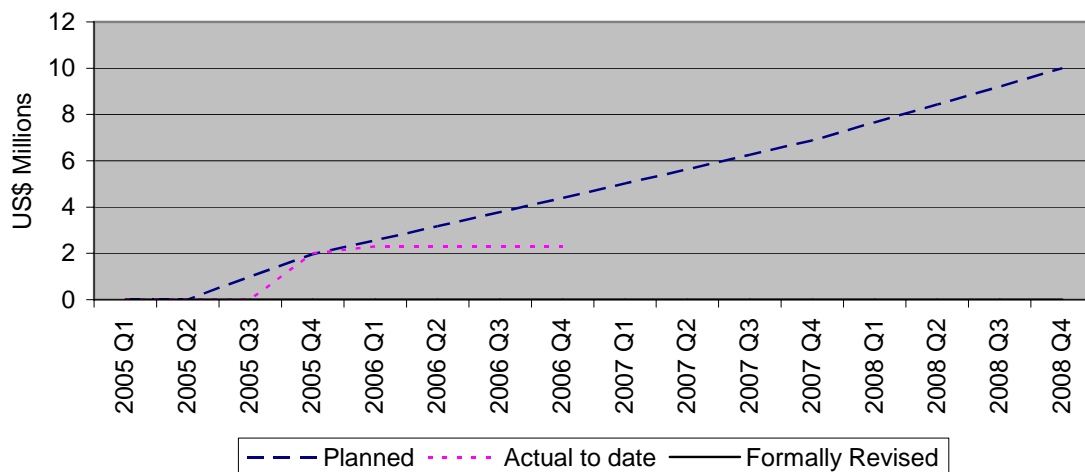

Project Name (ID): Great Lakes Initiative on HIV/AIDS (GLIA) Support (P080413)

Region: Africa

Board Approval Date : 03/15/2005

Midterm Review Date : 10/31/2007

Closing Date : 03/31/2009

Loan/Credit/Grant Number : IDA-H1500, IDA-Q4540, IDA-Q4541

Sector(s): Other social services (60%), Central government administration (40%)

Theme(s): HIV/AIDS (P), Health system performance (S), Gender (S), Other communicable diseases (S), Population and reproductive health (S)

Project Development Objectives:


The objective is to establish and coordinate HIV/AIDS prevention, care, treatment, and mitigation programs for mobile and vulnerable groups within the Great Lakes Region states.

Progress toward achieving development objective(s):

The project became effective at the end of the reporting period but was still in too early a stage for meaningful implementation progress.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-H1500	Effective	20.14	2.05	18.09	0.00
IDA-Q4540	Closed	0.60	0.00	0.60	0.00
IDA-Q4541	Closed	0.42	0.00	0.42	0.00

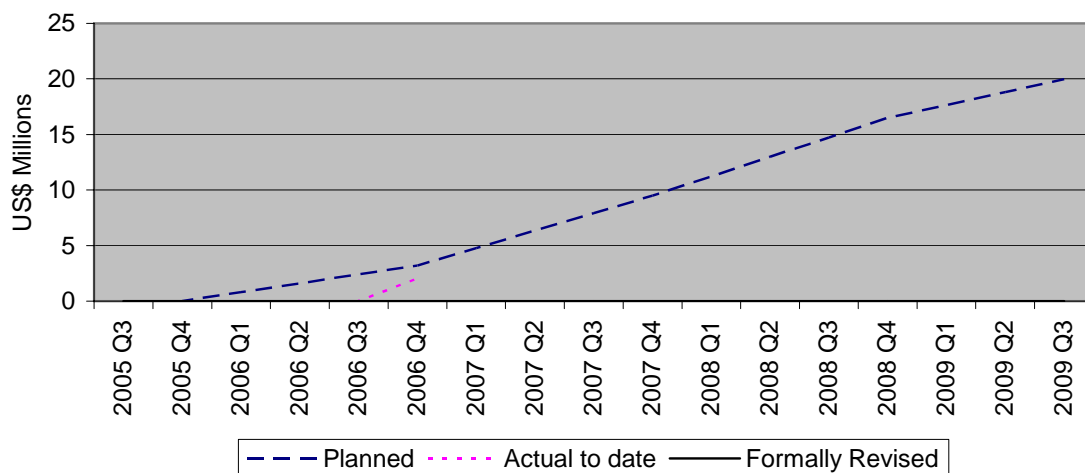

Project Name (ID): Regional HIV/AIDS Treatment Acceleration Project (P082613)

Region: Africa

Board Approval Date : 06/17/2004

Midterm Review Date : 06/10/2006

Closing Date : 09/30/2007

Loan/Credit/Grant Number : IDA-H1040, IDA-H1050, IDA-H1060, IDA-H1080, IDA-H1090

Sector(s): Health (65%), Central government administration (35%)

Theme(s): HIV/AIDS (P), Other communicable diseases (S), Population and reproductive health (S), Nutrition and food security (S), Social risk mitigation (S)

Project Development Objectives:

The project's objective is to pilot strategies for strengthening each country's capacity to scale up comprehensive HIV/AIDS programs providing care and treatment, which is effective, affordable, and equitable.

Progress toward achieving development objective(s):

The progress towards learning from the pilot strategies has been satisfactory since the elaboration of the project's learning agenda during a tri-partite meeting between World Bank, United Nations Economic Commission for Africa and World Health Organization in Nairobi in June 2005. As a consequence, regional meetings between the three international facilitators and the three participating countries (Burkina Faso, Ghana, and Mozambique) have been better focused on the project's the learning purposes: Initial lessons are exchanged and applied among the three countries – e.g., as to routine testing for HIV for pregnant mothers in order to increase the uptake for Prevention of Mother-to-Child Transmission program.


Research activities have started in all 3 countries: In Burkina Faso e.g., the general population survey (conducted by the National Institute of Statistics & Demography) was prepared in FY06, including questions on HIV and treatment. (The Bank has added a section in the questionnaire and the project is financing part of it). In Ghana and Mozambique, as well, questions on HIV and treatment were included into the general population surveys. In Ghana, specifically, data for a behavioral surveillance survey were collected in March/April 06, and an HIV/AIDS & antiviral therapy section will be included into a more general health facility/human resources survey. In Mozambique, the preparations for a baseline household survey and a baseline health facility survey are underway.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-H1040	Effective	21.17	6.10	15.17	0.00
IDA-H1050	Effective	15.14	4.73	10.46	0.00



IDA-H1060	Effective	18.37	7.24	11.15	0.00
IDA-H1080	Effective	2.06	1.27	0.81	0.00
IDA-H1090	Effective	4.12	0.43	3.68	0.00

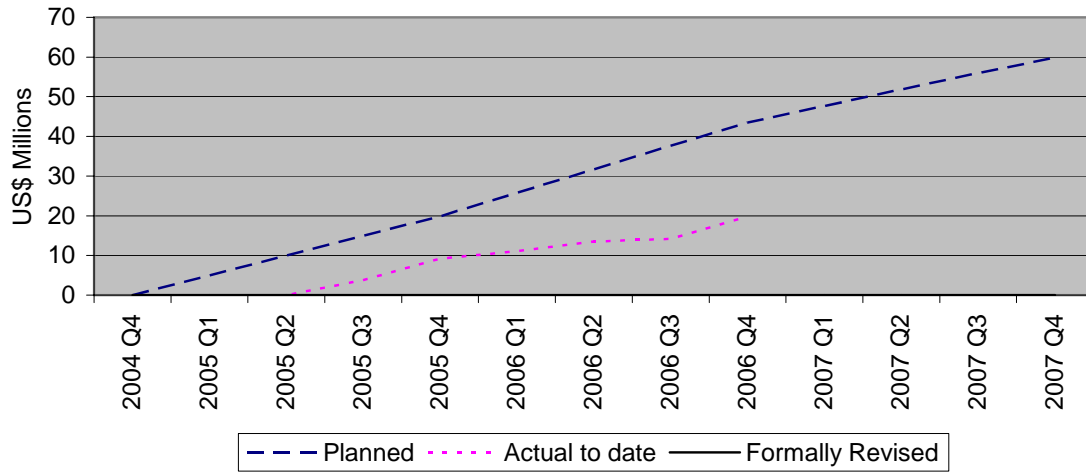

Project Name (ID): West and Central Africa Air Transport Safety & Security Project (P083751)

Region: Africa

Board Approval Date : 04/27/2006

Midterm Review Date : 06/30/2008

Closing Date : 12/31/2009

Loan/Credit/Grant Number : IDA-41630, IDA-41640, IDA-H2140, IDA-H2150

Sector(s): Aviation (94%), Central government administration (6%)

Theme(s): Regional integration (P), Trade facilitation and market access (P), Regulation and competition policy (S), Infrastructure services for private sector development (S)

Project Development Objectives:

The Project Development Objectives are: (i) Improve Civil Aviation Authorities' (CCAs) compliance with International Civil Aviation Organization (ICAO) safety standards; (b) Increase CAAs' compliance with ICAO's security standards; (c) Enhance main international airports' compliance with ICAO's security standards.

Progress toward achieving development objective(s):

The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-41630	Not Effective	6.61	0.00	6.61	0.00
IDA-41640	Not Effective	5.59	0.00	5.59	0.00
IDA-H2140	Not Effective	14.99	0.00	14.99	0.00
IDA-H2150	Not Effective	7.20	0.00	7.20	0.00



Project Name (ID): Africa Emergency Locust Project (P092473)

Region: Africa

Board Approval Date : 12/16/2004

Midterm Review Date : 12/11/2006

Closing Date : 06/30/2009

Loan/Credit/Grant Number : IDA-40190, IDA-40200, IDA-40210, IDA-40220, IDA-40230, IDA-40240, IDA-40250, IDA-Q4450, IDA-Q4460, IDA-Q4470, IDA-Q4480, IDA-Q4490, IDA-Q4500, IDA-Q4510

Sector(s): Crops (50%), Central government administration (30%), Agricultural extension and research (10%), Other social services (10%)

Theme(s): Natural disaster management (P), Pollution management and environmental health (S), Other rural development (S), Social safety nets (S), Regional integration (S)

Project Development Objectives:

The objective is to reduce the vulnerability of the concerned countries to present and future locust infestations by supporting improved strategies for prevention, early warning, reaction and mitigation, both at the national level and at the regional level.

Progress toward achieving development objective(s):

During the Desert Locust campaign of 2005/2006, survey and control activities have been implemented by the seven countries according to multi donors supported contingency plans. A reduced degree of infestation has been observed during this campaign, and countries have started investments for the long term (infrastructure, equipment and capacity building), in order to strengthen the early warning and prevention system.


At the regional front, the Bank has successfully pursued collaboration with Food and Agriculture Organization of the United Nations (FAO) and Commission for Locust Control in the Western Region, through the co-organization of regional workshops. The multi-donor supported Regional Locust Prevention Program meeting, held in February 2006 in Alger, has resulted in regional and country action plans for four years, which aims at strengthening the early warning and prevention system in West and North Africa. The Bank and the FAO have also co-organized a regional workshop for management of surplus of pesticides in the region (1,200 tons in the Sahel), and made recommendations to prevent that pesticides become obsolete.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-40190	Effective	8.38	1.70	6.67	0.00
IDA-40200	Effective	8.97	1.32	7.62	0.00
IDA-40210	Effective	1.91	0.22	1.69	0.00
IDA-40220	Effective	10.00	1.75	8.22	0.00
IDA-40230	Effective	10.44	0.83	9.61	0.00
IDA-40240	Effective	9.85	1.96	7.89	0.00
IDA-40250	Effective	9.85	2.44	7.42	0.00
IDA-Q4450	Closed	1.60	0.00	0.00	1.60



IDA-Q4460	Closed	0.86	0.00	0.00	0.86
IDA-Q4470	Closed	2.00	0.00	0.00	2.00
IDA-Q4480	Closed	1.93	0.00	0.00	1.93
IDA-Q4490	Closed	2.00	0.00	0.00	2.00
IDA-Q4500	Closed	2.00	0.00	0.00	2.00
IDA-Q4510	Closed	2.00	0.00	0.00	2.00

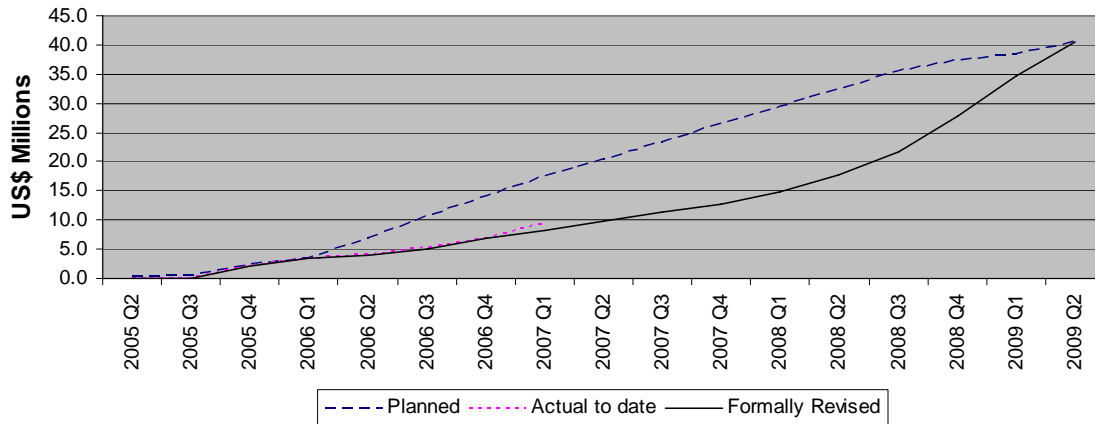

Project Name (ID): Senegal River Basin Multi-purpose Water Resources Development Project (P093826)

Region: Africa

Board Approval Date : 06/08/2006

Closing Date : 09/08/2011

Loan/Credit/Grant Number : IDA-41820, IDA-41830, IDA-41840, IDA-H2310, IDA-Q4890, IDA-Q4891

Sector(s): General water, sanitation and flood protection (27%), Health (22%), Irrigation and drainage (22%), Animal production (22%), Central government administration (7%)

Theme(s): Water resources management (P), Regional integration (P), Land administration and management (S), Pollution management and environmental health (S), Administrative and civil service reform (S)

Project Development Objectives:

The project development objective is to enhance regional integration among the riparian countries of the Senegal River Basin through OMVS (Organisation pour la Mise en Valeur du Fleuve Sénégal) for multi-purpose water resources development to foster growth including improved community livelihoods.

Progress toward achieving development objective(s):

The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-41820	Not Effective	30.87	0.00	30.87	0.00
IDA-41830	Not Effective	32.63	0.00	32.63	0.00
IDA-41840	Not Effective	30.87	0.00	30.87	0.00
IDA-H2310	Not Effective	18.52	0.00	18.52	0.00
IDA-Q4890	Effective	1.00	0.62	0.38	0.00
IDA-Q4891	Effective	0.70	0.00	0.70	0.00



Project Name (ID): WAPP APL 2 - OMVS Felou Hydroelectric Project (P094916)

Region: Africa

Board Approval Date : 06/29/2006

Closing Date : 06/30/2010

Loan/Credit/Grant Number : IDA-42150, IDA-42160, IDA-42170, IDA-Q4750

Sector(s): Renewable energy (93%), General public administration (7%)

Theme(s): Regional integration (P), Regulation and competition policy (P), Water resources management (S), Trade facilitation and market access (S)

Project Development Objectives:

The key objectives of the WAPP (West Africa Power Pool) is to establish a well-functioning, cooperative, power pooling mechanism among national power utilities of ECOWAS (Economic Community of West African States) member states, based on a transparent and harmonized legal, policy, regulatory and commercial framework.

Progress toward achieving development objective(s):

The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-42150	Not Effective	24.84	0.00	24.84	0.00
IDA-42160	Not Effective	24.84	0.00	24.84	0.00
IDA-42170	Not Effective	24.84	0.00	24.84	0.00
IDA-Q4750	Closed	0.65	0.39	0.26	0.00



Project Name (ID): WAPP APL 1 (2nd Phase - COASTAL TRANSMISSION BACKBONE) (P094917)

Region: Africa

Board Approval Date : 06/29/2006

Closing Date : 12/31/2010

Loan/Credit/Grant Number : IDA-42130, IDA-42140

Sector(s): Power (45%), District heating and energy efficiency services (45%), Renewable energy (5%), General public administration (5%)

Theme(s): Regional integration (P), Trade facilitation and market access (S)

Project Development Objectives:

The key objectives of the WAPP (West Africa Power Pool) are to establish a well-functioning, cooperative, power pooling mechanism among national power utilities of ECOWAS (Economic Community of West African States) member states, based on a transparent and harmonized legal, policy, regulatory and commercial framework.

Progress toward achieving development objective(s):

The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30 2006)

Loan/Credit/ Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-42130	Not Effective	45.28	0.00	45.28	0.00
IDA-42140	Not Effective	14.85	0.00	14.85	0.00

