

STATUS OF PROJECTS IN EXECUTION–FY08

AFRICA REGION

COUNTRY: UGANDA

**Operations Policy and Country Services
October 11, 2008**



Introduction

The Status of Projects in Execution (SOPE) Report for FY08 provides information on all IBRD/IDA projects that were active as of June 30, 2008. For the first time, the SOPE report will include recipient-executed projects (over US\$ 5 million). The World Bank has issued a SOPE Report every year as an internal communication to the Board of Executive Directors. In accordance with the Bank's revised disclosure policy, since FY02, the SOPE Report is available to the public.

The report is intended to bridge the gap in information available to the public between the Project Appraisal Document or Program Document, disclosed after the Bank approves a project, and the Implementation Completion Report, disclosed after the project closes.

In addition to the project progress description, the FY08 SOPE report¹ contains project level comparisons of disbursement estimates and actual disbursements, and a table showing the loan/credit/grant amount and disbursements to date.

¹ Notes:

- Amounts and graphs for loans/credits/grants in currencies other than U.S. dollars may not match exactly due to exchange rate fluctuations over the life of the project.
- Graphs of original estimates for some recipient-executed projects might not exist since they are not required in the project document.
- Disbursement graphs are not included for Development Policy Operations, which provide quick-disbursing financing to support policy and institutional reforms. For these operations, funds are disbursed in one or more stages (tranches), released when the borrower complies with agreed prior actions.
- Projects which are not yet effective may not have a planned disbursement schedule and thus will not include a graph.

Project Name (ID): UG-N Uganda Soc Action Fund (FY03) (P002952)

Country: Uganda

Board Approval Date: 07/23/2002

Midterm Review Date: 06/06/2005

Closing Date: 03/31/2009

Loan/Credit/Grant Number: IDA-3697A, TF-20972, IDA-Q3300, TF-50522, IDA-36970

Sector(s): Other social services (35%), Primary education (20%), Health (20%), Water supply (15%), General agriculture, fishing and forestry sector (10%)

Theme(s): Conflict prevention and post-conflict reconstruction (P), Participation and civic engagement (P), Other social protection and risk management (P), Social safety nets (P), Decentralization (P)

Project Development Objectives:


The objective is to empower communities in 18 districts by enhancing their capacity to systematically identify, prioritize, and plan for their needs and implement sustainable development initiatives.

Progress toward achieving development objective(s):

The project continues to demonstrate good results on the ground, and is likely to meet its development objectives. There was a slow start in the first year due partly to sporadic conflicts in the project area. Also, there were delays in establishing implementation structures at the community and local government levels. Nevertheless, implementation has progressed well since 2006. As a result, over 8,000 community sub-projects have been funded and, about 84% of them have been completed. These subprojects are benefiting 46.1% of the population in Northern Uganda against the target of 30%.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-3697A	Closed	5.83	5.42	0.00	0.00
TF-20972	Closed	5.02	4.31	0.00	0.00
IDA-Q3300	Closed	1.03	0.00	0.00	1.03
TF-50522	Closed	1.61	1.61	0.00	0.00
IDA-36970	Effective	123.68	112.95	1.96	0.00

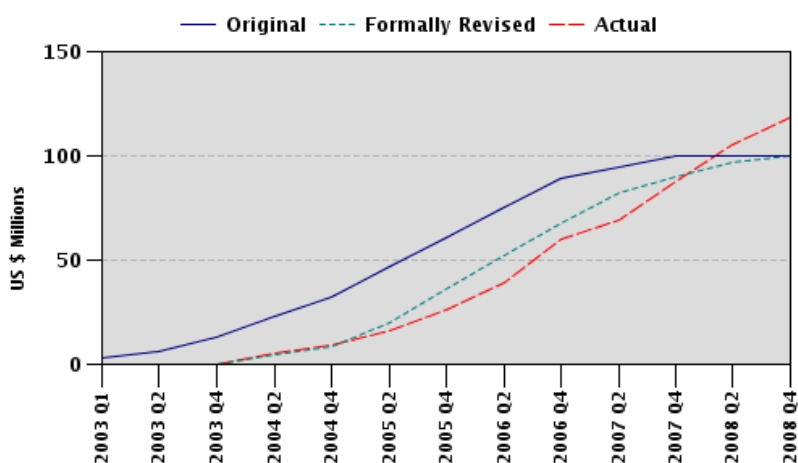

Project Name (ID): UG-Nat Agr Advisory Srvcs SIL (FY01) (P044695)

Country: Uganda

Board Approval Date: 02/15/2001

Midterm Review Date: 06/03/2005

Closing Date: 12/31/2009

Loan/Credit/Grant Number: COFN-4440, IDA-34630, IDA-3463A

Sector(s): Agricultural extension and research (70%), Central government administration (23%), Agricultural marketing and trade (7%)

Theme(s): Other rural development (P), Rural markets (P), Gender (S), Technology diffusion (S), Infrastructure services for private sector development (S)

Project Development Objectives:

The objective is to establish an effective and sustainable demand-driven agricultural advisory service which men and women farmers will be able to manage and use to identify opportunities to increase their own productivity and incomes in a sustainable manner.

The project was restructured, or received Additional Financing during FY 08


The changes brought by restructuring are: (a) The agricultural advisory services (AAS) grants for subproject category have been scaled up to 83 districts and 1,033 sub-counties, reaching over one million farm families by the end of the project period; (b) adopted a simplified community-based procurement system; (c) revised the project description and realigned the component structure; (d) refined and adjusted the Results Framework; and (f) extended the project closing date by eighteen months, from June 30, 2008, until December 31, 2009, to accommodate implementation of the Medium-Term Expenditure Framework (MTEF). These adjustments did not involve changes to project development objective and/or associated outcome targets.

Progress toward achieving development objective(s):

The project continues to progress towards achievement of its development objective. The National agricultural advisory services (NAADS) currently operates in 748 rural sub-counties and urban authorities, which cover all districts, regions and agro-ecological zones of Uganda. Mid-term evaluations and a recent analysis of surveys and studies by the International Food Policy Research Institute (IFPRI) and the independent performance evaluation of NAADS demonstrate that the project is increasing the availability and quality of agricultural services available to farmers, and that farmers covered by the project are adopting technologies that lead to real improvements in yields and farm incomes. IFPRI analysis shows the value of total agricultural production per capita in NAADS districts was higher by 175,000 Uganda Shillings (in 2000 Uganda shillings) than in non-NAADS districts. The adoption of improved crop varieties in NAADS districts was around 75%, about 15% higher than comparable households in non-NAADS districts.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
COFN-4440	Effective	21.65	7.15	14.00	0.00
IDA-34630	Effective	54.43	20.02	32.98	0.00
IDA-3463A	Closed	1.50	1.37	0.00	0.00

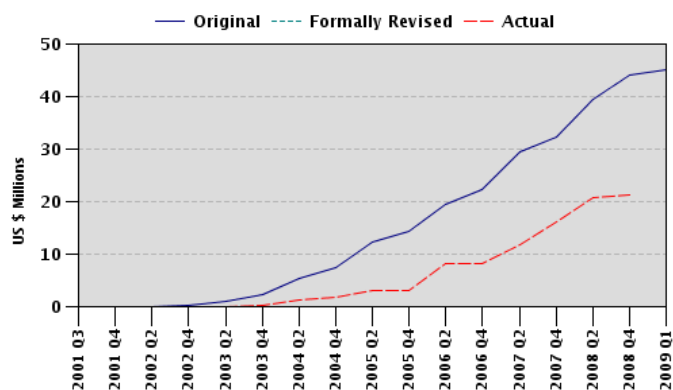

Project Name (ID): UG-Priv & Utility Sec Reform (FY01) (P050439)

Country: Uganda

Board Approval Date: 08/24/2000

Midterm Review Date: 01/31/2005

Closing Date: 02/15/2015

Loan/Credit/Grant Number: IDA-34110, IDA-3411A, IDA-B0070, IDA-Q2050

Sector(s): Central government administration (52%), Other social services (48%)

Theme(s): State enterprise/bank restructuring and privatization (P), Regulation and competition policy (P)

Project Development Objectives:


The objective is to improve the quality, coverage and economic efficiency of commercial and utility services, through privatization, private participation in infrastructure (PPI), and an improved regulatory framework.

Progress toward achieving development objective(s):

The distribution part of the power utility was put under concession March 2005 and to date, the contractual obligations have been met. It has to be noted however that the overall distribution sector environment is still challenging since the level of electricity losses remains relatively high (35%). The company and the Government of Uganda have recently taken steps to work together in limiting power thefts, which make up a substantial part of the losses. Power theft has become more of an issue since the increase of electricity tariffs at the end of 2006.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-34110	Effective	38.27	14.88	8.58	12.14
IDA-3411A	Effective	18.53	16.40	0.00	0.00
IDA-B0070	Effective	5.50	0.00	5.50	0.00
IDA-Q2050	Closed	0.93	0.00	0.00	0.93

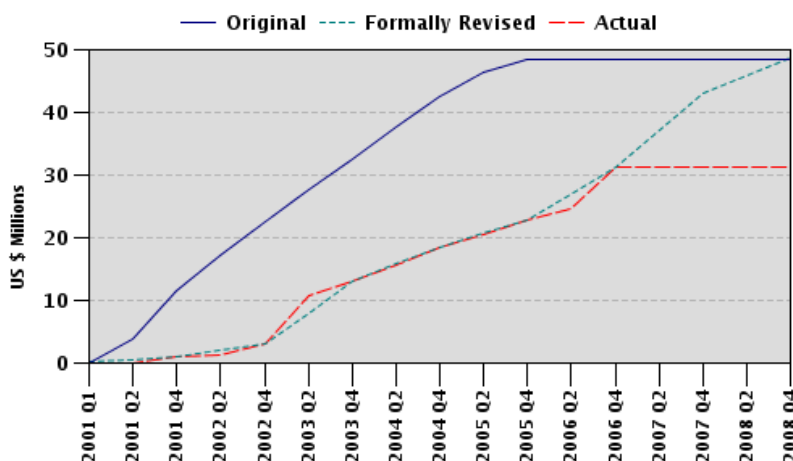

Project Name (ID): UG-Pub Serv Perform Enhance (FY06) (P050440)

Country: Uganda

Board Approval Date: 06/20/2006

Closing Date: 12/31/2011

Loan/Credit/Grant Number: IDA-41990, IDA-Q3970, TF-50519

Sector(s): General public administration sector (100%)

Theme(s): Administrative and civil service reform (P), Other accountability/anti-corruption (P), Other public sector governance (S), Public expenditure, financial management and procurement (S)

Project Development Objectives:

The objectives of the restructured project are: (a) the transformation of the public service so that it is affordable, efficient and accountable in its use of public resources and service delivery; and (b) the improvement of the policy, institutional and regulatory environment in targeted areas for sustainable growth and service delivery.

The project was restructured, or received Additional Financing during FY 08

The project was restructured in May 2008, in order to

a) Reduce component 2 (Performance Enhancement Facility) to three main activities, namely (i) the establishment of a Civil Service College (CSC) to provide a sustainable source of skilled workforce for the public service; (ii) provision of targeted training and research in strategic areas of the growth agenda; and (iii) equipping top public service managers with the skills leading to a more strategic approach to managing the service.

b) Reduce the Credit amount from SDR 48.7 million (USD 70 million) to SDR 13,973,353.42 million (USD 23 million).


c) Extend the closing date from June 30, 2011 to June 30, 2013.

Progress toward achieving development objective(s):

The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-41990	Effective	76.81	0.00	76.81	0.00
IDA-Q3970	Closed	0.49	0.49	0.00	0.00
TF-50519	Closed	0.38	0.32	0.00	0.06

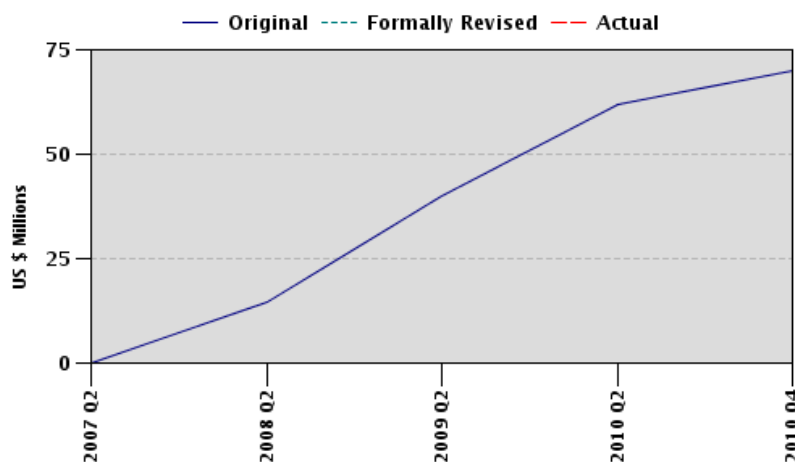

Project Name (ID): UG-Agr Rsrch & Training SIL 2 (FY99) (P059127)

Country: Uganda

Board Approval Date: 05/06/1999

Midterm Review Date: 04/17/2003

Closing Date: 06/30/2009

Loan/Credit/Grant Number: IDA-32040, IDA-32041, IDA-3204A, IDA-Q1370

Sector(s): Central government administration (60%), Agricultural extension and research (40%)

Theme(s): Technology diffusion (P), Other rural development (P), Other environment and natural resources management (P), Participation and civic engagement (S)

Project Development Objectives:

The project aims to generate and transfer relevant new knowledge, technologies, and strategies to support the Plan for Modernization of Agriculture.

The project was restructured, or received Additional Financing during FY 08


The PDO of the project has remained the same. Additional Financing of \$12 million was approved in August 2007 to finance agricultural research activities till June 2009 (a period of two years from original closing date of June 2007).

Progress toward achieving development objective(s):

Project effectiveness of the additional financing was delayed (till May 2008) because of delays in Parliamentary approval of the Additional Financing Credit. This has severely affected implementation of remaining project activities. From May 2008 implementation started following a revised work plan. Progress towards achievement of project development objective has been good: (a) proportion of National Agricultural Research Organization's (NARO) research outputs (technologies, knowledge and strategies) disseminated by technology pathways in specific locations has been achieved at 56.1% against a target of 60% at project end in June 2009; (b) proportion of farmers with significant uptake and adoption of specific research outputs in specific locations achieved at 45% on crops, 30% on livestock, 25% on natural resource management (NRM) against a target of 50% for crops; 35% for livestock; and 35% for NRM, respectively; (c) number of Zones with operational Competitive Grants Schemes has reached at 3 zones against a target of 7 at project end in June 2009; (d) number of completed research outputs at start of project (baseline) was 168, which has reached 545 against a target of 600 at project end in June 2009.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-32040	Effective	17.21	15.01	0.02	0.00
IDA-32041	Effective	13.01	0.00	13.01	0.00
IDA-3204A	Closed	13.46	11.86	0.00	0.00
IDA-Q1370	Closed	0.60	0.00	0.00	0.60

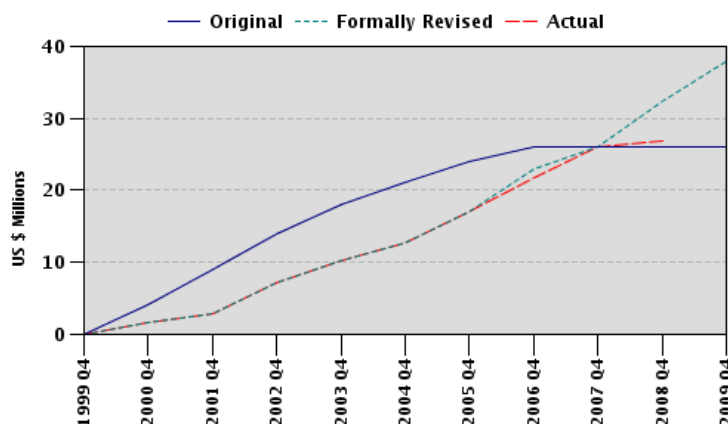

Project Name (ID): UG-PAMSU SIL (FY03) (P065437)

Country: Uganda

Board Approval Date: 07/09/2002

Midterm Review Date: 10/19/2005

Closing Date: 06/30/2009

Loan/Credit/Grant Number: IDA-36900, IDA-3690A

Sector(s): General agriculture, fishing and forestry sector (50%), Central government administration (45%), Other social services (5%)

Theme(s): Biodiversity (P), Environmental policies and institutions (P), Rural non-farm income generation (S), Land administration and management (S)

Project Development Objectives:


The objective is to facilitate the sustainable and cost-effective management of wildlife and cultural resources.

Progress toward achieving development objective(s):

The project is well on its way to achieving its development objective. Major achievements have been made within the Uganda Wildlife Authority (UWA) related to financial sustainability, securing the natural resource base of the protected areas estate, and encouraging community conservation. UWA has exceeded its target for revenue generation and has created a rainy day fund of over US\$1 million. All of the boundaries of the Protected Areas (PA) have been marked and issues of encroachment have also been resolved. Incidents of poaching have been reduced and the animal counts have shown an increase in most species, most exceptionally the endangered mountain gorilla.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-36900	Effective	27.87	17.76	8.57	0.00
IDA-3690A	Closed	7.00	6.32	0.00	0.00

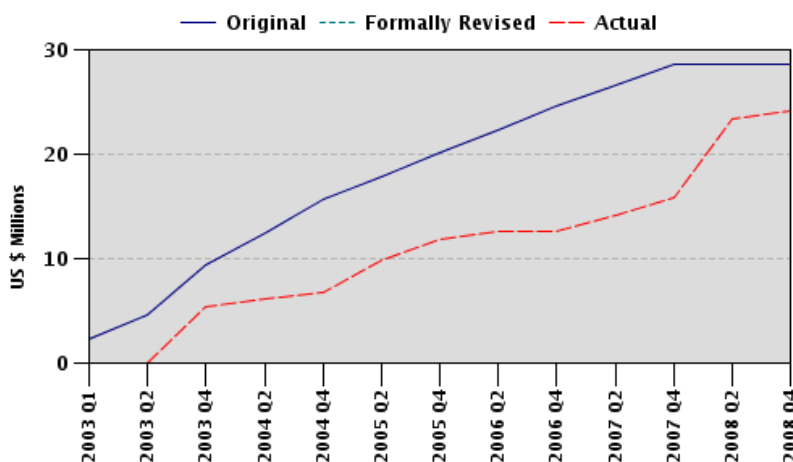

Project Name (ID): UG - Power Sector Dev. Project (FY07) (P069208)

Country: Uganda

Board Approval Date: 04/26/2007

Closing Date: 07/31/2011

Loan/Credit/Grant Number: IDA-42970

Sector(s): Power (96%), District heating and energy efficiency services (2%), Central government administration (2%)

Theme(s): Infrastructure services for private sector development (P), Regulation and competition policy (S), Regional integration (S), Rural services and infrastructure (S)

Project Development Objectives:


The objectives are to reduce short-term power shortages and financial imbalances, and facilitate orderly longer-term expansion of electricity services.

Progress toward achieving development objective(s):

Additional 50MW-thermal power station to be commissioned by August 2008. Preparation of a Power Sector Investment Plan ongoing. Energy efficiency initiatives commencing shortly.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-42970	Effective	324.96	89.56	229.49	0.00

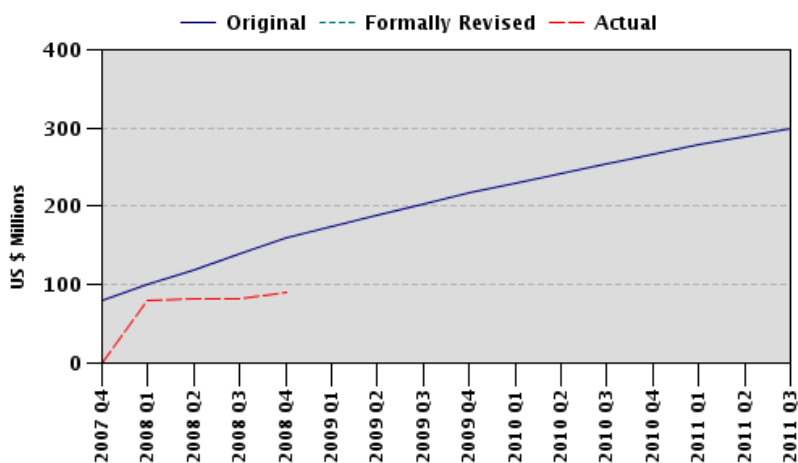

Project Name (ID): UG-Energy for Rural Transform (FY02) (P069996)

Country: Uganda

Board Approval Date: 12/13/2001

Midterm Review Date: 10/28/2004

Closing Date: 02/28/2009

Loan/Credit/Grant Number: IDA-35880, IDA-3588A

Sector(s): Power (55%), General energy sector (18%), Telecommunications (11%), Other social services (8%), General agriculture, fishing and forestry sector (8%)

Theme(s): Rural services and infrastructure (P), Other financial and private sector development (P), Education for the knowledge economy (P), Health system performance (P)

Project Development Objectives:


The project aims to put in place a conducive environment and related capacity for commercially oriented, sustainable service delivery of rural/renewable energy and Information & Communication Technologies.

Progress toward achieving development objective(s):

The requisite capacity and institutional framework have been developed. Most of the implementing agencies have now fully absorbed and internalized their role and activities under the Energy for Rural Transform (ERT) program, and are ready to move to Phase II of increased investments. Trigger-indicators for Phase II are on-track to meet their target values, apart from two lagging agencies, namely the Education and Agriculture components. Phase II is under preparation.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-35880	Effective	58.86	41.37	15.64	0.00
IDA-3588A	Effective	1.64	1.51	0.00	0.00

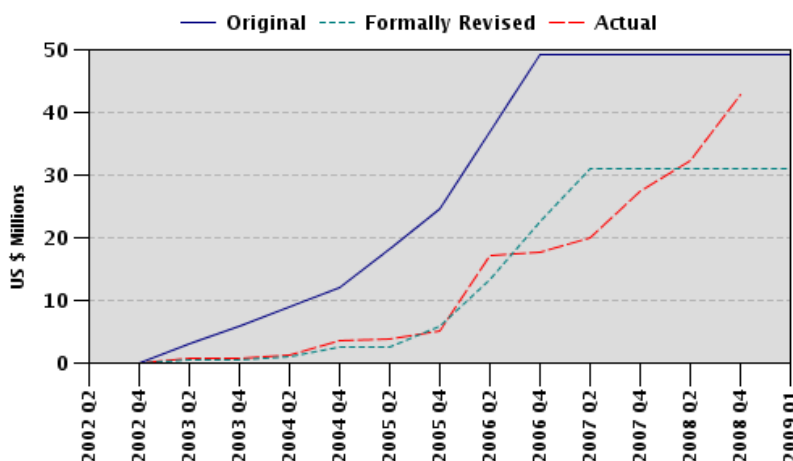

Project Name (ID): UG-EMCBP SIL 2 (FY01) (P073089)

Country: Uganda

Board Approval Date: 03/20/2001

Midterm Review Date: 05/18/2005

Closing Date: 11/30/2008

Loan/Credit/Grant Number: IDA-34770, IDA-3477A

Sector(s): Central government administration (66%), Sub-national government administration (17%), Other social services (17%)

Theme(s): Environmental policies and institutions (P), Decentralization (P), Participation and civic engagement (P)

Project Development Objectives:


The project aims to enhance environmental management in district and communities, promote capacity building in lead agencies as well as promote capacity within the National Environmental Management Authority (NEMA).

Progress toward achieving development objective(s):

The project has performed well and implementation progress is good. The legislative and regulatory framework for environmental management is well established. Compliance is being monitored and enforced by NEMA, the district authorities and the newly gazetted auditors and inspectors. District Environment Officers have been recruited and trained in most districts. Capacity for environmental management at the local level has been strengthened and local authorities empowered.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-34770	Effective	17.11	13.57	2.01	0.00
IDA-3477A	Closed	10.36	9.26	0.00	0.00

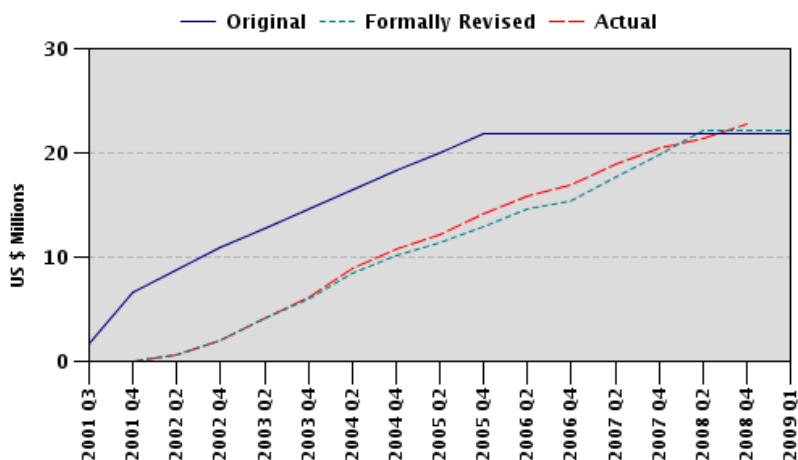

Project Name (ID): UG-Road Dev APL 3 (FY05) (P074079)

Country: Uganda

Board Approval Date: 09/02/2004

Midterm Review Date: 05/05/2008

Closing Date: 12/31/2009

Loan/Credit/Grant Number: IDA-H1220, IDA-39760

Sector(s): Roads and highways (100%)

Theme(s): Rural services and infrastructure (P), Administrative and civil service reform (S), Infrastructure services for private sector development (S), Other urban development (S)

Project Development Objectives:


The objective of the project is to support the Borrower in implementing the third phase of the program, including improving access to rural and economically productive areas, building a sustainable road sector planning, design and program management, and road safety management.

Progress toward achieving development objective(s):

After initial procurement related delays of about 2 years, all works contracts under this project have been awarded and are progressing well. Hence, there was no meaningful progress by the end of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-H1220	Effective	41.61	0.50	41.11	0.00
IDA-39760	Effective	74.70	22.79	51.65	0.00

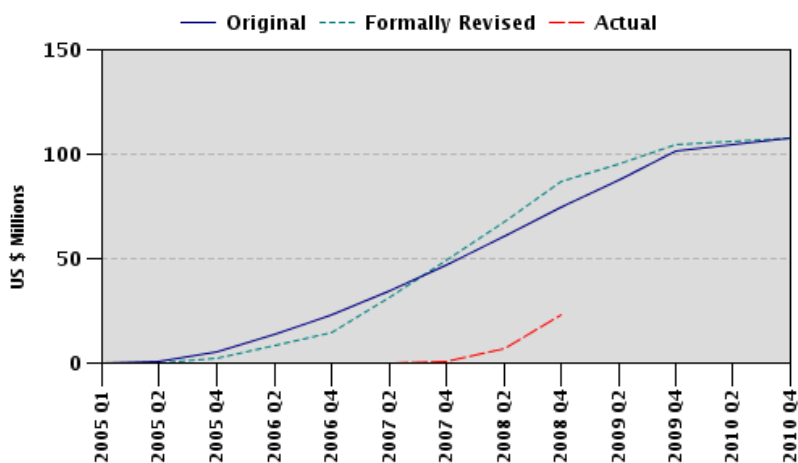

Project Name (ID): UG-Kampala Inst & Infrac Dev Prj (FY08) (P078382)

Country: Uganda

Board Approval Date: 11/06/2007

Closing Date: 12/31/2010

Loan/Credit/Grant Number: IDA-43670, IDA-Q4570, IDA-Q4571

Sector(s): Sub-national government administration (31%), Roads and highways (23%), Flood protection (23%), Solid waste management (23%)

Theme(s): Other urban development (P), Municipal governance and institution building (S), Municipal finance (S)

Project Development Objectives:

The objective is to improve institutional efficiency of Kampala City Council through implementation of the Strategic Framework for Reform.

Progress toward achieving development objective(s):

The Project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-43670	Not Effective	34.99	0.00	34.99	0.00
IDA-Q4570	Effective	0.60	0.60	0.00	0.00
IDA-Q4571	Effective	0.39	0.39	0.00	0.00



Project Name (ID): UG-Natl Re Dev TAL (FY04) (P079925)

Country: Uganda

Board Approval Date: 12/09/2003

Midterm Review Date: 01/09/2008

Closing Date: 06/30/2009

Loan/Credit/Grant Number: IDA-38350

Sector(s): Mining and other extractive (40%), Central government administration (35%), Other social services (15%), Sub-national government administration (10%)

Theme(s): Decentralization (P), Regulation and competition policy (P), Administrative and civil service reform (P), Participation and civic engagement (P), Environmental policies and institutions (S)

Project Development Objectives:


The overall objective is to assist the Government of Uganda (GOU) in implementing its strategy to (i) accelerate sustainable development and reduce poverty by strengthening governance, transparency and capacity in the management of mineral resources, with particular emphasis on community development in mining areas and improvement of small-scale and artisanal mining; and (ii) promote a socially and environmentally sound development of the minerals sector based on private investments.

Progress toward achieving development objective(s):

The project continues to make progress toward achieving its objectives. The project is achieving results in attracting investors, increasing revenue and improving small scale mining. Implementation was delayed by about two years, affecting mainly the mining cadastre and geological mapping activities, but is now progressing well.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-38350	Effective	27.97	8.58	19.05	0.00

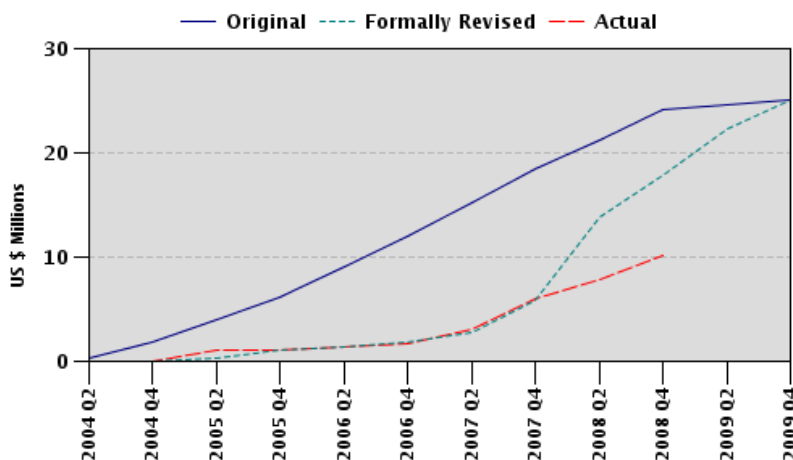

Project Name (ID): UG-Priv Sec Competitiveness 2 (P083809)

Country: Uganda

Board Approval Date: 09/02/2004

Closing Date: 07/31/2010

Loan/Credit/Grant Number: TF-52807, IDA-39750

Sector(s): Central government administration (35%), Other industry (30%), Micro- and SME finance (15%), Agro-industry (10%), Other domestic and international trade (10%)

Theme(s): Small and medium enterprise support (P), Export development and competitiveness (P), Rural markets (P), Infrastructure services for private sector development (S), Legal institutions for a market economy (S)

Project Development Objectives:


The objective of the project is to create sustainable conditions for enterprise creation and growth that responds to local and export markets.

Progress toward achieving development objective(s):

Achievement of the development objectives is progressing well, despite the one year delay in effectiveness and slow disbursements. There have been a number of secondary benefits derived from the policy/advocacy role of the Private Sector Foundation of Uganda (PSFU); the public-private consultations on land reform which is necessary for community buy-in and a number of innovative products which have been introduced, but require time to build understanding. The forthcoming mid-tem review of the project will be a good time to take stock of the project's focus and to consider the merits of reallocation of resources away from some of the slower-moving components.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
TF-52807	Closed	0.75	0.62	0.00	0.13
IDA-39750	Effective	77.66	12.64	64.28	0.00

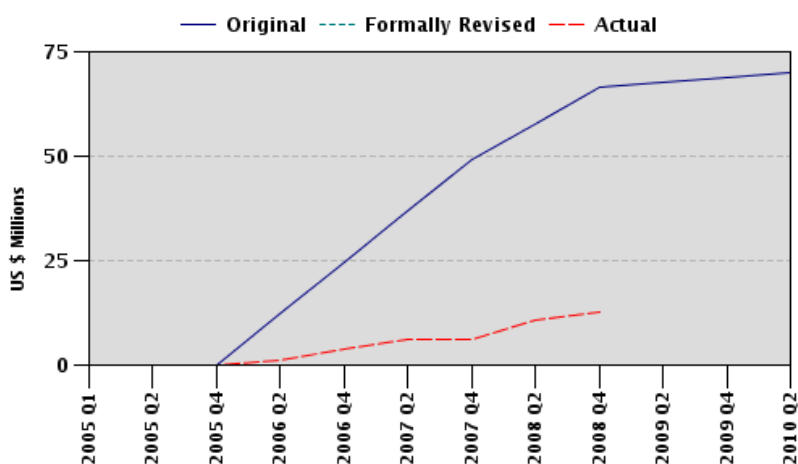

Project Name (ID): UG-Millennium Science Init (FY06) (P086513)

Country: Uganda

Board Approval Date: 05/25/2006

Closing Date: 12/31/2011

Loan/Credit/Grant Number: IDA-Q4870, IDA-41740

Sector(s): Tertiary education (65%), Central government administration (29%), Other industry (6%)

Theme(s): Education for the knowledge economy (P), Other financial and private sector development (P), Improving labor markets (S)

Project Development Objectives:


The objective is for Ugandan universities and research institutes to produce more and better qualified science and engineering graduates, and higher quality and more relevant research for firms.

Progress toward achieving development objective(s):

The project is implementing on schedule and continues to make good progress toward its development objectives. Twelve major research and training subprojects (grants) were selected in September 2007. The process was universally acknowledged as transparent and fair. All eleven grantee research groups have signed contracts and are beginning to undertake their projects. The second calls-for-proposals was issued ahead of schedule and the shortlist of finalists has been selected. The Uganda Industrial Research Institute is acquiring the needed upgrades to its physical plant. Progress in monitoring and evaluation is on track, as are the fiduciary aspects of implementation.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-Q4870	Closed	0.50	0.00	0.00	0.50
IDA-41740	Effective	32.27	3.13	29.07	0.00

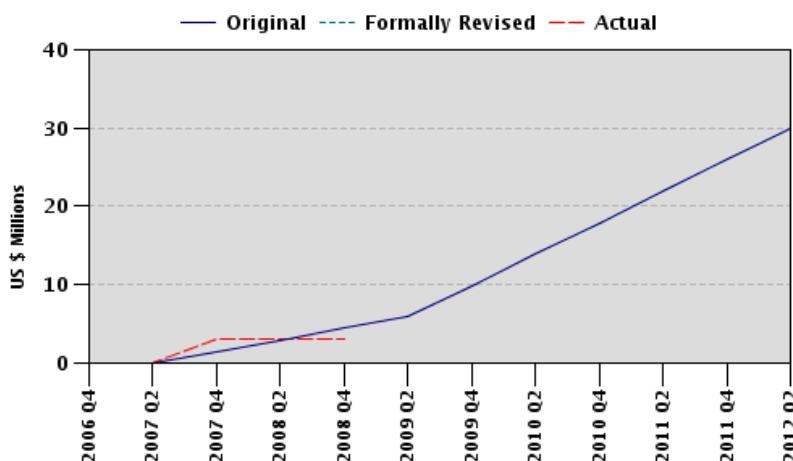

Project Name (ID): UG-Local Govt Mgt Svc Del Pjt (FY08) (P090867)

Country: Uganda

Board Approval Date: 12/18/2007

Closing Date: 12/31/2011

Loan/Credit/Grant Number: IDA-43720

Sector(s): Sub-national government administration (72%), Central government administration (20%), Other social services (8%)

Theme(s): Decentralization (P), Public expenditure, financial management and procurement (P), Municipal governance and institution building (S), Municipal finance (S), Gender (S)

Project Development Objectives:

The objective is to strengthen the ability of the Ministries, Departments and Agencies (MDAs) and local governments (LGs) to plan and manage their resources in collaboration with local communities for effective service delivery.

Progress toward achieving development objective(s):

The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-43720	Not Effective	55.82	0.00	55.82	0.00



Project Name (ID): UG-PRSC 7 (FY08) (P101231)

Country: Uganda

Board Approval Date: 05/06/2008

Closing Date: 11/30/2009

Loan/Credit/Grant Number: IDA-44310

Sector(s): Central government administration (64%), General industry and trade sector (9%), General agriculture, fishing and forestry sector (9%), General education sector (9%), Health (9%)

Theme(s): Public expenditure, financial management and procurement (P), Administrative and civil service reform (P), Regulation and competition policy (S), Rural policies and institutions (S), Education for all (S)

Project Development Objectives:

The objectives of the project are to: (i) enhance productivity and competitiveness, (ii) accelerate the effective delivery of social services, (iii) improve public sector management, and (iv) reach the poverty reduction, human development and growth targets.

Progress toward achieving development objective(s):

The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-44310	Not Effective	201.38	0.00	201.38	0.00

Project Name (ID): UG:Program for Control of Avian Influenza (P110207)

Country: Uganda

Board Approval Date: 06/19/2008

Closing Date: 06/30/2012

Loan/Credit/Grant Number: IDA-44820

Sector(s): Agricultural extension and research (39%), Central government administration (36%), Animal production (13%), Health (11%), Agro-industry (1%)

Theme(s): Rural services and infrastructure (P), Other communicable diseases (P), Natural disaster management (P)

Project Development Objectives:

The development objective is to substantially reduce the threat posed to the poultry industry and humans in Uganda by HPAI infection and other zoonoses and to prepare for, control, and respond effectively to future AHN pandemics and other infectious disease emergencies in livestock and humans.

Progress toward achieving development objective(s):

The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-44820	Not Effective	10.03	0.00	10.03	0.00

