

STATUS OF PROJECTS IN EXECUTION – FY08

EAST ASIA AND PACIFIC REGION

COUNTRY: CAMBODIA

**Operations Policy and Country Services
October 11, 2008**



Introduction

The Status of Projects in Execution (SOPE) Report for FY08 provides information on all IBRD/IDA projects that were active as of June 30, 2008. For the first time, the SOPE report will include recipient-executed projects (over US\$ 5 million). The World Bank has issued a SOPE Report every year as an internal communication to the Board of Executive Directors. In accordance with the Bank's revised disclosure policy, since FY02, the SOPE Report is available to the public.

The report is intended to bridge the gap in information available to the public between the Project Appraisal Document or Program Document, disclosed after the Bank approves a project, and the Implementation Completion Report, disclosed after the project closes.

In addition to the project progress description, the FY08 SOPE report¹ contains project level comparisons of disbursement estimates and actual disbursements, and a table showing the loan/credit/grant amount and disbursements to date.

¹ Notes:

- Amounts and graphs for loans/credits/grants in currencies other than U.S. dollars may not match exactly due to exchange rate fluctuations over the life of the project.
- Graphs of original estimates for some recipient-executed projects might not exist since they are not required in the project document.
- Disbursement graphs are not included for Development Policy Operations, which provide quick-disbursing financing to support policy and institutional reforms. For these operations, funds are disbursed in one or more stages (tranches), released when the borrower complies with agreed prior actions.
- Projects which are not yet effective may not have a planned disbursement schedule and thus will not include a graph.

Project Name (ID): KH-Rural Electrification & Transmission (P064844)

Country: Cambodia

Board Approval Date: 12/16/2003

Closing Date: 06/30/2009

Loan/Credit/Grant Number: TF-26154, IDA-Q2990, IDA-38400

Sector(s): Power (78%), Central government administration (14%), Renewable energy (8%)

Theme(s): Infrastructure services for private sector development (P), Rural services and infrastructure (P), Rural policies and institutions (P), Regulation and competition policy (S), Climate change (S)

Project Development Objectives:

The main development objectives of the project are to: (a) improve power sector efficiency and reliability and reduce electricity supply costs; (b) improve standards of living and foster economic growth in rural areas by expanding rural electricity supplies; and (c) strengthen electricity institutions, the regulatory framework and the enabling environment for sector commercialization and privatization. The project's global environmental objective is to overcome barriers to renewable energy development in Cambodia, including those related to lack of policy framework, financing, information and institutional capacity.

Progress toward achieving development objective(s):

The Project's development objectives are likely to be achieved if the closing date is extended for two years. Most of the contracts for physical investment managed by Electricity du Cambodge (EDC) are under implementation. The expected target date for project completion is March 30th, 2011. For the off-grid electrification supported by the Rural Electrification Fund (REF), little progress was achieved in solar home system (SHS) and mini/micro-hydro electrification.


On GEF objectives:

The GEO rating is rated satisfactory with project development objectives likely to be achieved. Most of the technical assistance and institutional capacity building activities for EDC, Ministry of Industry and Energy and Electricity Authority of Cambodia for overcoming barriers to renewable energy development in Cambodia were completed. The review and licensing mechanism for rural electrification enterprises (REEs) projects has been in place and operating smoothly; the tariff review mechanism for REE projects is in place; REF is operational and providing financial support to licensed REE projects; generation of HV system expansion planning have been completed; and a number of REE projects covering LV distribution expansion, micro-hydro, SHS, and biomass are under either implementation or processing. However, major delays in the REF supported installation of renewable generation capacity (micro-hydro 6,850 MW) and delivery of SHS (12,000 households) had been experienced and the targets were unlikely to be achieved by the existing closing date.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
TF-26154	Closed	0.19	0.19	0.00	0.00
IDA-Q2990	Closed	0.29	0.00	0.00	0.29
IDA-38400	Effective	44.33	4.76	39.31	0.00



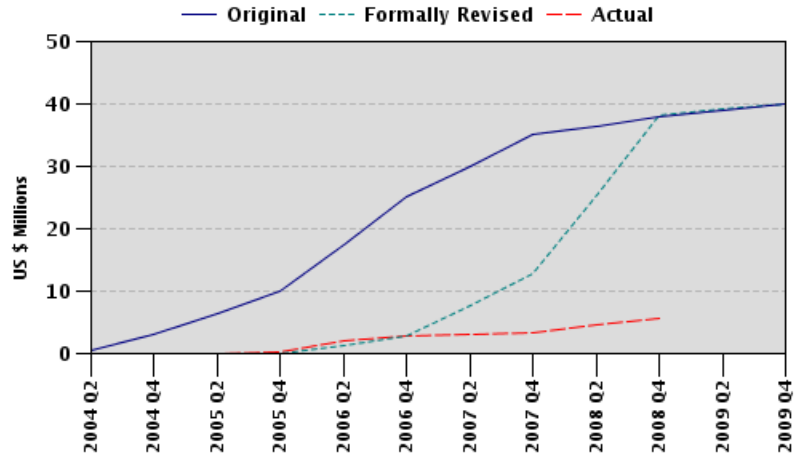

Project Name (ID): KH-Health Sector Support Project (P070542)

Country: Cambodia

Board Approval Date: 12/19/2002

Midterm Review Date: 10/03/2006

Closing Date: 12/31/2008

Loan/Credit/Grant Number: IDA-37280, IDA-H0150, IDA-H0160, TF-26771, TF-51053

Sector(s): Health (80%), Non-compulsory health finance (10%), Central government administration (5%), Sub-national government administration (5%)

Theme(s): Other communicable diseases (P), Health system performance (P), Nutrition and food security (P), Child health (P), Rural services and infrastructure (S)

Project Development Objectives:


The objective of this project is to contribute to the improvement of the health status of the population by: (a) increasing the accessibility and the quality of health services; and (b) assisting the Kingdom of Cambodia to implement its Health Sector Strategic Plan and strengthen the sector's capacity to manage resources efficiently.

Progress toward achieving development objective(s):

The Project continues to move in a satisfactory manner towards achievement of the development objectives. This is evidenced by findings from the 2005 Demographic and Health Survey on a number of indicators, as well as improvements in tuberculosis detection and cure rates, percentage of deliveries attended by trained staff, and in the decrease of incidence of malaria in high risk areas.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-37280	Effective	21.35	9.77	10.63	0.00
IDA-H0150	Effective	9.72	7.37	1.73	0.00
IDA-H0160	Effective	2.59	2.06	0.41	0.00
TF-26771	Closed	0.15	0.06	0.00	0.09
TF-51053	Effective	2.52	0.97	1.47	0.00

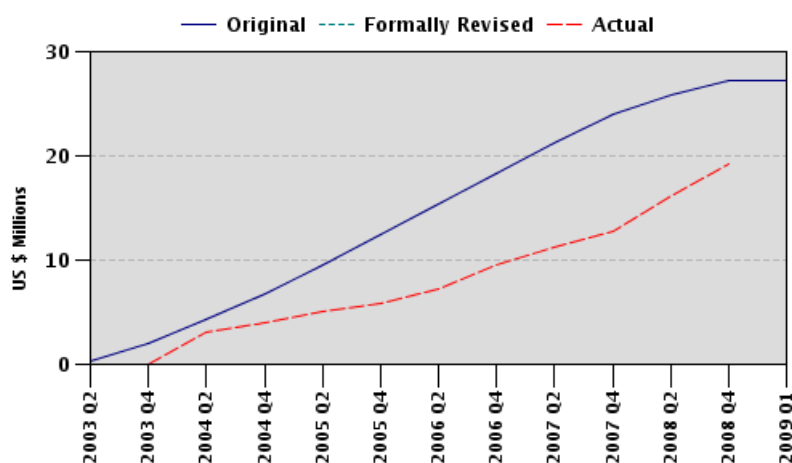

Project Name (ID): KH-Cambodia Education Sector Support (P070668)

Country: Cambodia

Board Approval Date: 05/12/2005

Closing Date: 12/31/2010

Loan/Credit/Grant Number: TF-51642, IDA-H1610, IDA-40550, TF-52059, TF-54868

Sector(s): Secondary education (45%), Other social services (25%), Primary education (14%), General public administration sector (9%), Tertiary education (7%)

Theme(s): Education for all (P), Gender (S), Indigenous peoples (S), Social safety nets (S), Decentralization (S)

Project Development Objectives:

The project development objectives will support the National Poverty Reduction Strategy goals to expand access to educational services by addressing supply, demand, quality and efficiency constraints, especially focusing on the poorest and groups at risk.

Progress toward achieving development objective(s):


Outcomes have been positive on all project development objectives. To expand access, 232 Lower Secondary schools were contracted and the construction of 158 schools was completed in poor and underserved areas. Scholarship numbers are currently on target. The first tranche of scholarships was delivered to 33,000 recipients in October 2007.

Transition rates in target schools are higher than expected and the majority of those who stay until Grade 6 continue to grade 7.

Activities relating to leadership development, decentralized school improvement and national assessment are well on target. The higher education components are moving forward toward meeting the project development objective, with slight delay in the expansion of the new library.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
TF-51642	Closed	0.39	0.37	0.00	0.02
IDA-H1610	Effective	20.57	8.29	12.03	0.00
IDA-40550	Effective	8.58	5.75	2.48	0.00
TF-52059	Closed	1.83	1.83	0.00	0.00
TF-54868	Effective	1.80	1.35	0.45	0.00

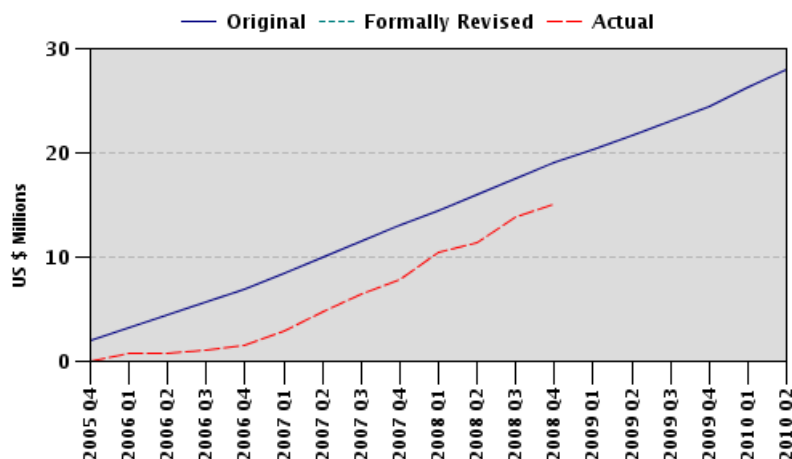

Project Name (ID): KH-Land Management and Administration (P070875)

Country: Cambodia

Board Approval Date: 02/26/2002

Midterm Review Date: 10/11/2004

Closing Date: 12/31/2009

Loan/Credit/Grant Number: TF-53043, TF-26421, IDA-36050

Sector(s): Central government administration (90%), Law and justice (5%), Tertiary education (3%), Other industry (2%)

Theme(s): Land administration and management (P), Personal and property rights (P), Rural markets (P), Access to law and justice (S), Judicial and other dispute resolution mechanisms (S)

Project Development Objectives:


The objectives are to improve land tenure security and promote the development of efficient land markets.

Progress toward achieving development objective(s):

In the period under review, the project achieved the PAD target of surveying one million titles. Significant savings in production costs per title have allowed a "no-cost" extension of the project for an additional 24 months. Concerns regarding overpayments to land registration teams in urban areas and delays in title delivery in some areas led to the inclusion of covenants related to improved reporting arrangements in the DCA to ensure titles are delivered in a timely and efficient manner.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
TF-53043	Effective	2.35	0.74	1.57	0.05
TF-26421	Closed	0.35	0.35	0.00	0.00
IDA-36050	Effective	30.52	15.97	12.91	0.44

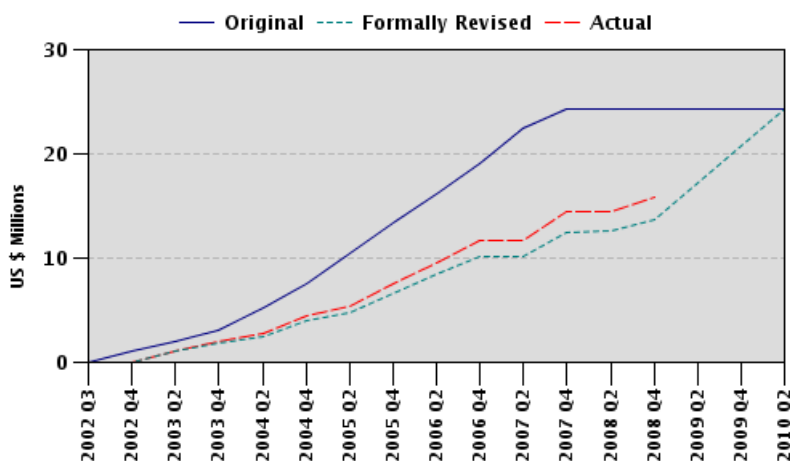

Project Name (ID): KH- RURAL INVESTMENT & LOCAL GOVERNANCE (P071146)

Country: Cambodia

Board Approval Date: 04/22/2003

Midterm Review Date: 02/06/2006

Closing Date: 12/31/2010

Loan/Credit/Grant Number: TF-26423, IDA-H3260, IDA-37470

Sector(s): Sub-national government administration (30%), Central government administration (20%), General agriculture, fishing and forestry sector (20%), General water, sanitation and flood protection sector (15%), Roads and highways (15%)

Theme(s): Other public sector governance (P), Other rural development (P), Gender (S), Other environment and natural resources management (S)

Project Development Objectives:

The objectives are: (a) to contribute to rural development and poverty reduction through supporting the provision of priority public goods and services at the commune level; and (b) to promote good local governance through support of decentralized and deconcentrated participatory local governance systems at the commune and provincial levels.

The project was restructured, or received Additional Financing during FY 08


An Additional Financing IDA Credit of US\$36.25 million was approved by the Board in July 2007 to allow the expansion of the project from 14 to 23 provinces; the completion date was extended to December 31, 2010.

Progress toward achieving development objective(s):

The project continues to make good progress and the achievement of its intended development objectives is already evident. The Commune/Sangkat Fund, being supported by the project as the inter-governmental fiscal transfer mechanism, has proven to be one of the most efficient and transparent components of the national budget. The transfer of its executive body from Seila Task Forces of the Council for Development of Cambodia to the Project Support Team of the National Committee for Management of the Decentralized and Deconcentrated Reform and handing over the procurement role to an Independent Procurement Agent have slightly slowed down the progress of project implementation in the last FY.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
TF-26423	Closed	0.47	0.46	0.00	0.01
IDA-H3260	Effective	37.81	3.53	34.38	0.00
IDA-37470	Effective	26.35	23.49	0.51	0.10

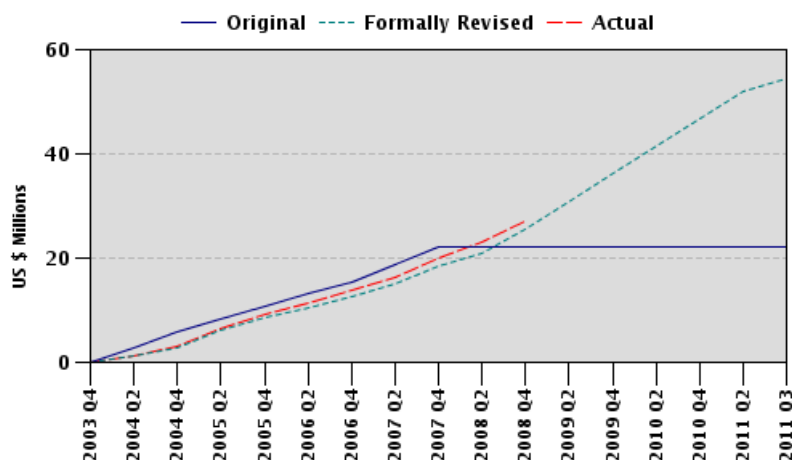

Project Name (ID): KH-PROVL & RURAL INFRA (P071207)

Country: Cambodia

Board Approval Date: 09/11/2003

Midterm Review Date: 07/03/2006

Closing Date: 09/30/2009

Loan/Credit/Grant Number: TF-56974, TF-26422, IDA-Q2791, IDA-Q2790, IDA-38220

Sector(s): Roads and highways (83%), Central government administration (9%), Sub-national government administration (8%)

Theme(s): Conflict prevention and post-conflict reconstruction (P), Rural services and infrastructure (P), Other accountability/anti-corruption (P), HIV/AIDS (S), Injuries and non-communicable diseases (S)

Project Development Objectives:


To assist the Kingdom of Cambodia to enhance the livelihood of the peoples residing in the provinces of Kampong Thom, Oddar Meanchey, Preah Vihear and Siem Reap with sustainable access to markets and essential services through (i) a program of road rehabilitation and maintenance; (ii) a program of capacity building and training; and (iii) development of improved public policies and strategies.

Progress toward achieving development objective(s):

The Credit suspension was lifted in February 2007 after the Government completed the necessary measures. Normalization of activities and implementation of the project have progressed slowly. With the incorporation of the International Procurement Agent, the remaining activities are under way and the contractors and consultants should be on board by the fourth quarter of 2008. The project is expected to achieve its development objectives.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
TF-56974	Effective	0.45	0.00	0.45	0.00
TF-26422	Closed	0.73	0.69	0.00	0.04
IDA-Q2791	Closed	0.11	0.00	0.00	0.11
IDA-Q2790	Closed	0.21	0.00	0.00	0.21
IDA-38220	Effective	22.42	12.04	7.20	2.21

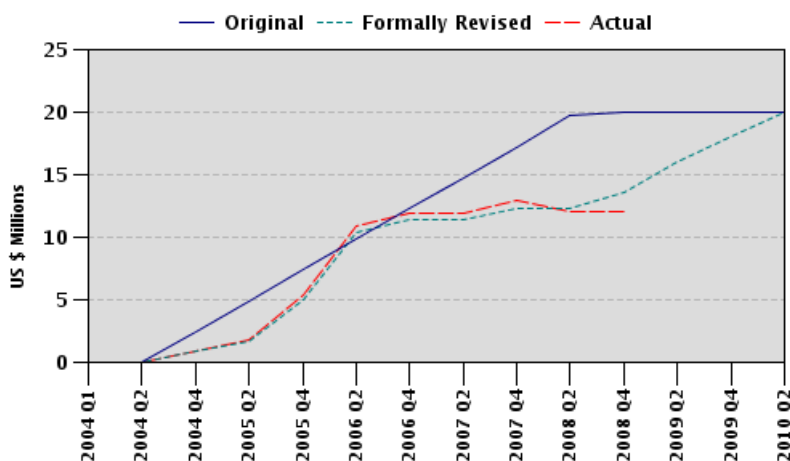

Project Name (ID): KH-PROV & PERI-URB WATER (P073311)

Country: Cambodia

Board Approval Date: 04/22/2003

Closing Date: 06/30/2010

Loan/Credit/Grant Number: TF-50943, TF-26848, IDA-H0340, IDA-37460

Sector(s): Water supply (80%), Central government administration (15%), Sanitation (5%)

Theme(s): Access to urban services and housing (P), Pollution management and environmental health (P), Participation and civic engagement (S), Other human development (S)

Project Development Objectives:


The project's development objectives are to assist the Kingdom of Cambodia move forward in fulfilling the Millennium Development Goals in water supply and sanitation by 2015.

Progress toward achieving development objective(s):

The project is making progress toward achieving its development objective. Coverage and reliability of water supply and sanitation services has been improved in both provincial and peri-urban areas. Output-based aid and design-build-lease contracts were completed in 11 provincial communities. Planned investments in 9 other communities were cancelled, but the project has been extended with the expectation that the unused funds will be used to finance water service networks and in-home sanitation facilities in peri-urban areas, where more than 16,000 low-income households have already been connected to the water supply network as a result of the project.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
TF-50943	Closed	0.77	0.72	0.00	0.06
TF-26848	Closed	0.54	0.54	0.00	0.00
IDA-H0340	Effective	3.76	0.46	2.09	1.06
IDA-37460	Effective	20.08	10.53	8.11	0.60

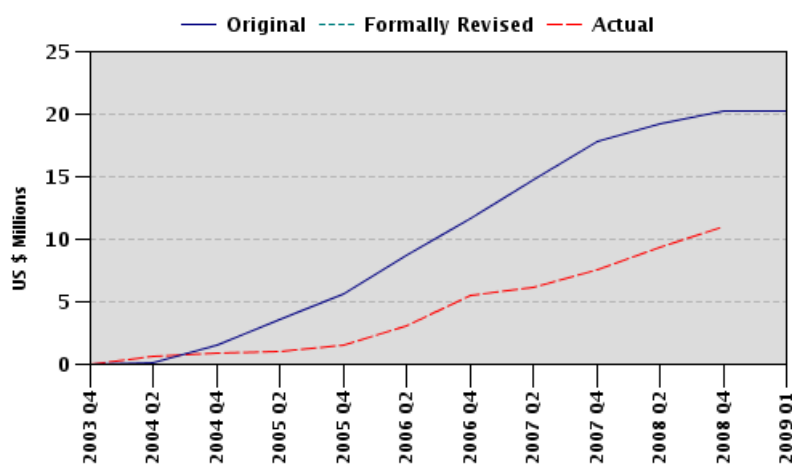

Project Name (ID): KH-Land Allocation for Soc.and Eco. Dev. (P084787)

Country: Cambodia

Board Approval Date: 05/20/2008

Closing Date: 06/30/2013

Loan/Credit/Grant Number: IDA-H3860, IDA-44410, TF-55139, TF-55390, TF-91833, TF-91836, TF-91839

Sector(s): General agriculture, fishing and forestry sector (65%), Sub-national government administration (35%)

Theme(s): Other rural development (P), Land administration and management (S), Participation and civic engagement (S)

Project Development Objectives:

The objective is to improve the process for identification and use of state land transferred to eligible poor and formerly landless or land-poor recipients selected through a transparent and well-targeted process.

Progress toward achieving development objective(s):

The Financing and Grant Agreements were countersigned on June 13, 2008 but did not become effective before the end of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-H3860	Not Effective	8.55	0.00	8.55	0.00
IDA-44410	Not Effective	2.74	0.00	2.74	0.00
TF-55139	Effective	0.51	0.24	0.27	0.00
TF-55390	Effective	1.76	0.35	1.41	0.00
TF-91833	Effective	0.47	0.00	0.47	0.00
TF-91836	Effective	0.42	0.00	0.42	0.00
TF-91839	Effective	1.48	0.00	1.48	0.00



Project Name (ID): Cambodia - Public Fin. Mgmt. & Acct. (P087945)

Country: Cambodia

Board Approval Date: 06/27/2006

Closing Date: 01/15/2012

Loan/Credit/Grant Number: IDA-H2410, TF-54547, TF-54627

Sector(s): Central government administration (100%)

Theme(s): Public expenditure, financial management and procurement (P), Tax policy and administration (S), Administrative and civil service reform (S), Law reform (S)

Project Development Objectives:


The development objective of the project is to improve public financial management by strengthening: (a) the mobilization of public resources; (b) the management of public resources; (c) the management of human resources; and (d) external audit capacity.

Progress toward achieving development objective(s):

There has been significant improvement in Budget Credibility during FY2008 including: a) domestic revenue 122.5% of targeted budget revenue; b) introduction of more orderly budget process encompassing Budget Strategic Plans and improved Classification. Arrears eliminated, aggregate execution rates for Salaries 98.5%, Goods/Services 102.6%, Domestic Capital 80.5%. Budget holders are now able to commit expenditure in line with budgets and cash flow forecasts, quarterly commitment profile 13%, 36%, 62%, 98%; c) Merit Based Pay Initiative extended to apply to all Strategic Reform Activities. Development of Public Sector Management Reform Program underway; d) National Audit Authority SWaP established and action plan agreed. e) Next three year stage of the Public Financial Management SWaP targeting Financial Accountability Platform agreed by Government and Development Partners.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-H2410	Effective	15.88	1.19	14.65	0.00
TF-54547	Effective	7.04	3.69	3.35	0.00
TF-54627	Closed	0.49	0.02	0.00	0.47

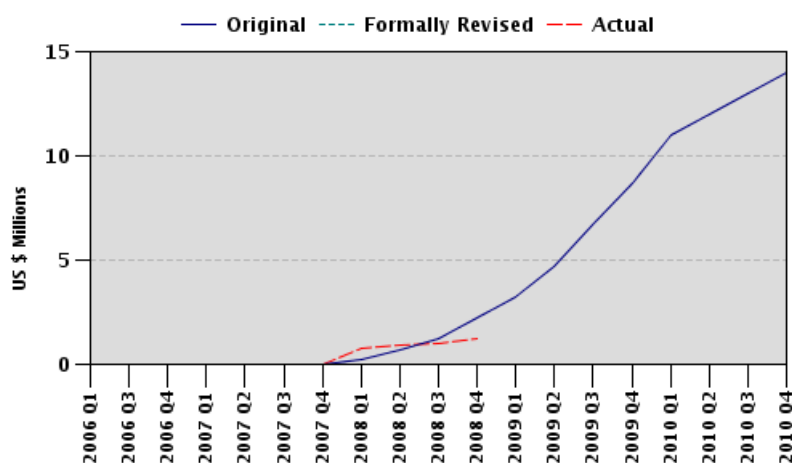

Project Name (ID): KH- Trade Facilitation & Competitiveness (P089196)

Country: Cambodia

Board Approval Date: 06/02/2005

Closing Date: 12/01/2009

Loan/Credit/Grant Number: IDA-Q4560, IDA-H1650

Sector(s): Other domestic and international trade (80%), General public administration sector (20%)

Theme(s): Export development and competitiveness (P), Trade facilitation and market access (P), Other public sector governance (S), Technology diffusion (S), Infrastructure services for private sector development (S)

Project Development Objectives:


Promote economic growth by reducing transaction costs associated with trade and investment, introducing transparency in investment processes, and facilitating access of enterprises to export markets.

Progress toward achieving development objective(s):

The mid-term review for the Trade Facilitation and Competitiveness Project (TFCP) was conducted in May 2008. The review of the TFCP found overall encouraging progress on customs automation and risk management (Component 1). There are delays noted in the implementation timelines for most components; however the project development objectives (PDO) and its outcomes remain relevant. The main focus of the review was to discuss and finalize the proposed project restructuring which would help provide the conditions to implement this project effectively and achieve the results. All technical discussions have been completed and consensus emerging along the expansion of ASYCUDA, the initial automation of Ministry of Commerce, and the creation of a Trade Information Website. The restructuring proposal awaits the endorsement from the Royal Government of Cambodia; so that the Bank task team can process the restructuring for its management approval.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-Q4560	Closed	0.58	0.00	0.00	0.58
IDA-H1650	Effective	10.72	2.69	7.83	0.00

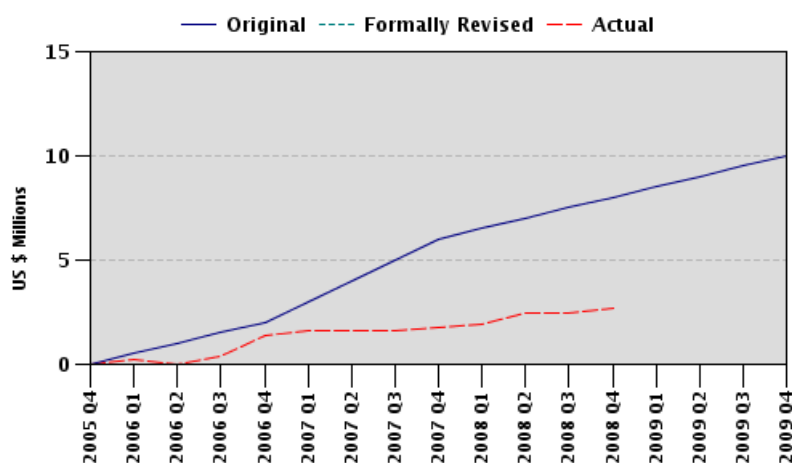

Project Name (ID): KH-Avian Influenza Emergency Project (P100084)

Country: Cambodia

Board Approval Date: 03/24/2008

Closing Date: 12/31/2011

Loan/Credit/Grant Number: IDA-H3610, TF-56832, TF-58146

Sector(s): Central government administration (49%), Agricultural extension and research (26%), Sub-national government administration (13%), Health (8%), Animal production (4%)

Theme(s): Other communicable diseases (P), Rural services and infrastructure (P), Natural disaster management (P)

Project Development Objectives:

The objective is to reduce the threat of Avian Influenza infection in poultry and humans.

Progress toward achieving development objective(s):

The Grant was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-H3610	Not Effective	6.15	0.00	6.15	0.00
TF-56832	Effective	3.00	0.00	3.00	0.00
TF-58146	Effective	2.00	0.00	2.00	0.00

Project Name (ID): KH-Second Health Sector Support Program (P102284)

Country: Cambodia

Board Approval Date: 06/19/2008

Closing Date: 06/30/2014

Loan/Credit/Grant Number: IDA-44700

Sector(s): Health (44%), Central government administration (24%), Sub-national government administration (24%), Other social services (4%), Compulsory health finance (4%)

Theme(s): Health system performance (P), Population and reproductive health (S), Administrative and civil service reform (S), Child health (S), Participation and civic engagement (S)

Project Development Objectives:

To support the implementation of the Government's Health Strategic Plan 2008-2015 to improve health outcomes through strengthening institutional capacity and mechanisms by which the Government and development partners can achieve more effective and efficient sector performance.

Progress toward achieving development objective(s):

The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-44700	Not Effective	30.28	0.00	30.28	0.00



Project Name (ID): KH - GMS Power Trade Project (P105329)

Country: Cambodia

Board Approval Date: 06/05/2007

Closing Date: 12/31/2011

Loan/Credit/Grant Number: IDA-H3010

Sector(s): Power (100%)

Theme(s): Infrastructure services for private sector development (P), Regional integration (P), Rural services and infrastructure (S)

Project Development Objectives:


Within the long-term GMS framework, the proposed project is to enhance regional power trade within the Greater Mekong Sub-Region with a view to bring affordable grid-based electricity to selected provinces in Cambodia through import of power from Lao PDR and Vietnam.

Progress toward achieving development objective(s):

Meaningful achievement of Development Objectives depends on implementation of the project. Though the implementation has just started, the environmental and social sustainability is being ensured through including implementation of Environmental Management Plans within the scope of construction contracts and putting in place satisfactory monitoring arrangements. The Government and the implementing agencies complied with all conditions of effectiveness and the Grant was declared effective on 4 February 2008. Power Purchase Agreements have been signed with Electricite du Laos and Power Company II of Vietnam. For revising the bidding documents for transmission interconnection to Lao PDR and Vietnam to incorporate the mitigation measures for protecting large birds in Stung Treng area and due to change in location of one of the substations, Electricity du Cambodge (EDC) is about to hire Korean Electric Power Company on sole source basis. International Procurement Agent (IPA) will soon issue the advertisement for engaging the Project Implementation Consultant (PIC), and start the procurement process for transmission interconnections once the revised bid documents are submitted by EDC.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-H3010	Effective	20.12	0.00	20.12	0.00

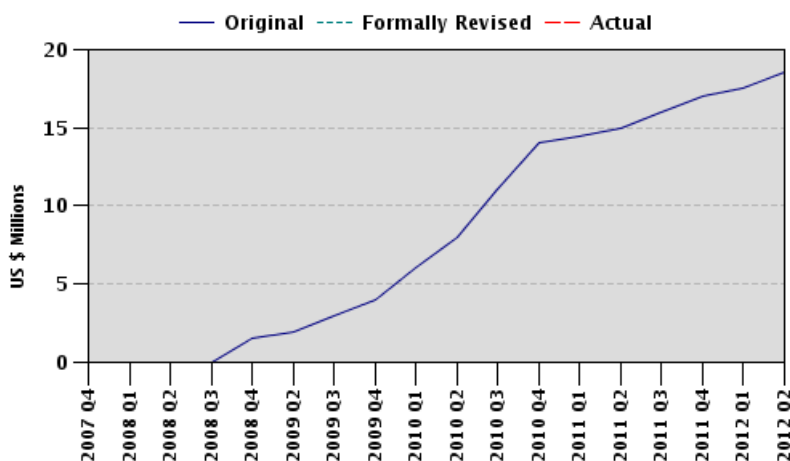

Project Name (ID): KH - Road Asset Mgmt (ADB/AusAID) (P106603)

Country: Cambodia

Board Approval Date: 05/20/2008

Closing Date: 09/30/2013

Loan/Credit/Grant Number: IDA-44420

Sector(s): Roads and highways (97%), Central government administration (3%)

Theme(s): Other public sector governance (P), Infrastructure services for private sector development (P), Administrative and civil service reform (S)

Project Development Objectives:

To ensure continued effective use of the rehabilitated national and provincial road network in support of the economic development of Cambodia. It will do so by improving the institutional and technical capacity of the MPWT for road maintenance planning, budgeting and operations, and to expanding and strengthening maintenance activities.

Progress toward achieving development objective(s):

The project was approved in May 2008, the implementing agency is working on the effectiveness conditions which are expected to be fulfilled by September 2008.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
IDA-44420	Not Effective	29.53	0.00	29.53	0.00



Project Name (ID): KH-EFA-FTI Catalytic Trust Fund (P109925)

Country: Cambodia

Board Approval Date: 04/10/2008

Closing Date: 06/30/2010

Loan/Credit/Grant Number: TF-92097

Sector(s): Primary education (71%), Pre-primary education (22%), Central government administration (5%), Sub-national government administration (2%)

Theme(s): Education for all (P)

Project Development Objectives:

To improve grade 1 right-age entry, net enrollment, retention, progression rates and grade 6 completion rates in primary education

Progress toward achieving development objective(s):

The project had just become effective before the close of the reporting period.

Lending Information/Disbursement Summary (USD millions, as of June 30, 2008)

Loan/Credit/Grant	Status	Amount	Disbursed	Undisbursed	Cancellation
TF-92097	Effective	57.40	0.00	57.40	0.00

